





ID		WBS	Task Name	Contact	Resource Initials	D0 Request	Major Milestone	Duration
308	✓	4.1.5	MILESTONE: D0 Primary Production Runnable on Fermigrid	MD	MD	No	Yes	0 days
26	✓ 	2.4.4	MILESTONE: Start Prod at Stage 2 Working	GG		Yes	Yes	0 days
134	✓	3.3.1.4	MILESTONE: Phase 1 of Operations Transfer completed	GG,AL		No	Yes	0 days
112	✓	3.2.3.5	MILESTONE: Operations Reduction plan: Working plan	GG		No	Yes	0 days
138	✓	3.3.2.3	MILESTONE: Phase 2 of Operations Transfer completed	GG,AL		No	Yes	0 days
421	✓ 	8.3.8	MILESTONE: Baseline Project Plan v1.0	RDK		No	Yes	0 days
9		1.8	MILESTONE: D0 Grid Production Architecture document	AL	AL	No	Yes	0 days
153		3.4.5	MILESTONE: SamGrid migrated to new VDT version	GG		No	Yes	0 days
427		8.3.14	MILESTONE: Project Plan v1.1 w/supporting PM docs	RDK		No	Yes	0 days
142		3.3.3.3	MILESTONE: Phase 3 of Operations Transfer completed	GG,AL		No	Yes	0 days
91		3.1.4.7	MILESTONE: Operations Policies doc	AL		No	Yes	0 days
364		5.3	MILESTONE: Grid Production System functionality completed	GG		No	Yes	0 days
52		2.8.8	MILESTONE: Support testing v7/d0runjob/SamGrid functionality	GG		Yes	Yes	0 days
38		2.6.7	MILESTONE: D0repro tools uses Sam v7 request system	GG		Yes	Yes	0 days
182		3.5.1.2.2.7	MILESTONE: OSG Forwarding nodes reinstalled with standard configuration	GG		No	Yes	0 days
268		3.5.5.8	MILESTONE: System health alarms via NGOP automated	GG		No	Yes	0 days
211		3.5.1.4.3	MILESTONE: Durable Locations reinstalled with standard configuration	GG		No	Yes	0 days
198		3.5.1.3.3	MILESTONE: Queuing nodes reinstalled with standard configuration	GG		No	Yes	0 days
226		3.5.2.7	MILESTONE: Routine maintenance operations automated	GG		No	Yes	0 days
43		2.7.4	MILESTONE: How to add production paths in future resolved	GG		Yes	Yes	0 days
146		3.3.4.3	MILESTONE: Phase 4 of Operations Transfer completed	GG,AL		No	Yes	0 days
21		2.3.5	MILESTONE: Store output from any stage	GG		Yes	Yes	0 days
347		4.3.7	MILESTONE: D0 Primary Production Stable on Fermigrid	MD		No	Yes	0 days
64		2.11	MILESTONE: Achieve architecture-defined responsibilities among tools	GG		No	Yes	0 days
284		3.6.3	MILESTONE: Close-out of Operations Reduction/Transfer completed	GG,AL		No	Yes	0 days
437		9	MILESTONE: Initiative completed	ASB		No	Yes	0 days


Start	Finish	July 2007												August 2007												September 2007											
		26	29	2	5	8	11	14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	1							
Fri 7/13/07	Fri 7/13/07	7/13 ♦ MILESTONE: D0 Primary Production Runnable on Fermigrid																																			
Mon 8/13/07	Mon 8/13/07	8/13 ♦ MILESTONE: Start Prod at Stage 2 Working																																			
Fri 8/24/07	Fri 8/24/07	8/24 ♦ MILESTONE: Phase 1 of Operations Transfer co																																			
Tue 9/18/07	Tue 9/18/07	9/18 ♦																																			
Tue 10/2/07	Tue 10/2/07																																				
Mon 10/8/07	Mon 10/8/07																																				
Fri 10/12/07	Fri 10/12/07																																				
Mon 10/22/07	Mon 10/22/07																																				
Tue 10/23/07	Tue 10/23/07																																				
Tue 11/6/07	Tue 11/6/07																																				
Thu 11/8/07	Thu 11/8/07																																				
Fri 11/16/07	Fri 11/16/07																																				
Tue 11/20/07	Tue 11/20/07																																				
Mon 11/26/07	Mon 11/26/07																																				
Tue 11/27/07	Tue 11/27/07																																				
Thu 11/29/07	Thu 11/29/07																																				
Fri 11/30/07	Fri 11/30/07																																				
Tue 12/4/07	Tue 12/4/07																																				
Tue 12/11/07	Tue 12/11/07																																				
Fri 12/14/07	Fri 12/14/07																																				
Fri 12/14/07	Fri 12/14/07																																				
Wed 12/26/07	Wed 12/26/07																																				
Thu 1/10/08	Thu 1/10/08																																				
Wed 1/30/08	Wed 1/30/08																																				
Wed 1/30/08	Wed 1/30/08																																				
Mon 2/11/08	Mon 2/11/08																																				

7/13 ♦ MILESTONE: D0 Primary Production Runnable on Fermigrid

8/13 ♦ MILESTONE: Start Prod at Stage 2 Working

8/24 ♦ MILESTONE: Phase 1 of Operations Transfer co

9/18 ♦

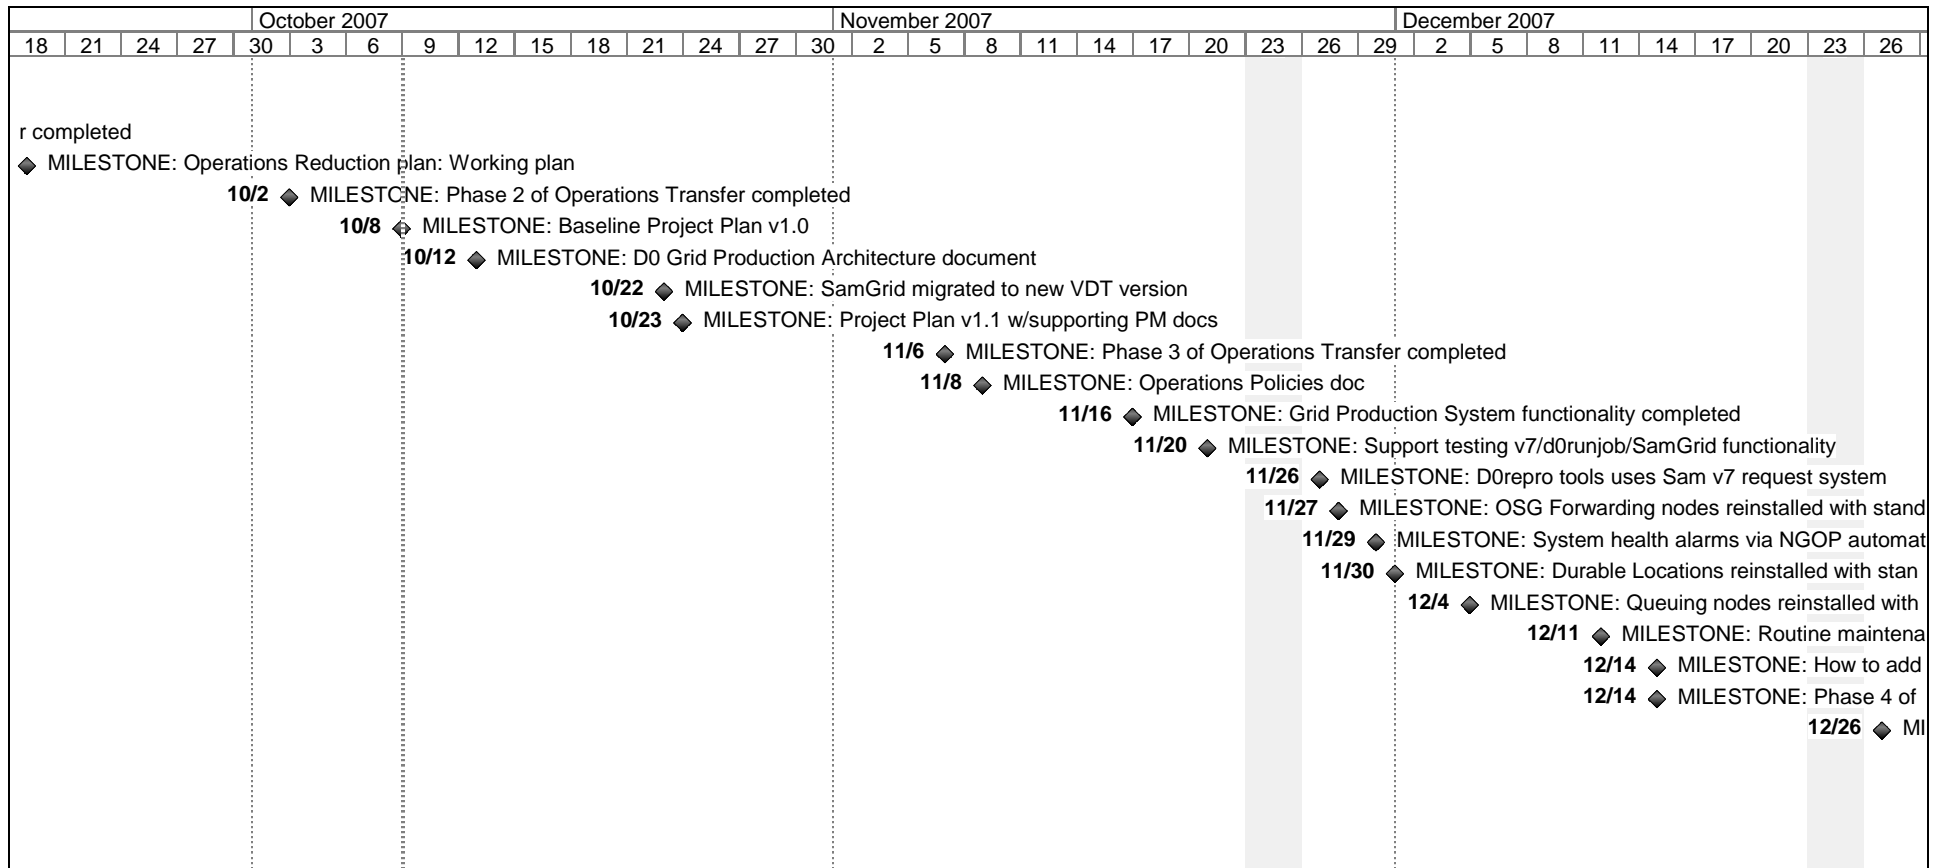

January 2008											February 2008											March 2008											April 2008				
29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	1	4	7	10	13	16	19	22	25	28	31	3	6				
<div><div><div>Standard configuration</div><div>ated</div><div>Standard configuration</div><div>Standard configuration</div><div>ance operations automated</div><div>d production paths in future resolved</div><div>f Operations Transfer completed</div><div>ILESTONE: Store output from any stage</div><div>1/10 ♦ MILESTONE: D0 Primary Production Stable on Fermigrid</div><div>1/30 ♦ MILESTONE: Achieve architecture-defined responsibilities among tools</div><div>1/30 ♦ MILESTONE: Close-out of Operations Reduction/Transfer completed</div><div>2/11 ♦ MILESTONE: Initiative completed</div></div></div>																																					

Page 4

Project: D0 Grid Production Computin
Date: Tue 10/9/07

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

