



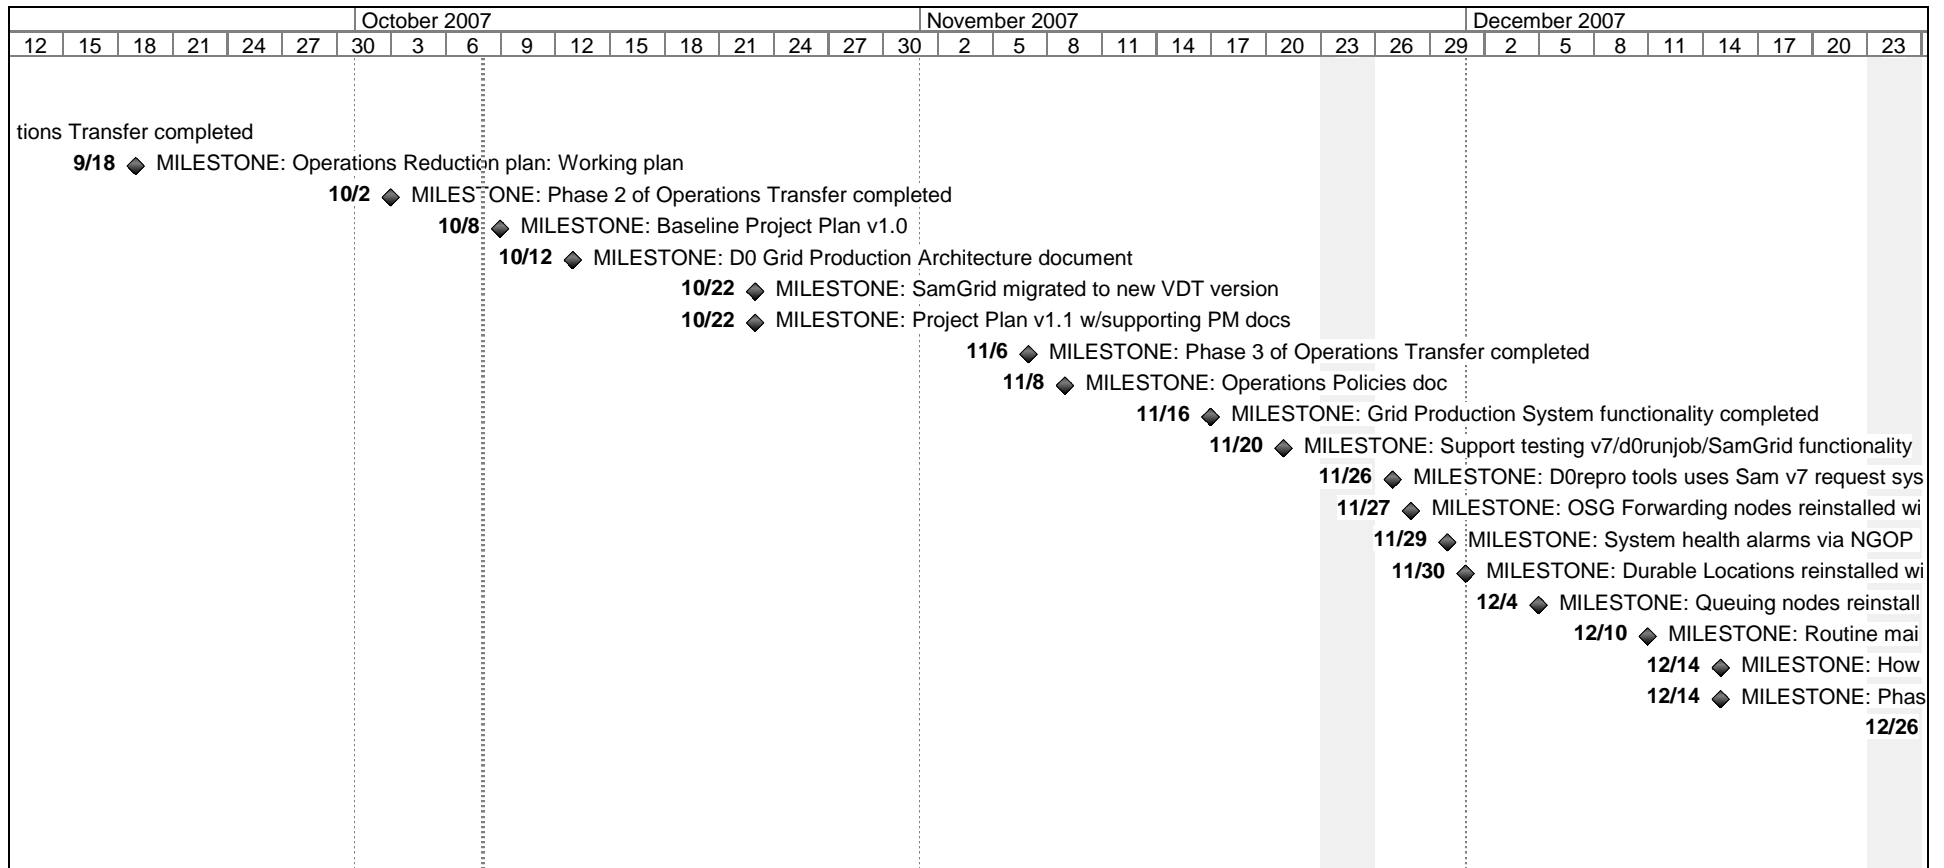


ID		WBS	Task Name	Contact	Resource Initials
308	✓	4.1.5	MILESTONE: D0 Primary Production Runnable on Fermigrid	MD	MD
26	✓ 	2.4.4	MILESTONE: Start Prod at Stage 2 Working	GG	
134	✓	3.3.1.4	MILESTONE: Phase 1 of Operations Transfer completed	GG,AL	
112	✓	3.2.3.5	MILESTONE: Operations Reduction plan: Working plan	GG	
138	✓	3.3.2.3	MILESTONE: Phase 2 of Operations Transfer completed	GG,AL	
421	✓ 	8.3.8	MILESTONE: Baseline Project Plan v1.0	RDK	
9		1.8	MILESTONE: D0 Grid Production Architecture document	AL	AL
153		3.4.5	MILESTONE: SamGrid migrated to new VDT version	GG	
426		8.3.13	MILESTONE: Project Plan v1.1 w/supporting PM docs	RDK	
142		3.3.3.3	MILESTONE: Phase 3 of Operations Transfer completed	GG,AL	
91		3.1.4.7	MILESTONE: Operations Policies doc	AL	
364		5.3	MILESTONE: Grid Production System functionality completed	GG	
52		2.8.8	MILESTONE: Support testing v7/d0runjob/SamGrid functionality	GG	
38		2.6.7	MILESTONE: D0repro tools uses Sam v7 request system	GG	
182		3.5.1.2.2.7	MILESTONE: OSG Forwarding nodes reinstalled with standard configuration	GG	
268		3.5.5.8	MILESTONE: System health alarms via NGOP automated	GG	
211		3.5.1.4.3	MILESTONE: Durable Locations reinstalled with standard configuration	GG	
198		3.5.1.3.3	MILESTONE: Queuing nodes reinstalled with standard configuration	GG	
226		3.5.2.7	MILESTONE: Routine maintenance operations automated	GG	
43		2.7.4	MILESTONE: How to add production paths in future resolved	GG	
146		3.3.4.3	MILESTONE: Phase 4 of Operations Transfer completed	GG,AL	
21		2.3.5	MILESTONE: Store output from any stage	GG	
347		4.3.7	MILESTONE: D0 Primary Production Stable on Fermigrid	MD	
64		2.11	MILESTONE: Achieve architecture-defined responsibilities among tools	GG	
284		3.6.3	MILESTONE: Close-out of Operations Reduction/Transfer completed	GG,AL	
436		9	MILESTONE: Initiative completed	ASB	

Duration	D0	Major ilestone	Start	July 2007														August 2007														September 2007											
	Request			26	29	2	5	8	11	14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12													
0 days	No	Yes	Fri 7/13/07	7/13 ♦ MILESTONE: D0 Primary Production Runnable on Fermigrid																																							
0 days	Yes	Yes	Mon 8/13/07	8/13 ♦ MILESTONE: Start Prod at Stage 2 Working																																							
0 days	No	Yes	Fri 8/24/07	8/24 ♦ MILESTONE: Phase 1 of Operation																																							
0 days	No	Yes	Tue 9/18/07																																								
0 days	No	Yes	Tue 10/2/07																																								
0 days	No	Yes	Mon 10/8/07																																								
0 days	No	Yes	Fri 10/12/07																																								
0 days	No	Yes	Mon 10/22/07																																								
0 days	No	Yes	Mon 10/22/07																																								
0 days	No	Yes	Tue 11/6/07																																								
0 days	No	Yes	Thu 11/8/07																																								
0 days	No	Yes	Fri 11/16/07																																								
0 days	Yes	Yes	Tue 11/20/07																																								
0 days	Yes	Yes	Mon 11/26/07																																								
0 days	No	Yes	Tue 11/27/07																																								
0 days	No	Yes	Thu 11/29/07																																								
0 days	No	Yes	Fri 11/30/07																																								
0 days	No	Yes	Tue 12/4/07																																								
0 days	No	Yes	Mon 12/10/07																																								
0 days	Yes	Yes	Fri 12/14/07																																								
0 days	No	Yes	Fri 12/14/07																																								
0 days	Yes	Yes	Wed 12/26/07																																								
0 days	No	Yes	Wed 1/9/08																																								
0 days	No	Yes	Wed 1/30/08																																								
0 days	No	Yes	Wed 1/30/08																																								
0 days	No	Yes	Mon 2/11/08																																								



January 2008										February 2008										March 2008										April 2008				
26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	1	4	7	10	13	16	19	22	25	28	31	3	6
<div> <div>stem</div> <div>ith standard configuration</div> <div>automated</div> <div>ith standard configuration</div> <div>lled with standard configuration</div> <div>aintenance operations automated</div> <div>to add production paths in future resolved</div> <div>se 4 of Operations Transfer completed</div> <div> <div>◆ MILESTONE: Store output from any stage</div> <div>1/9 ◆ MILESTONE: D0 Primary Production Stable on Fermigrid</div> <div>1/30 ◆ MILESTONE: Achieve architecture-defined responsibilities among tools</div> <div>1/30 ◆ MILESTONE: Close-out of Operations Reduction/Transfer completed</div> <div>2/11 ◆ MILESTONE: Initiative completed</div> </div> </div>																																		

Project: D0 Grid Production Computin
Date: Mon 10/8/07

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

