






ID		WBS	Task Name	Contact	Resource Initials	Duration
37		2.6.4	D0repro tools adaptation: Use generic runjob interfaces in Samgrid for data processing App	GG	PM	16 days
42		2.7.1	Generalization of Job Types according to I/O Characteristics	GG	PM	5 days
243		3.5.2.1.3	Install auto-clean up for SamGrid job queue	GG	PM	2 days
245		3.5.2.1.4	Test/observe auto-clean up for SamGrid job queue	GG	PM,SS	1 day
246		3.5.2.1.5	Install auto-clean up of OSG job queue	GG	PM	2 days
43		2.7.2	Resolve how to add production paths in future: Document	GG	PM	5 days
248		3.5.2.1.2	Test/observe auto-clean up for OSG job queue	GG	PM,SS	1 day
250		3.5.2.2.1	Resolve: Globus gatekeeper does not properly cleanup gass caches	GG	PM	1 day
354		4.3.2.6	Job State diagram with most common error state causes	MD	PM	5 days
251		3.5.2.2.2	Periodically clean up gram log files at fwd nodes and exec sites	GG	PM	1 day
252		3.5.2.2.3	Clean up sandboxes and jim_tmp areas at fwd node	GG	PM	1 day
253		3.5.2.2.4	Clean up non-rotated log files (eg. Tomcat)	GG	PM	2 days
18		2.3.2	Store output from any stage: Describe suitable test of feature	GG	PM	2 days
56		2.9.1	Start Prod at Stage 2: SamGrid notification=all bug fix	GG	PM	10 days
254		3.5.2.3	Automation of all gridmap file management (including condor_schedd)	GG	PM	2 days
330		3.7.5.5	Fix Immortal Jobs: SamGrid development/integration	GG	PM	5 days
359		4.3.3.3	Augment Job States to be more meaningful to large customer	GG	PM	5 days
261		3.5.3.1.1	Determine goal level, requirements	GG	PM	4 days
256		3.5.2.5	Add the deployment of scripts to installation instructions	GG	PM	3 days
262		3.5.3.1.2	Determine existing querying performance	GG	PM	4 days
264		3.5.3.1.4	Evaluate condor_quill, if determined to be necessary	GG	PM	5 days
265		3.5.3.2	Improve algorithm for selection of OSG resources	GG	PM	6 days

Start	Finish	Dec 2, '07							Dec 9, '07							Dec 16, '07							Dec 23, '07							Dec 30, '07							Jan 6, '08		
		S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	
Mon 12/10/07	Fri 1/4/08								PM																														
Mon 1/7/08	Fri 1/11/08																																						
Mon 1/7/08	Tue 1/8/08																																						
Wed 1/9/08	Wed 1/9/08																																						
Thu 1/10/08	Fri 1/11/08																																						
Mon 1/14/08	Fri 1/18/08																																						
Mon 1/14/08	Mon 1/14/08																																						
Tue 1/15/08	Tue 1/15/08																																						
Tue 1/15/08	Tue 1/22/08																																						
Wed 1/16/08	Wed 1/16/08																																						
Thu 1/17/08	Thu 1/17/08																																						
Fri 1/18/08	Tue 1/22/08																																						
Tue 1/22/08	Wed 1/23/08																																						
Tue 1/22/08	Mon 2/4/08																																						
Wed 1/23/08	Thu 1/24/08																																						
Wed 1/23/08	Tue 1/29/08																																						
Wed 1/23/08	Tue 1/29/08																																						
Fri 1/25/08	Wed 1/30/08																																						
Thu 1/31/08	Mon 2/4/08																																						
Thu 1/31/08	Tue 2/5/08																																						
Wed 2/6/08	Tue 2/12/08																																						
Wed 2/13/08	Mon 3/17/08																																						

Dorepro tool
 PM
 PM
 PM,
 PM

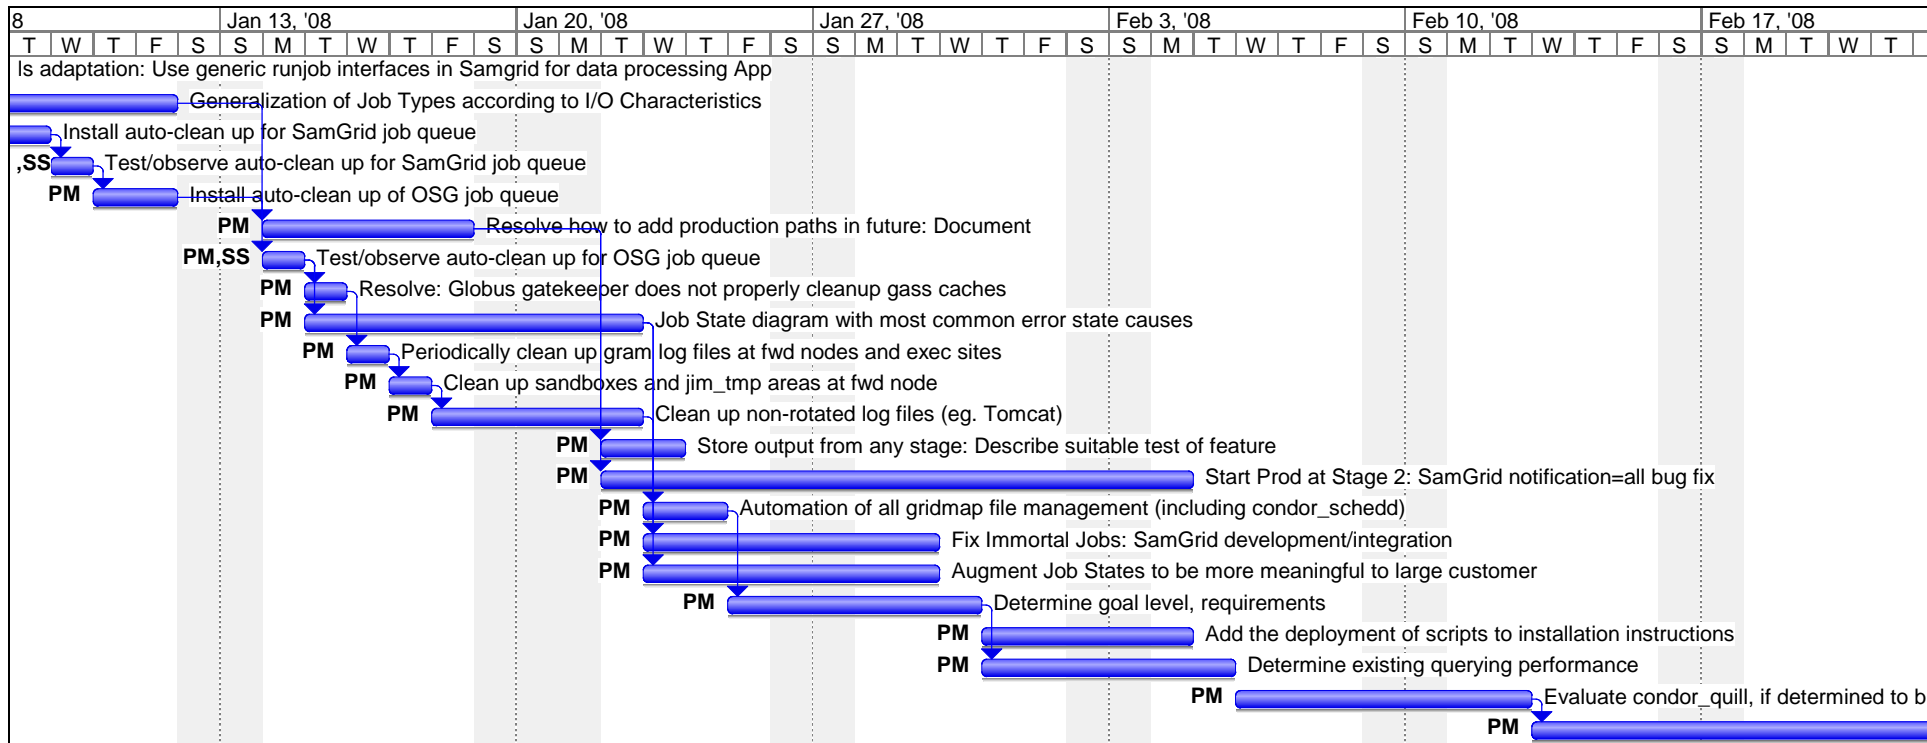

Feb 24, '08								Mar 2, '08								Mar 9, '08								Mar 16, '08								Mar 23, '08								Mar 30, '08								Apr	
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S												
<div><div>be necessary</div><div>Improve algorithm for selection of OSG resources</div></div>																																																	

Page 4

Project: D0 Grid Production Computin
Date: Wed 12/19/07

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

