



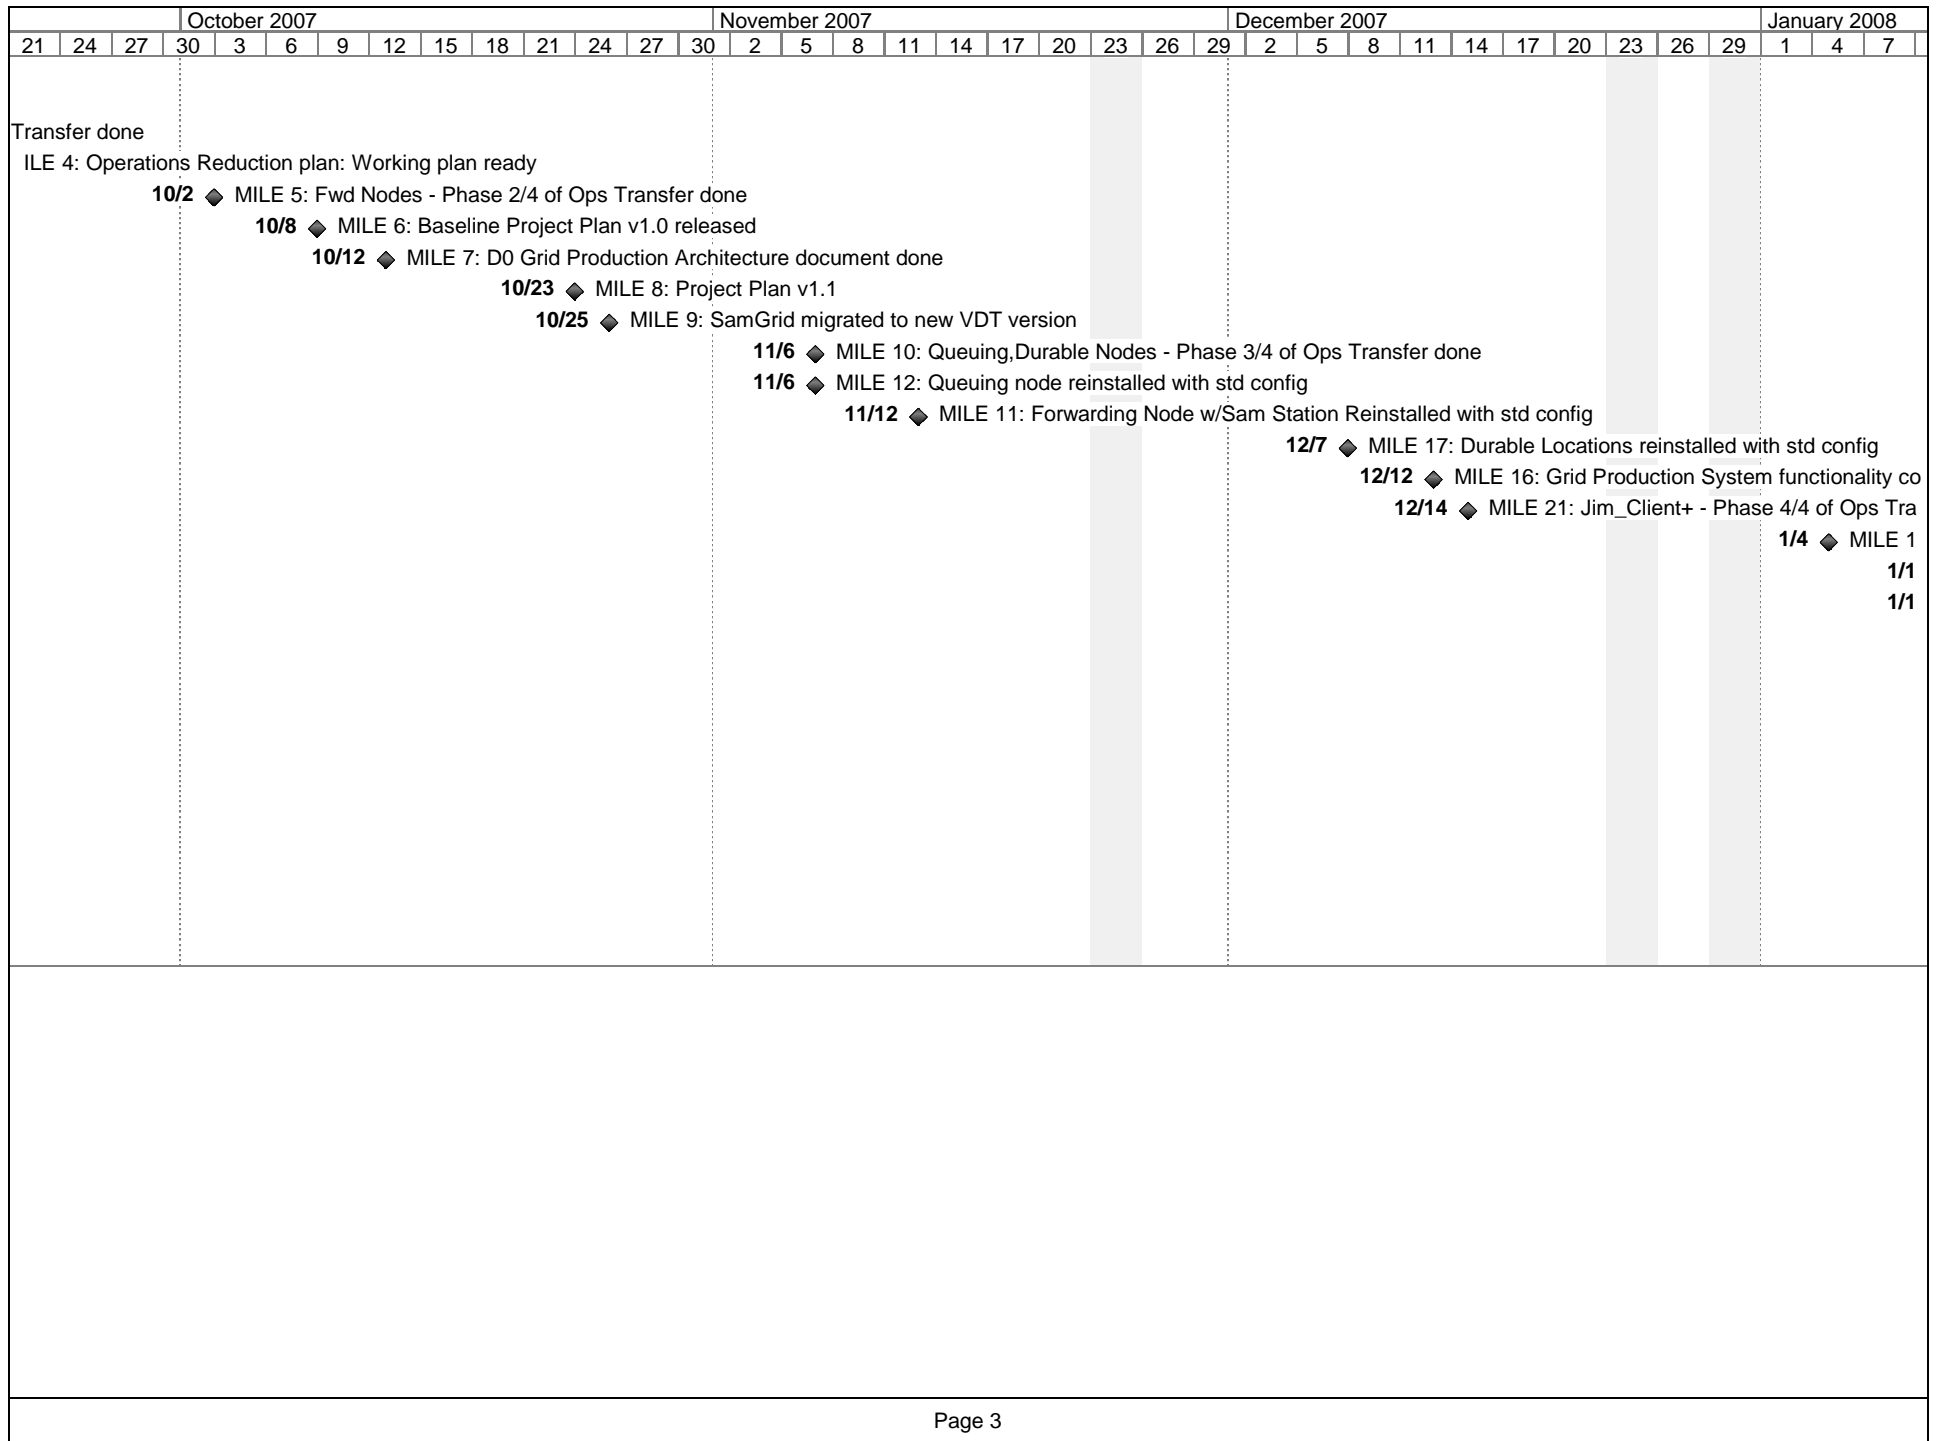


ID		WBS	Task Name	Contact	Resource Initials	Duration
321	✓	4.1.5	MILE 1: D0 Primary Production Runnable on Fermigrid	MD		0 days
24	✓ 	2.4.4	MILE 2: Start (MC) Production at Stage 2 - Working	GG		0 days
138	✓	3.3.1.4	MILE 3: Manual Checklist - Phase 1/4 of Ops Transfer done	GG,AL		0 days
116	✓	3.2.3.5	MILE 4: Operations Reduction plan: Working plan ready	GG		0 days
142	✓	3.3.2.3	MILE 5: Fwd Nodes - Phase 2/4 of Ops Transfer done	GG,AL		0 days
437	✓ 	8.3.8	MILE 6: Baseline Project Plan v1.0 released	RDK		0 days
9	✓	1.8	MILE 7: D0 Grid Production Architecture document done	AL		0 days
441	✓ 	8.3.14	MILE 8: Project Plan v1.1	RDK		0 days
156	✓	3.4.5	MILE 9: SamGrid migrated to new VDT version	GG		0 days
146	✓	3.3.3.3	MILE 10: Queuing,Durable Nodes - Phase 3/4 of Ops Transfer done	GG,AL		0 days
215	✓	3.5.1.3.3	MILE 12: Queuing node reinstalled with std config	GG		0 days
173	✓	3.5.1.2.2.8	MILE 11: Forwarding Node w/Sam Station Reinstalled with std config	GG		0 days
234	✓	3.5.1.4.3	MILE 17: Durable Locations reinstalled with std config	GG		0 days
364	✓	5.3	MILE 16: Grid Production System functionality completed	GG		0 days
150	✓	3.3.4.3	MILE 21: Jim_Client+ - Phase 4/4 of Ops Transfer done	GG,AL		0 days
299	✓	3.5.5.4	MILE 19: System health alarms deployed via NGOP with static config	GG		0 days
19	✓	2.3.5	MILE 22: Store output from any stage of processing	GG		0 days
54	✓	2.8.8	MILE 18: Support testing v7/d0runjob/SamGrid functionality	GG		0 days
187		3.5.1.2.2.7	MILE 15: OSG Fwd nodes reinstalled with std config	GG		0 days
95		3.1.4.7	MILE 13: Grid Production Operations Policies doc done	AL		0 days
40		2.6.7	MILE 14: D0repro-tools uses Sam v7 request system	GG		0 days
258		3.5.2.7	MILE 23: Routine maintenance operations automated	GG		0 days
358		4.7	MILE 28: D0 Primary Production Stable on Fermigrid	MD		0 days
378		6.5	MILE 24: Preparation of D0 Apps for long-term	ASB		0 days
406		7.11	MILE 25: Evaluation of D0 SamGrid Requests done	RDK		0 days
45		2.7.4	MILE 20: How to add production paths in future - resolved	GG		0 days
67		2.11	MILE 26: Tools have defined API, testing responsibilities	GG		0 days
314		3.8	MILE 27: Close-out of Ops Reduction/Transfer completed	GG		0 days
451		9	MILE 29: D0 GPC Initiative completed	ASB		0 days

Start	Finish	July 2007												August 2007												September 2007											
		23	26	29	2	5	8	11	14	17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21					
Fri 7/13/07	Fri 7/13/07	7/13 ♦ MILE 1: D0 Primary Production Runnable on Fermigrid																																			
Mon 8/13/07	Mon 8/13/07	8/13 ♦ MILE 2: Start (MC) Production at Stage 2 - Working																																			
Fri 8/24/07	Fri 8/24/07	8/24 ♦ MILE 3: Manual Checklist - Phase 1/4 of Ops Tran																																			
Tue 9/18/07	Tue 9/18/07	9/18 ♦ MILE																																			
Tue 10/2/07	Tue 10/2/07																																				
Mon 10/8/07	Mon 10/8/07																																				
Fri 10/12/07	Fri 10/12/07																																				
Tue 10/23/07	Tue 10/23/07																																				
Thu 10/25/07	Thu 10/25/07																																				
Tue 11/6/07	Tue 11/6/07																																				
Tue 11/6/07	Tue 11/6/07																																				
Mon 11/12/07	Mon 11/12/07																																				
Fri 12/7/07	Fri 12/7/07																																				
Wed 12/12/07	Wed 12/12/07																																				
Fri 12/14/07	Fri 12/14/07																																				
Fri 1/4/08	Fri 1/4/08																																				
Fri 1/11/08	Fri 1/11/08																																				
Fri 1/11/08	Fri 1/11/08																																				
Fri 1/25/08	Fri 1/25/08																																				
Tue 1/29/08	Tue 1/29/08																																				
Wed 1/30/08	Wed 1/30/08																																				
Wed 1/30/08	Wed 1/30/08																																				
Mon 2/11/08	Mon 2/11/08																																				
Mon 2/11/08	Mon 2/11/08																																				
Mon 2/11/08	Mon 2/11/08																																				
Wed 2/13/08	Wed 2/13/08																																				
Fri 2/15/08	Fri 2/15/08																																				
Fri 2/15/08	Fri 2/15/08																																				
Fri 2/29/08	Fri 2/29/08																																				



							February 2008							March 2008							April 2008															
10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27
<div>Completed</div> <div>Transfer done</div> <div>19: System health alarms deployed via NGOP with static config</div> <div>11◆ MILE 22: Store output from any stage of processing</div> <div>11◆ MILE 18: Support testing v7/d0runjob/SamGrid functionality</div> <div>1/25◆ MILE 15: OSG Fwd nodes reinstalled with std config</div> <div>1/29◆ MILE 13: Grid Production Operations Policies doc done</div> <div>1/30◆ MILE 14: D0repro-tools uses Sam v7 request system</div> <div>1/30◆ MILE 23: Routine maintenance operations automated</div> <div>2/11◆ MILE 28: D0 Primary Production Stable on Fermigrid</div> <div>2/11◆ MILE 24: Preparation of D0 Apps for long-term</div> <div>2/11◆ MILE 25: Evaluation of D0 SamGrid Requests done</div> <div>2/13◆ MILE 20: How to add production paths in future - resolved</div> <div>2/15◆ MILE 26: Tools have defined API, testing responsibilities</div> <div>2/15◆ MILE 27: Close-out of Ops Reduction/Transfer completed</div> <div>2/29◆ MILE 29: D0 GPC Initiative completed</div>																																				

Page 4

Project: D0 Grid Production Computin
Date: Wed 1/23/08

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

