















ID		WBS	Task Name	Contact	Resource Initials	Duration
44		2.7.3	Resolve how to add production paths in future: D0 Approval	GG	ASB	2 days
95		3.1.4.6	Operations Policies doc: Approve - CD, D0	AL	ASB,RDK	2 days
456		8.5.3	Project Close-out Report Approval: ABS, CD	RDK	ASB,RDK	3 days
383		6.4.5	Perform data migration to SAM storage	AL	D0	64 days
34		2.6.9	D0repro tools adaptation: Final 10% implementation	DW	DW	9 days
343		4.3.2.6	Job State diagram with most common error state causes	MD	EXT	5 days
347		4.3.3.2	Improve job monitoring, include trend plots	RDK	EXT	5 days
348		4.3.3.3	Augment Job States to be more meaningful to large customer	MD	EXT	5 days
346	 	4.3.3.1	CAB web monitoring changes requested by MD,JS	RDK	FEF	24 days
243		3.5.8.2	Admins fix disk on test queue node (old samgrid)	AL	FEF	5 days
39		2.6.6	D0repro tools adaptation: MC Production test	GG	JS	3 days
57		2.9.2	Start Prod at Stage 2: Production-level re-test	GG	JS	2 days
38		2.6.11	D0repro tools adaptation: Production test	GG	MD	3 days
351	 	4.3.4.1	Allow access by MD to dir/files on CAB owned by dzeropro (suggested: get root access)	MD	MD	5 days
352		4.3.4.2	JIM production release consistent with d0runjob v7-7-3 and higher	MD	MD	5 days
452		8.4.2	Execution Phase (Level of Effort >= 15%)	RDK	RDK	77 days
407		7.12.3	Create form to capture D0 App requirements, workflow, use patterns	RDK	RDK	6 days
408		7.12.4	Create maintainable list of known portability issues for D0 Apps on Grid	RDK	RDK	6 days
409		7.12.1	Write evaluation of requests based on generic WBS	RDK	RDK	6 days
384		6.8	INPUT (7.12.1): Write recommendations for productization of D0 Apps	RDK	RDK	0 days
412		7.12.6	D0 SamGrid Requests Evaluation: Revision	RDK	RDK	1 day
454	 	8.5.1	Project Close-out Meeting	RDK	RDK	1 day
455		8.5.2	Project Close-out Report	RDK	RDK	5 days
457		8.5.4	Archive project artifacts	RDK	RDK	1 day

Start	Finish	7	Jan 6, '08					Jan 13, '08					Jan 20, '08					Jan 27, '08					Feb						
		T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	
Tue 2/12/08	Wed 2/13/08																												
Mon 2/4/08	Tue 2/5/08																												
Tue 2/26/08	Thu 2/28/08																												
Thu 10/25/07	Thu 1/31/08	<div>Perform data</div>																											
Tue 1/29/08	Fri 2/8/08																												
Mon 2/11/08	Fri 2/15/08																												
Mon 2/11/08	Fri 2/15/08																												
Mon 2/11/08	Fri 2/15/08																												
Mon 1/7/08	Fri 2/8/08																												
Mon 1/28/08	Fri 2/1/08																												
Mon 1/28/08	Wed 1/30/08																												
Thu 2/14/08	Fri 2/15/08																												
Mon 1/28/08	Wed 1/30/08																												
Tue 1/29/08	Mon 2/4/08																												
Tue 1/29/08	Mon 2/4/08																												
Tue 10/9/07	Fri 2/15/08	<div></div>																											
Wed 1/30/08	Wed 2/6/08																												
Wed 1/30/08	Wed 2/6/08																												
Wed 1/30/08	Wed 2/6/08																												
Wed 2/6/08	Wed 2/6/08																												
Thu 2/14/08	Thu 2/14/08																												
Mon 2/18/08	Mon 2/18/08																												
Tue 2/19/08	Mon 2/25/08																												
Fri 2/29/08	Fri 2/29/08																												

ASB,RDK

Perform data

DW

FEF

FEF

Admins fi

JS

D0repro tools adap

MD

D0repro tools adap


MD

MD

RDK

RDK

RDK

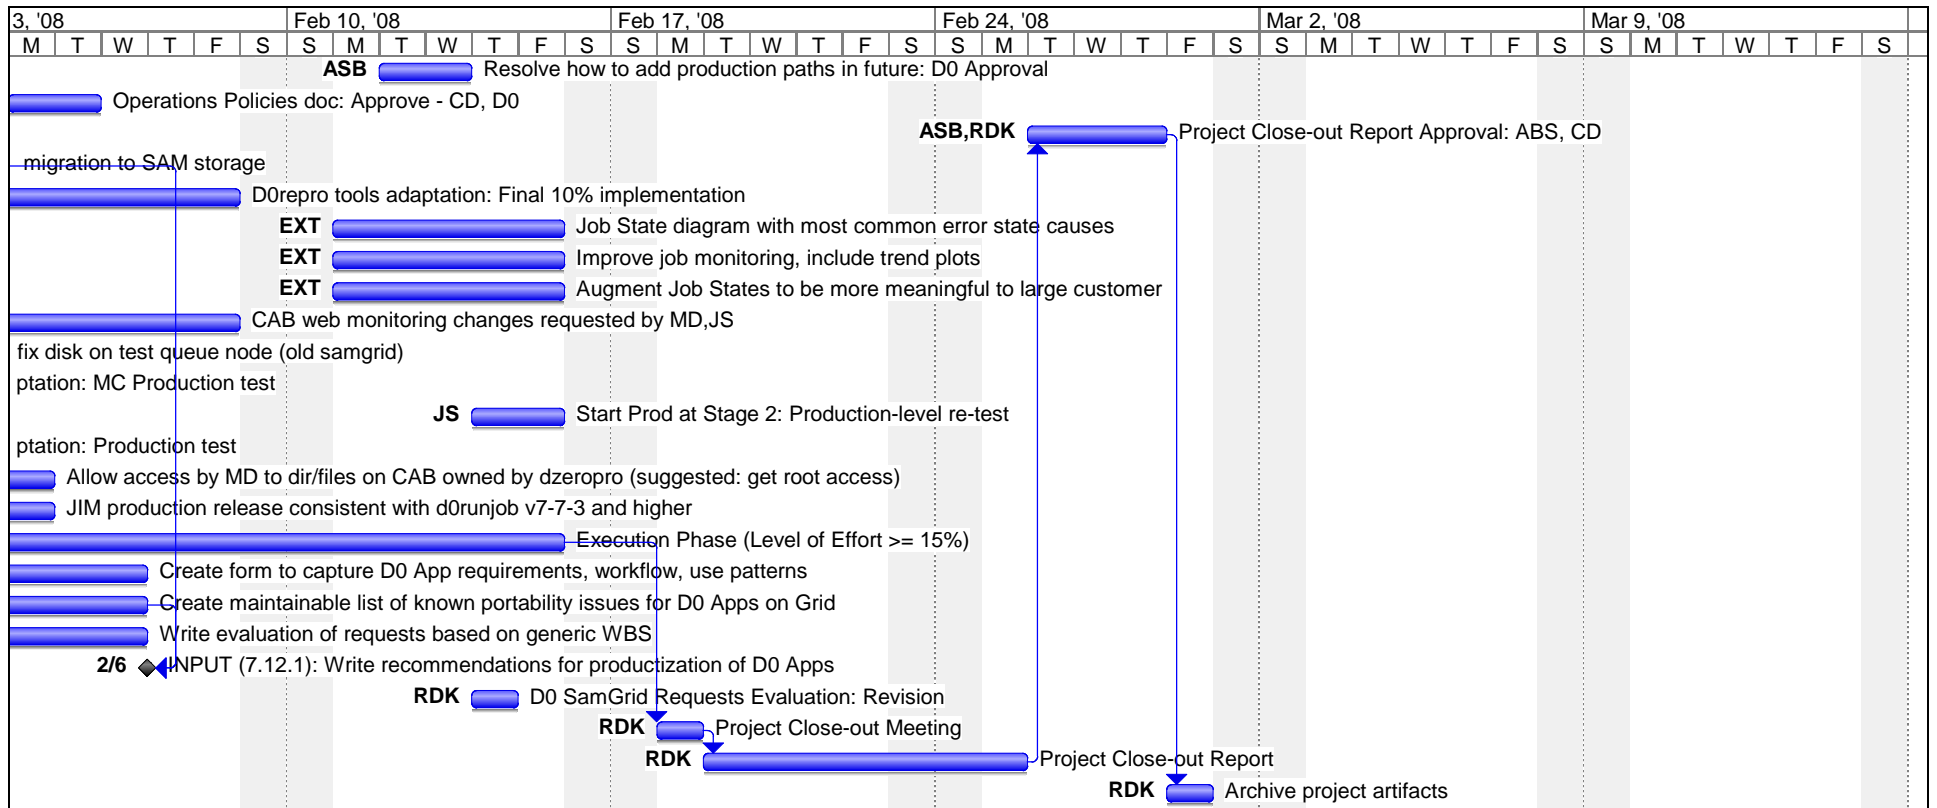

Project: D0 Grid Production Computin
Date: Wed 1/30/08

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

