









ID		WBS	Task Name	Contact	Resource Initials
47		2.7.3	Resolve how to add production paths in future: D0 Approval	GG	ASB
99		3.1.4.11	Operations Policies doc: Approve - CD, D0	AL	ASB,RDK
477		8.5.3	Project Close-out Report Approval: ABS, CD	RDK	ASB,RDK
355		4.3.3.5	CAB web monitoring changes requested by MD,JS - data presentation	RDK	FEF
45		2.7.6	D0repro tools/Generalization changes: MC Production test	GG	JS
60		2.9.2	Start Prod at Stage 2: Production-level re-test	GG	JS
358	 	4.3.4.1	Allow access by MD to dir/files on CAB owned by dzeropro (suggested: get root access)	MD	MD
359		4.3.4.2	JIM production release consistent with d0runjob v7-7-3 and higher	MD	MD
44		2.7.11	D0repro tools/Generalization changes: Production test	GG	MD
365		4.3.4.9	Forward user's job scheduler requirements to sites: pre-production testing	GG	MD
473		8.5.6	Project Objectives Close-out Document	RDK	RDK
474		8.5.7	Prepare Rough Draft D0 Technical Note with Project Documents	RDK	RDK
475	 	8.5.1	Project Close-out Meeting	RDK	RDK
476		8.5.2	Project Close-out Report	RDK	RDK
478		8.5.4	Archive project artifacts	RDK	RDK


Duration	Start	Finish	Mar 16, '08							Mar 23, '08							Mar 30, '08							Apr 6, '08							Apr 13, '08							Apr	
			S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		S
1 day	Wed 4/30/08	Wed 4/30/08																																					
1 day	Mon 4/28/08	Mon 4/28/08																																					
3 days	Fri 5/16/08	Tue 5/20/08																																					
10 days	Mon 4/21/08	Fri 5/2/08																																					FEF
3 days	Tue 4/15/08	Thu 4/17/08																																				JS	
2 days	Wed 5/7/08	Thu 5/8/08																																					
55 days	Tue 1/22/08	Mon 4/21/08																																					
55 days	Tue 1/22/08	Mon 4/21/08																																					
3 days	Tue 4/15/08	Thu 4/17/08																																				MD	
2 days	Fri 4/18/08	Mon 4/21/08																																				MD	
4 days	Mon 5/5/08	Thu 5/8/08																																					
2 days	Fri 5/9/08	Mon 5/12/08																																					
1 day	Tue 5/13/08	Tue 5/13/08																																					
2 days	Wed 5/14/08	Thu 5/15/08																																					
2 days	Wed 5/21/08	Thu 5/22/08																																					

FEF

JS D0repro too

MD D0repro too

MD

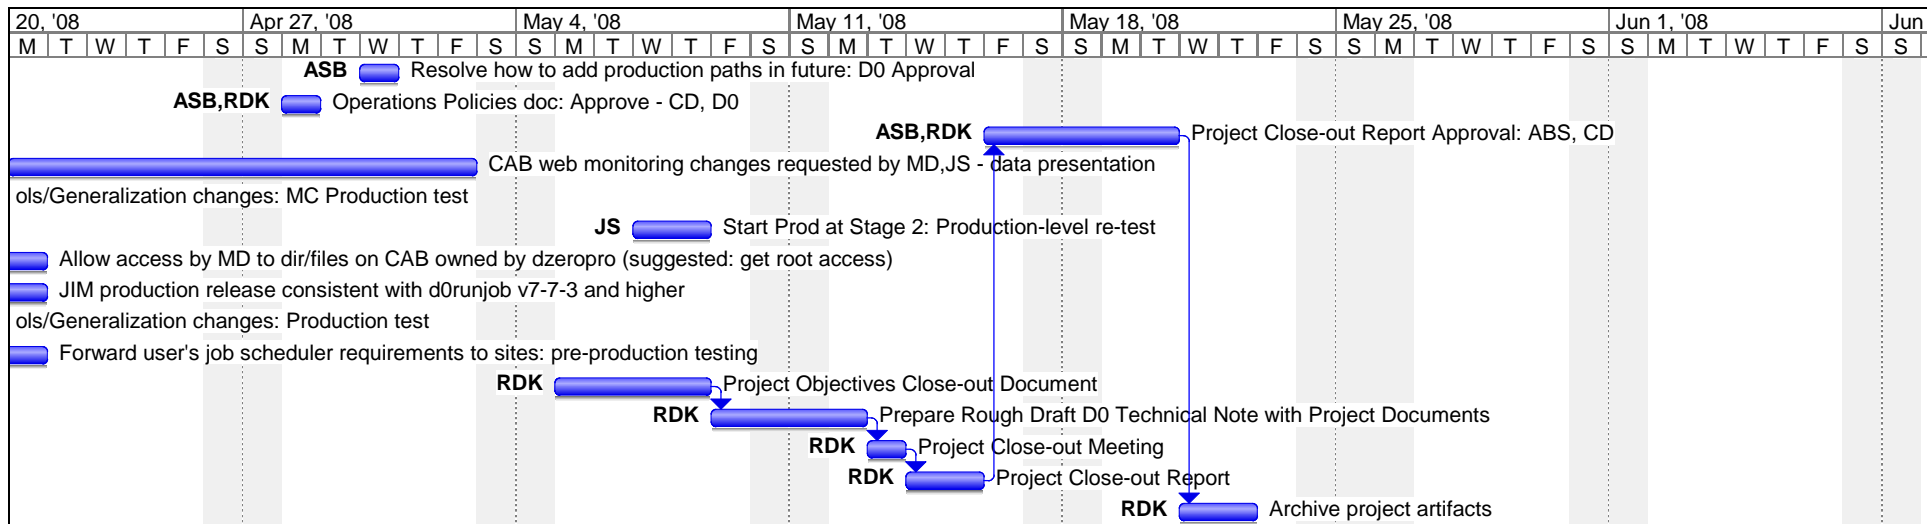

Project: D0 Grid Production Computin  
Date: Mon 4/14/08

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

