






ID		WBS	Task Name	Contact	Resource Initials
336	✓	4.1.5	MILE 1: D0 Primary Production Runnable on Fermigrid	MD	
24	✓ 	2.4.4	MILE 2: Start (MC) Production at Stage 2 - Working	GG	
143	✓	3.3.1.4	MILE 3: Manual Checklist - Phase 1/4 of Ops Transfer done	GG,AL	
121	✓	3.2.3.5	MILE 4: Operations Reduction plan: Working plan ready	GG	
147	✓	3.3.2.3	MILE 5: Fwd Nodes - Phase 2/4 of Ops Transfer done	GG,AL	
466	✓ 	8.3.8	MILE 6: Baseline Project Plan v1.0 released	RDk	
9	✓	1.8	MILE 7: D0 Grid Production Architecture document done	AL	
470	✓ 	8.3.14	MILE 8: Project Plan v1.1	RDk	
161	✓	3.4.5	MILE 9: SamGrid migrated to new VDT version	GG	
151	✓	3.3.3.3	MILE 10: Queuing,Durable Nodes - Phase 3/4 of Ops Transfer done	GG,AL	
224	✓	3.5.1.3.3	MILE 12: Queuing node reinstalled with std config	GG	
178	✓	3.5.1.2.2.8	MILE 11: Forwarding Node w/Sam Station Reinstalled with std config	GG	
243	✓	3.5.1.4.3	MILE 17: Durable Locations reinstalled with std config	GG	
384	✓	5.3	MILE 16: Grid Production System functionality completed	GG	
155	✓	3.3.4.3	MILE 21: Jim_Client+ - Phase 4/4 of Ops Transfer done	GG,AL	
311	✓	3.5.5.4	MILE 19: System health alarms deployed via NGOP with static config	GG	
19	✓	2.3.5	MILE 22: Store output from any stage of processing	GG	
57	✓	2.8.8	MILE 18: Support testing v7/d0runjob/SamGrid functionality	GG	
38	✓	2.6.7	DEFER - MILE 14: D0repro-tools uses Sam v7 request system	GG	
428	✓	7.11	MILE 25: Evaluation of D0 SamGrid Requests done	RDk	
398	✓	6.5	MILE 24: Preparation of D0 Apps for long-term	ASB	
198	✓	3.5.1.2.2.5.11	MILE 15: OSG Fwd nodes reinstalled with std config	GG	
48	✓	2.7.4	MILE 20: How to add production paths in future - resolved	GG	
69	✓	2.11	MILE 26: Tools have defined API, testing responsibilities	GG	
378	✓	4.7	DEFER - MILE 28: D0 Primary Production Stable on Fermigrid	MD	
273	✓	3.5.2.7	MILE 23: Routine maintenance operations automated	GG	
100	✓	3.1.4.7	MILE 13: Grid Production Operations Policies doc done	AL	
329	✓	3.8	DEFER - MILE 27: Close-out of Ops Reduction/Transfer completed	GG	
483		9	MILE 29: D0 GPC Initiative completed	ASB	

September 2007							October 2007							November 2007							December 2007													
6	9	12	15	18	21	24	27	30	3	6	9	12	15	18	21	24	27	30	2	5	8	11	14	17	20	23	26	29	2	5	8	11	14	
Working																																		
cklist - Phase 1/4 of Ops Transfer done																																		
9/18 ♦ MILE 4: Operations Reduction plan: Working plan ready																																		
10/2 ♦ MILE 5: Fwd Nodes - Phase 2/4 of Ops Transfer done																																		
10/8 ♦ MILE 6: Baseline Project Plan v1.0 released																																		
10/12 ♦ MILE 7: D0 Grid Production Architecture document done																																		
10/23 ♦ MILE 8: Project Plan v1.1																																		
10/25 ♦ MILE 9: SamGrid migrated to new VDT version																																		
11/6 ♦ MILE 10: Queuing,Durable Nodes - Phase 3/4 of Ops Transfer done																																		
11/6 ♦ MILE 12: Queuing node reinstalled with std config																																		
11/12 ♦ MILE 11: Forwarding Node w/Sam Station Reinstalled with std co																																		
12/7 ♦ MILE 17: Durabl																																		
12/12 ♦ MILE																																		
12/14 ♦ MI																																		

Page 3

					January 2008										February 2008										March 2008									
17	20	23	26	29	1	4	7	10	13	16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	1	4	7	10	13	16	19	22	25	
<div>onfig</div> <div>ble Locations reinstalled with std config</div> <div>16: Grid Production System functionality completed</div> <div>ILE 21: Jim_Client+ - Phase 4/4 of Ops Transfer done</div> <div>1/4 ♦ MILE 19: System health alarms deployed via NGOP with static config</div> <div>1/11 ♦ MILE 22: Store output from any stage of processing</div> <div>1/11 ♦ MILE 18: Support testing v7/d0runjob/SamGrid functionality</div> <div>2/5 ♦ DEFER - MILE 14: D0repro-tools uses Sam v7 request system</div> <div>2/27 ♦ MILE 25: Evaluation of D0 SamGrid Requests done</div> <div>3/4 ♦ MILE 24: Preparation of D0 Apps for long-te</div>																																		

Page 4

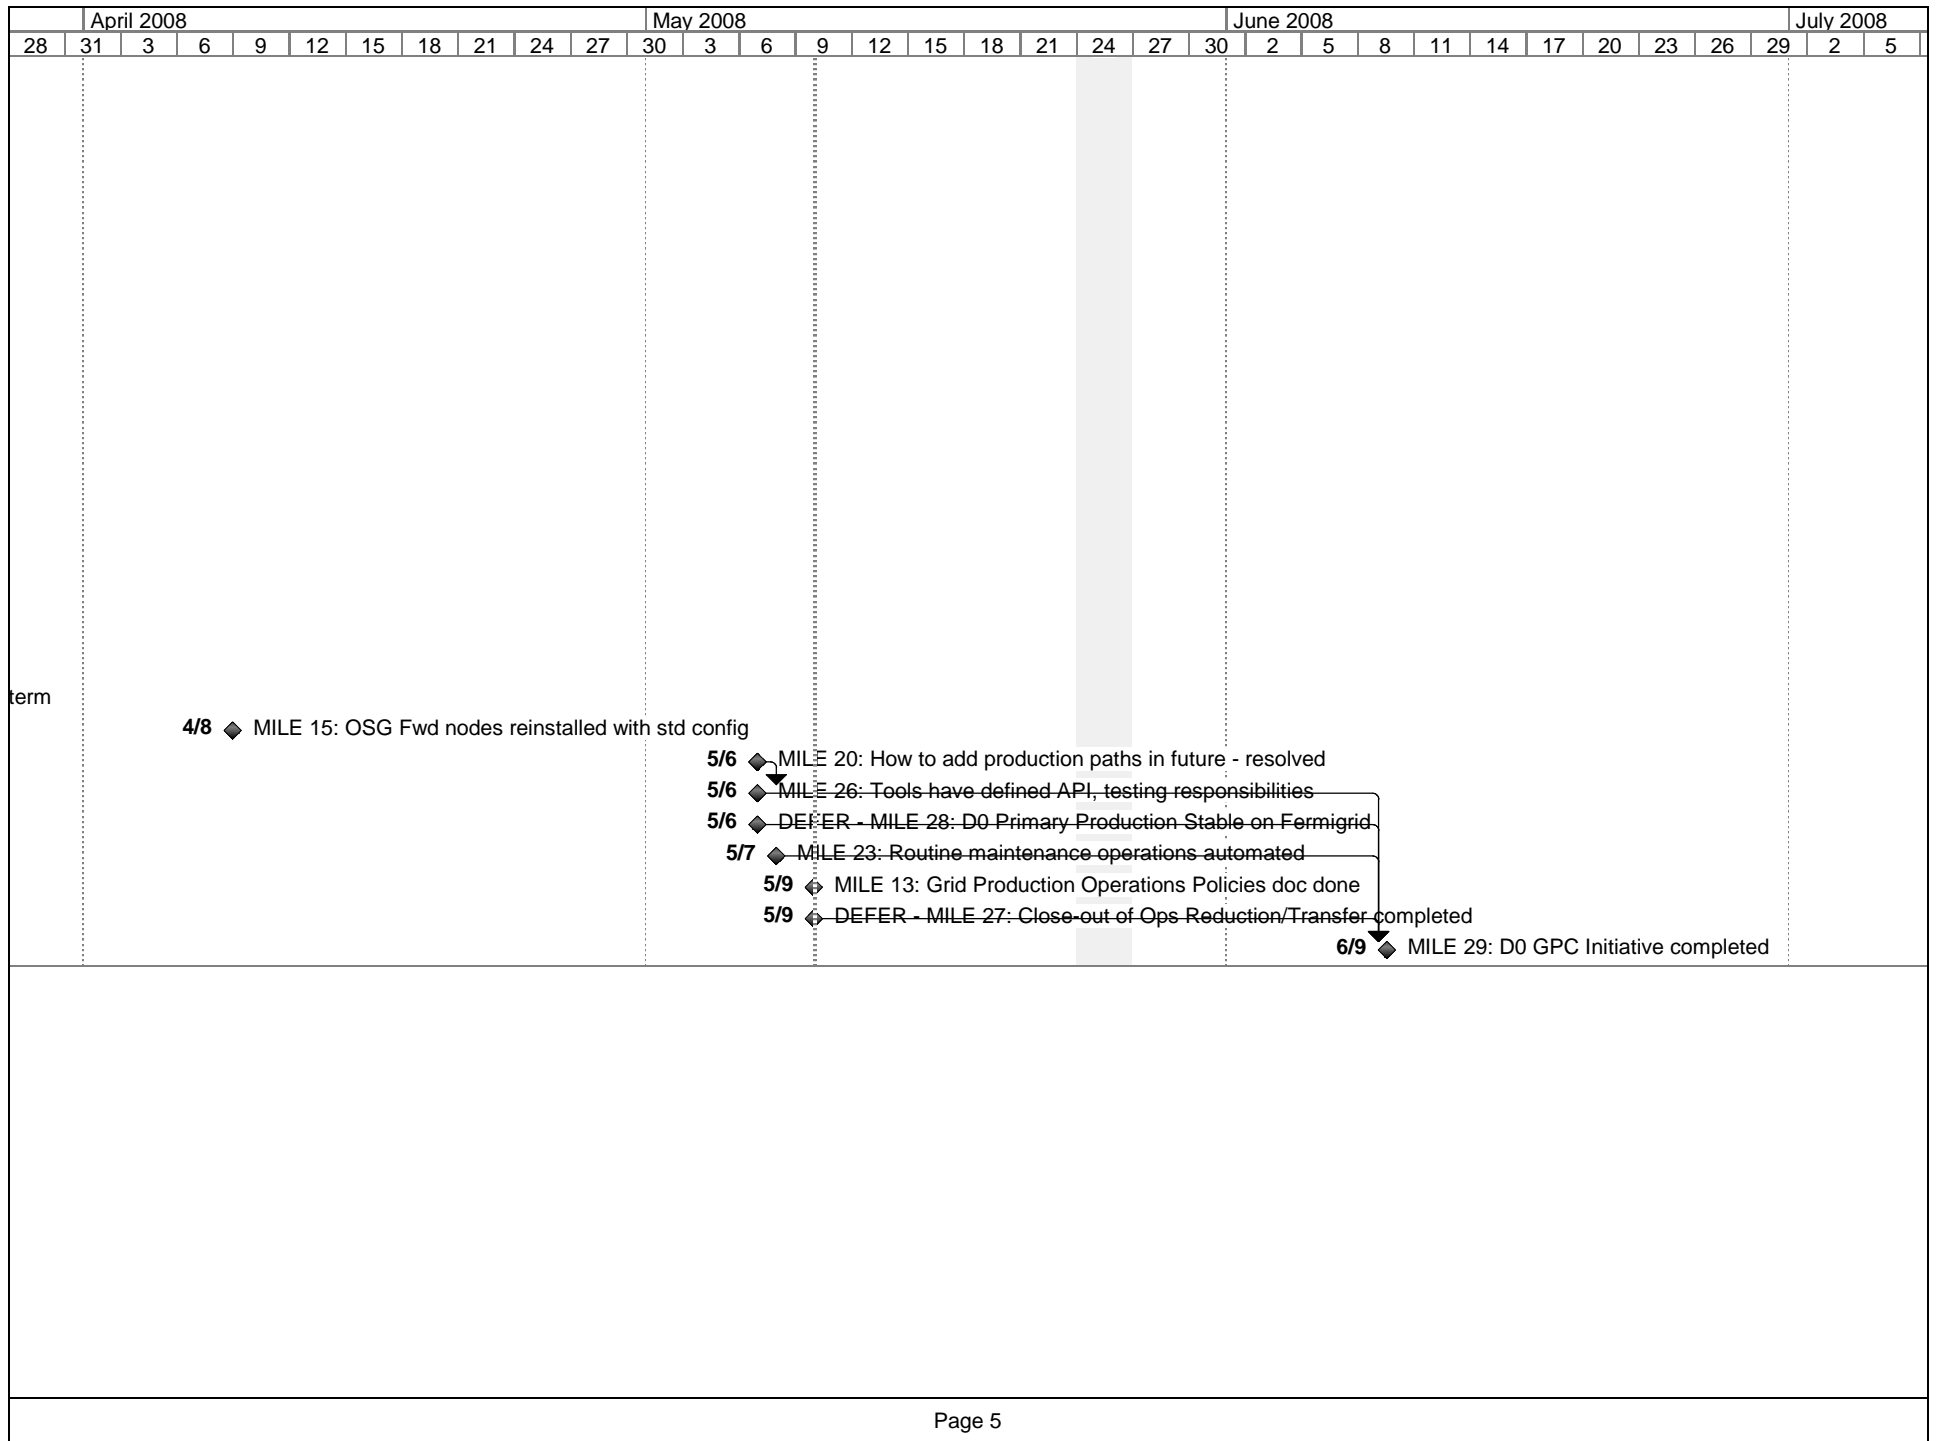

Project: D0 Grid Production Computin
Date: Sat 5/10/08

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

