


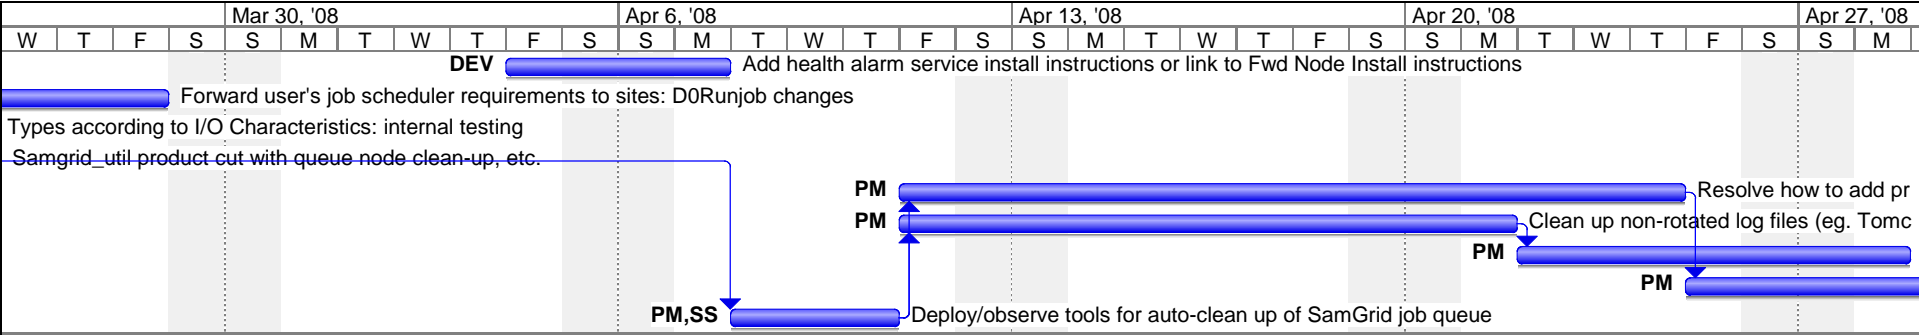


ID		WBS	Task Name	Contact	Resource Initials
312		3.5.5.18	Add health alarm service install instructions or link to Fwd Node Install instructions	AL	DEV
361		4.3.4.8	Forward user's job scheduler requirements to sites: D0Runjob changes	GG	PL,PM
42		2.7.14	Generalization of Job Types according to I/O Characteristics: internal testing	GG	PM
255		3.5.2.1.3	Samgrid_util product cut with queue node clean-up, etc.	GG	PM
46		2.7.2	Resolve how to add production paths in future: Document	GG	PM
264		3.5.2.2.6	Clean up non-rotated log files (eg. Tomcat): Logrotate part B	GG	PM
265		3.5.2.3	Automation of all gridmap file management (including condor_schedd)	GG	PM
59		2.9.1	Start Prod at Stage 2: SamGrid notification=all bug fix	GG	PM
256		3.5.2.1.4	Deploy/observe tools for auto-clean up of SamGrid job queue	GG	PM,SS

Duration	Start	Finish	Mar 2, '08							Mar 9, '08							Mar 16, '08							Mar 23, '08			
			S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
2 days	Fri 4/4/08	Mon 4/7/08																									
5 days	Mon 3/24/08	Fri 3/28/08																									
4 days	Tue 3/18/08	Fri 3/21/08																									
2 days	Mon 3/24/08	Tue 3/25/08																									
10 days	Fri 4/11/08	Thu 4/24/08																									
7 days	Fri 4/11/08	Mon 4/21/08																									
5 days	Tue 4/22/08	Mon 4/28/08																									
5 days	Fri 4/25/08	Thu 5/1/08																									
3 days	Tue 4/8/08	Thu 4/10/08																									





					May 4, '08							May 11, '08							May 18, '08							May 25, '08							Jun 1
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
roduction paths in future: Document																																	
cat): Logrotate part B																																	
Automation of all gridmap file management (including condor_schedd)																																	
<div></div> Start Prod at Stage 2: SamGrid notification=all bug fix																																	

Project: D0 Grid Production Computin
Date: Tue 3/18/08

Task



Split



Progress



Milestone



Summary



Project Summary



External Tasks



External Milestone



Deadline

