ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
0			**D0 Grid Production Computing Initiative**	**No**		**nnlein**				**#######**	**127.5 days?**
1		**1**	**D0 Grid Production Architecture**	**No**		**AL**				**0 edays**	**21 days**
2	✓	1.1	INPUT: Draft architecture document v1.2	No		AL	AL			0 edays	0 days
3	✓	1.2	Architecture document v2: draft - APIs, component responsibilities	No		AL	ASB,AL	2		0 edays	7 days
4	✓	1.3	MILESTONE: Draft architecture document v2	No		AL	AL	3		0 edays	0 days
5		1.4	Architecture document v2: Review	No		AL	RDK,ASB	4		0 edays	5 days
6		1.5	Architecture document v2: Revised version	No		AL	AL	5		0 edays	5 days
7		1.6	Architecture document v2: Approval - D0	No		AL	ASB	6		0 edays	2 days
8		1.7	Architecture document v2: Approval - CD	No		AL	ASB	6		0 edays	2 days
9		1.8	MILESTONE: D0 Grid Production Architecture document	No		AL	AL	8,7		0 edays	0 days
10		**2**	**Adjust Responsibilities among SamGrid, D0runjob, D0repro, automc tools**	**No**		**GG**				**0 edays**	**23 days?**
11		2.1	Define scope of work for automc	No				9	9	0 edays	1 day?
12		2.2	Define scope of work for D0 repro tools	No				9	9	0 edays	1 day?
13		2.3	Define scope of work for D0runjob	No				9	9	0 edays	1 day?
14		2.4	Define scope of work for SamGrid	No				9	9	0 edays	1 day?
15		2.5	Design achievable APIs, component responsibilities	No		??		11,12,:		0 edays	1 day?
16		2.6	Agreement on achievable architecture and plan to achieve it	No				15		0 edays	1 day?
17		2.7	Agreement on Unit and Integration testing responsibilities	No				16		0 edays	1 day?
18		2.8	Create document describing implementation of tool responsibilities	No				17		0 edays	1 day?
19		2.9	Resolve how to add production paths in future	Yes	MC4			18		0 edays	1 day?
20		2.10	MILESTONE: Adjusted Responsibilities defined	No				19		0 edays	0 days
21		2.11	Post-release evaluation of responsibilities	No				20		16 edays	5 days
22		2.12	MILESTONE: Achieve architecture-defined responsibilities among tools	No				21		0 edays	0 days
23		**3**	**Reduce Operations Load of Grid Production**	**No**		**GG,AL**				**0 edays**	**68 days**
24		**3.1**	**Current Operations**	**No**		**GG**				**0 edays**	**19 days**
25	✓	3.1.1	INPUT: Write-up of operations issues	No		GG	GG			0 edays	0 days
26	✓	3.1.2	Current Operations description: draft - level and causes	No		GG	GG	25		0 edays	4 days
27		3.1.3	Current Operations description: Review	No		GG	I,RDK,AL	26		0 edays	5 days
28		3.1.4	Current Operations description: Revised version	No		GG	GG	27		0 edays	5 days
29		3.1.5	Current Operations description: Approve	No		GG	ASB	28		0 edays	1 day
30		3.1.6	MILESTONE: Current Operations description	No		GG	GG	29		0 edays	0 days
31		**3.2**	**Future Operations**	**No**		**AL**				**0 edays**	**17 days**
32	✓	3.2.1	INPUT: FY08 REX budget determined	No		RS				0 edays	0 days
33	✓	3.2.2	Future Operations description: draft - acceptable load level and activities	No		AL	RS,AL	32		0 edays	6 days
34		3.2.3	Future Operations description: Review	No		AL	RDK,ASB	33		0 edays	5 days
35		3.2.4	Future Operations description: Revised version	No		AL	AL	34		0 edays	4 days
36		3.2.5	Future Operations description: Approve	No		AL	ASB	35		0 edays	2 days
37		3.2.6	MILESTONE: Future Operations description	No		AL	AL	36		0 edays	0 days

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
38		**3.3**	**Operations Reduction Plan**	**No**		**GG**				**0 edays**	**23 days**
39		3.3.1	Operations Reduction plan: outline - reduce load level to acceptable level	No		GG	L,AB2,RI	30,37		0 edays	5 days
40		3.3.2	Operations Reduction plan: draft	No		GG	L,AB2,RI	39		0 edays	5 days
41		3.3.3	Operations Reduction plan: Review	No		GG	SB,RDK	40		0 edays	5 days
42		3.3.4	Operations Reduction plan: Revised version	No		GG	L,AB2,RI	41		0 edays	6 days
43		3.3.5	Operations Reduction plan: Approve	No		GG	ASB,AL	42		0 edays	2 days
44		3.3.6	MILESTONE: Operations Reduction plan	No		GG	GG	43		0 edays	0 days
45		3.4	EXECUTE operations reduction plan	No		GG,AL		44		0 edays	19 days
46		3.5	Post-evaluation of operations load by dev and ops groups	No		GG,AL	l,AL,RDK	45		0 edays	5 days
47		3.6	MILESTONE: Achieve acceptable Operations level	No		GG,AL	GG,AL	46		0 edays	0 days
48		**4**	**Operations Support Transition from SamGrid to Run2 Ops**	**No**		**GG,AL**				**0 edays**	**44 days?**
49		**4.1**	**Operations Documentation**	**No**		**AL**				**0 edays**	**21 days**
50		**4.1.1**	**Data Queues Doc**	**No**		**AL**				**0 edays**	**15 days**
51	✓	4.1.1.1	INPUT: Data Queues Doc: Recent Draft	No		AL	AB2			0 edays	0 days
52	✓	4.1.1.2	Data Queues Doc: Feed-back, update	No		AL	AB3,AB2	51		0 edays	5 days
53		4.1.1.3	Data Queues Doc: Approve	No		AL	AL	52		0 edays	8 days
54		4.1.1.4	Data Queues Doc: Integrate into SamGrid Documentation	No		AL	DZ,PM	53		0 edays	2 days
55		4.1.1.5	MILESTONE: Data Queues Doc: Completed	No		AL	AL	54		0 edays	0 days
56		**4.1.2**	**Forwarding Node Installation Doc**	**Yes**	**Prd10**	**AL**				**0 edays**	**21 days**
57	✓	4.1.2.1	INPUT: Fwd Node Install Doc: Recent Draft	Yes	Prd10	AL	DZ			0 edays	0 days
58		4.1.2.2	Fwd Node Install Doc: Feed-back, update	Yes	Prd10	AL	DZ,SS	57		12 edays	7 days
59		4.1.2.3	Fwd Node Install Doc: Approve	Yes	Prd10	AL	AL	58		0 edays	3 days
60		4.1.2.4	Fwd Node Install Doc: Integrate into SamGrid Installation Manual	Yes	Prd10	AL	DZ	59		0 edays	2 days
61		4.1.2.5	MILESTONE: Fwd Node Install Doc: Completed	Yes	Prd10	AL	AL	60		0 edays	0 days
62		**4.1.3**	**Integrating SRM Storage with SAM Doc**	**No**		**GG**				**0 edays**	**7 days**
63		4.1.3.1	SRM with SAM Doc: Integrate into SamGrid Documentation	No		GG	AB2			0 edays	7 days
64		4.1.3.2	MILESTONE: SRM with SAM Doc: Completed	No		GG	GG	63		0 edays	0 days
65		4.1.4	MILESTONE: Operations Documentation prepared for transition	No		AL	AL	55,61,		0 edays	0 days
66		**4.2**	**Transition Plan**	**No**						**0 edays**	**1 day?**
67		4.2.1	Develop a multi-phase transition plan	No						35 edays	1 day?
68		4.2.2	Define processes for post-transition integration and deployment	No						35 edays	1 day?
69		4.2.3	Define processes for post-transition change requests, bug fixes	No						35 edays	1 day?
70		4.2.4	MILESTONE: Transition Plan completed	No				67,68,		0 edays	0 days
71		**4.3**	**Training**	**No**						**0 edays**	**1 day?**
72		4.3.1	General Training Sessions	No						40 edays	1 day?
73		4.3.2	Assisted Hands-on Real-life Experience	No						40 edays	1 day?
74		4.3.3	One-on-one Sessions on Specific Operations Topics	No						40 edays	1 day?
75		4.3.4	One-on-one Sessions on Specific Component Topics	No						40 edays	1 day?

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
76		4.3.5	MILESTONE: Training completed	No				72,73,		0 edays	0 days
77		4.4	Creation of SamGrid Integration Testbed	No						45 edays	1 day?
78		4.5	Support testing v7/d0runjob/SamGrid functionality (SAME ABOVE?)	Yes	MC3					45 edays	1 day?
79		4.6	Trial roll-out: Test processes pre-transition	No						45 edays	1 day?
80		4.7	Evaluate processes post-transition	No				79		13 edays	2 days
81		4.8	MILESTONE: Achieve support transition to Run2 Ops team	No				65,70,		0 edays	0 days
82		**5**	**Grid Production System**	**No**		**GG**				**0 edays**	**56 days?**
83	✓	**5.1**	**Decouple D0runjob macro and SamGrid**	**No**		**GG**				**0 edays**	**4 days**
84	✓	5.1.1	INPUT: Interface changes documented	No		GG	PM			0 edays	0 days
85	✓	5.1.2	Decouple D0runjob macro and SamGrid development work	No		GG	PL	84		0 edays	1 day
86	✓	5.1.3	Decoupling: MC Job Type: SamGrid Integration	No		GG	PM	85		0 edays	3 days
87		**5.2**	**Start Prod via SAM Definition from Stage 2 of Prod**	**Yes**	**MC2a**	**GG**				**0 edays**	**19 days**
88	✓	5.2.1	INPUT: Start Prod at Stage 2: D0runjob development	Yes	MC2a	GG	PL			0 edays	0 days
89		5.2.2	Start Prod at Stage 2: Request for d0runjob-only test	Yes	MC2a	GG	TA	88		12 edays	1 day
90		5.2.3	Start Prod at Stage 2: d0runjob-only test	Yes	MC2a	GG	JS	89		0 edays	4 days
91		5.2.4	Start Prod at Stage 2: SamGrid development/integration	Yes	MC2a	GG	PM	88,86	85	0 edays	8 days
92		5.2.5	Start Prod at Stage 2: Request for Prod-level test	Yes	MC2a	GG	TA	91,90		0 edays	1 day
93		5.2.6	Start Prod at Stage 2: Production-level test	Yes	MC2a	GG	JS	92		0 edays	4 days
94		5.2.7	MILESTONE: Start Prod at Stage 2 Ready for Production Release	Yes	MC2a	GG		93		0 edays	0 days
95		**5.3**	**Error Recovery in Phased Processing**	**No**		**GG**				**0 edays**	**21 days**
96	✓	5.3.1	Error Recovery: SamGrid development/integration	No		GG	PM			0 edays	1 day
97		5.3.2	Error Recovery: SamGrid, D0runjob integration	No		GG	PM	96		15 edays	5 days
98		5.3.3	Error Recovery: Production-level test	No		GG	JS	97		0 edays	5 days
99		5.3.4	MILESTONE: Error Recovery in Phased Processing	No		GG		98		0 edays	0 days
100		**5.4**	**VDT Version Migration**	**No**		**GG**				**0 edays**	**13 days**
101		5.4.1	VDT-oriented Testbed setup	No		GG	PM			15 edays	8 days
102		5.4.2	Migration to new VDT for security bug fixes	No		GG	PM	101		0 edays	5 days
103		5.4.3	MILESTONE: SamGrid migrated to new VDT version	No		GG		102		0 edays	0 days
104		**5.5**	**Fix "Immortal Jobs" Operations Issue**	**No**		**GG**				**0 edays**	**7 days**
105		5.5.1	Fix Immortal Jobs: SamGrid development/integration	No		GG	PM	103		0 edays	5 days
106		5.5.2	Fix Immortal Jobs: Production-level test	No		GG	JS	105		0 edays	2 days
107		5.5.3	MILESTONE: Fix Ready for Production Release	No		GG	GG	106		0 edays	0 days
108		**5.6**	**Automate Mgmt of XML database**	**No**		**GG**				**0 edays**	**12 days**
109		5.6.1	Auto Mgmt XML DB: Handle disk full condition	No		GG	PM			43 edays	2 days
110		5.6.2	Auto Mgmt XML DB: Large DB performance degradation	No		GG	PM	109	92	0 edays	5 days
111		5.6.3	Auto Mgmt XML DB: Infrequent index corruption	No		GG	PM	110	93	0 edays	5 days
112		5.6.4	MILESTONE: Ops Scripts automate mgmt of XML DB	No		GG	GG	109,11		0 edays	0 days
113		**5.7**	**Development Activities to Evaluate**	**No**						**0 edays**	**1 day?**

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
114		**5.7.1**	**Development Activities to Extend Recent Work**	**No**						**0 edays**	**1 day?**
115		5.7.1.1	D0runjob/SamGrid Decoupling: Skim Job Type	No						65 edays	1 day?
116		5.7.1.2	D0runjob/SamGrid Decoupling: Reco Job Type	No						65 edays	1 day?
117		5.7.1.3	D0runjob/SamGrid Decoupling: Merge Job Type	No						65 edays	1 day?
118		5.7.1.4	Start Prod via SAM Definition from Stage 3+ of Prod	Yes	MC2b					65 edays	1 day?
119		**5.7.2**	**Development Activities to Adjust Responsibilities**	**No**						**0 edays**	**1 day?**
120		5.7.2.1	D0repro tools adapted to use Sam v7	Yes	Prd7					65 edays	1 day?
121		5.7.2.2	D0runjob sets up its own environment	No						65 edays	1 day?
122		5.7.2.3	Fabric interface no longer dependent on Job Type	No						65 edays	1 day?
123		5.7.2.4	All merge code into D0runjob	No						65 edays	1 day?
124		**5.7.3**	**Development Activities to Automate Operations**	**No**						**0 edays**	**1 day?**
125		5.7.3.1	Adoption of Runjob macro-preprocessor	No						65 edays	1 day?
126		5.7.3.2	Generalization of Job Types according to I/O Characteristics	No						65 edays	1 day?
127		5.7.3.3	Worker Node Environment Testbed for Runjob	No						65 edays	1 day?
128		5.7.3.4	Monitoring Information improvements	No						65 edays	1 day?
129		5.7.3.5	Minimal Resource Brokering	Yes	Prd9					65 edays	1 day?
130		5.8	MILESTONE: Grid Production System completed	No				94,107		0 edays	0 days
131		**6**	**Current Work: D0 Apps on Grid Production System**	**No**		**ASB**				**0 edays**	**46 days?**
132		**6.1**	**Reco**	**No**						**0 edays**	**16 days**
133		**6.1.1**	**D0 Primary Production on Fermigrid**	**No**		**MD**				**0 edays**	**16 days**
134	✓	6.1.1.1	INPUT: Attempt to run D0 Primary Production on FermiGrid	No		MD	MD			0 edays	0 days
135	✓	6.1.1.2	OSG/Fermigrid Resource Selection Meeting	No		MD		134		0 edays	0.1 days
136	✓	6.1.1.3	Create/config D0Production role/account: Fermigrid, GUMS, CAB, PBS	No		ST/JB?		135		0 edays	6 days
137	✓	6.1.1.4	Run D0 Primary Prod via D0Production role	No		MD	MD	136		0 edays	1 day
138	✓	6.1.1.5	Fix d0srv065 storage issues	No		MD	PM	137		0 edays	1 day
139		6.1.1.6	Run D0 Primary Prod to verify storage fix	No		MD	MD	138		0 edays	2 days
140		6.1.1.7	Create/config D0 Prod submission service	No		ST?		136		0 edays	6 days
141		6.1.1.8	Run D0 Primary Prod via D0 Prod submission service	No		MD	MD	140,13	133	0 edays	2 days
142		6.1.1.9	MILESTONE: D0 Primary Production Run on Fermigrid	No		MD	MD	141		0 edays	0 days
143		**6.2**	**MC Production**	**Yes**						**0 edays**	**1 day?**
144		6.2.1	Ability to write out any stage of output	Yes	MC1					65 edays	1 day?
145		6.3	MILESTONE: Achieve deployment or functionality necessary to support future de	No				132,14		0 edays	0 days
146		**7**	**Eval for Future: D0 Apps on Grid Production System**	**No**		**ASB**				**0 edays**	**1 day?**
147		**7.1**	**Reco**	**Yes**						**0 edays**	**1 day?**
148		7.1.1	Ability to merge more than 1 stream from Reco	Yes	Prd5					65 edays	1 day?
149		**7.2**	**MC Production**	**Yes**						**0 edays**	**1 day?**
150		7.2.1	Ability to run TrigSim in MC Production	Yes	MC5					65 edays	1 day?
151		**7.3**	**Skimming**	**Yes**						**0 edays**	**1 day?**

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
152		7.3.1	Skimming in Production	Yes	Prd1					65 edays	1 day?
153		7.4	Fixing	Yes	Prd11					65 edays	1 day?
154		**7.5**	**Raw2Sim**	**Yes**						**0 edays**	**1 day?**
155		7.5.1	Run raw2siim on minbias files	Yes	Prd3					65 edays	1 day?
156		**7.6**	**Reco-cert**	**Yes**						**0 edays**	**1 day?**
157		7.6.1	Merging of reco-cert files	Yes	Prd4					65 edays	1 day?
158		7.6.2	Stand-alone production of reco-cert output	Yes	Prd8					65 edays	1 day?
159		**7.7**	**CAF**	**Yes**						**0 edays**	**1 day?**
160		7.7.1	CAF Trees from Production	Yes	Prd2					65 edays	1 day?
161		7.8	MC CAF	No						65 edays	1 day?
162		7.9	AADST	Yes	Prd6					65 edays	1 day?
163		7.10	Grid Analysis	Yes	Prd12					65 edays	1 day?
164		7.11	MILESTONE: Evaluation of work necessary for future deployment	No				147,14		0 edays	0 days
165		**8**	**Project Management**	**No**		**RDK**				**0 edays**	**127.5 days**
166		8.1	INPUT: Draft Preliminary High-level WBS	No		RDK	RDK			0 edays	0 days
167		**8.2**	**Initiative Coordination Meeting**	**No**		**RDK**				**0 edays**	**123.13 days**
168		8.2.1	Initiative Coordination Meeting 1	No				166		0 edays	1 hr
169		8.2.2	Initiative Coordination Meeting 2	No						0 edays	1 hr
170		8.2.3	Initiative Coordination Meeting 3	No						0 edays	1 hr
171		8.2.4	Initiative Coordination Meeting 4	No						0 edays	1 hr
172		8.2.5	Initiative Coordination Meeting 5	No						0 edays	1 hr
173		8.2.6	Initiative Coordination Meeting 6	No						0 edays	1 hr
174		8.2.7	Initiative Coordination Meeting 7	No						0 edays	1 hr
175		8.2.8	Initiative Coordination Meeting 8	No						0 edays	1 hr
176		8.2.9	Initiative Coordination Meeting 9	No						0 edays	1 hr
177		8.2.10	Initiative Coordination Meeting 10	No						0 edays	1 hr
178		8.2.11	Initiative Coordination Meeting 11	No						0 edays	1 hr
179		8.2.12	Initiative Coordination Meeting 12	No						0 edays	1 hr
180		8.2.13	Initiative Coordination Meeting 13	No						0 edays	1 hr
181		8.2.14	Initiative Coordination Meeting 14	No						0 edays	1 hr
182		**8.3**	**Planning and Setup**	**No**		**RDK**				**0 edays**	**42 days**
183		8.3.1	WBS/Schedule v0.8 for 3/7 objectives	No		RDK	RDK	168		0 edays	10 days
184		8.3.2	MILESTONE: WBS/Schedule v0.8, begin weekly status'ing	No		RDK	RDK	183		0 edays	0 days
185		8.3.3	WBS/Schedule v1.0 for 5/7 objectives	No		RDK	RDK	184		0 edays	5 days
186		8.3.4	Project Definition Document: Draft w/o WBS/Schedule	No		RDK	RDK	184		0 edays	5 days
187		8.3.5	Project Definition Document: Integrate components, feed-back	No		RDK	RDK	186		0 edays	1 day
188		8.3.6	Project Definition Approval: ABS, CD	No		RDK	RDK,ASB	185,18		0 edays	1 day
189		8.3.7	MILESTONE: Plan v1.0 sufficient to drive near-term work	No		RDK	RDK	188		0 edays	0 days

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

ID		WBS	Task Name	D0 eques	D0 Reques Id	Lead	Resource Initials	Predec	Soft Links	Leveling Delay	Duration
190		8.3.8	Baseline WBS/Schedule v1.1 for ~7/7 objectives	No		RDK	RDK	189		0 edays	14 days
191		8.3.9	Project Execution Plan: Draft w/o WBS/Schedule	No		RDK	RDK	189		0 edays	14 days
192		8.3.10	Project Execution Plan: Integrate components, feed-back	No		RDK	RDK	191,19		0 edays	1 day
193		8.3.11	Project Execution Plan Approval: ABS, CD	No		RDK	RDK,ASB	192		0 edays	1 day
194		8.3.12	MILESTONE: Plan v1.1 project baseline	No		RDK	RDK	193		0 edays	0 days
195		**8.4**	**Project Administration**	**No**		**RDK**				**0 edays**	**116.4 days**
196		8.4.1	Planning Phase (Level of Effort = 5%)	No		RDK	RDK	184		0 edays	23 days
197		8.4.2	Execution Phase (Level of Effort = 15%)	No		RDK	RDK	196,19		1 eday	80 days
198		**8.4.3**	**Close-Out Phase**	**No**		**RDK**	**RDK**	**1,23,4**		**0 edays**	**3.5 days**
199		8.4.3.1	Project Close-out Meeting	No		RDK	RDK			0 edays	0.5 days
200		8.4.3.2	Project Close-out Report	No		RDK	RDK	199		0 edays	1.5 days
201		8.4.3.3	Project Close-out Report Approval: ABS, CD	No		RDK	RDK,ASB	200		0 edays	1 day
202		8.4.3.4	Archive project artifacts	No		RDK	RDK	201		0 edays	0.5 days
203		8.4.3.5	MILESTONE: Initiative Closed-out	No		RDK	RDK	202		0 edays	0 days
204		**8.5**	**Critical Resource Accounting**	**No**		**RDK**				**0 edays**	**124 days**
205		8.5.1	SamGrid Support (Level of Effort = 25%)	No		GG	PM			0 edays	109 days
206		9	MILESTONE: Initiative completed	No		ASB	ASB	203		0 edays	0 days

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Sun 7/1/07	**Mon 1/7/08**
Sun 7/1/07	**Tue 7/31/07**
Sun 7/1/07	Sun 7/1/07
Thu 7/5/07	Fri 7/13/07
Fri 7/13/07	Fri 7/13/07
Mon 7/16/07	Fri 7/20/07
Mon 7/23/07	Fri 7/27/07
Mon 7/30/07	Tue 7/31/07
Mon 7/30/07	Tue 7/31/07
Tue 7/31/07	Tue 7/31/07
Wed 8/1/07	**Fri 8/31/07**
Wed 8/1/07	Wed 8/1/07
Wed 8/1/07	Wed 8/1/07
Wed 8/1/07	Wed 8/1/07
Wed 8/1/07	Wed 8/1/07
Thu 8/2/07	Thu 8/2/07
Fri 8/3/07	Fri 8/3/07
Mon 8/6/07	Mon 8/6/07
Tue 8/7/07	Tue 8/7/07
Wed 8/8/07	Wed 8/8/07
Wed 8/8/07	Wed 8/8/07
Mon 8/27/07	Fri 8/31/07
Fri 8/31/07	Fri 8/31/07
Sun 7/1/07	**Fri 10/5/07**
Sun 7/1/07	**Fri 7/27/07**
Sun 7/1/07	Sun 7/1/07
Mon 7/9/07	Thu 7/12/07
Fri 7/13/07	Thu 7/19/07
Fri 7/20/07	Thu 7/26/07
Fri 7/27/07	Fri 7/27/07
Fri 7/27/07	Fri 7/27/07
Mon 7/9/07	**Tue 7/31/07**
Mon 7/9/07	Mon 7/9/07
Mon 7/9/07	Mon 7/16/07
Tue 7/17/07	Mon 7/23/07
Tue 7/24/07	Fri 7/27/07
Mon 7/30/07	Tue 7/31/07
Tue 7/31/07	Tue 7/31/07

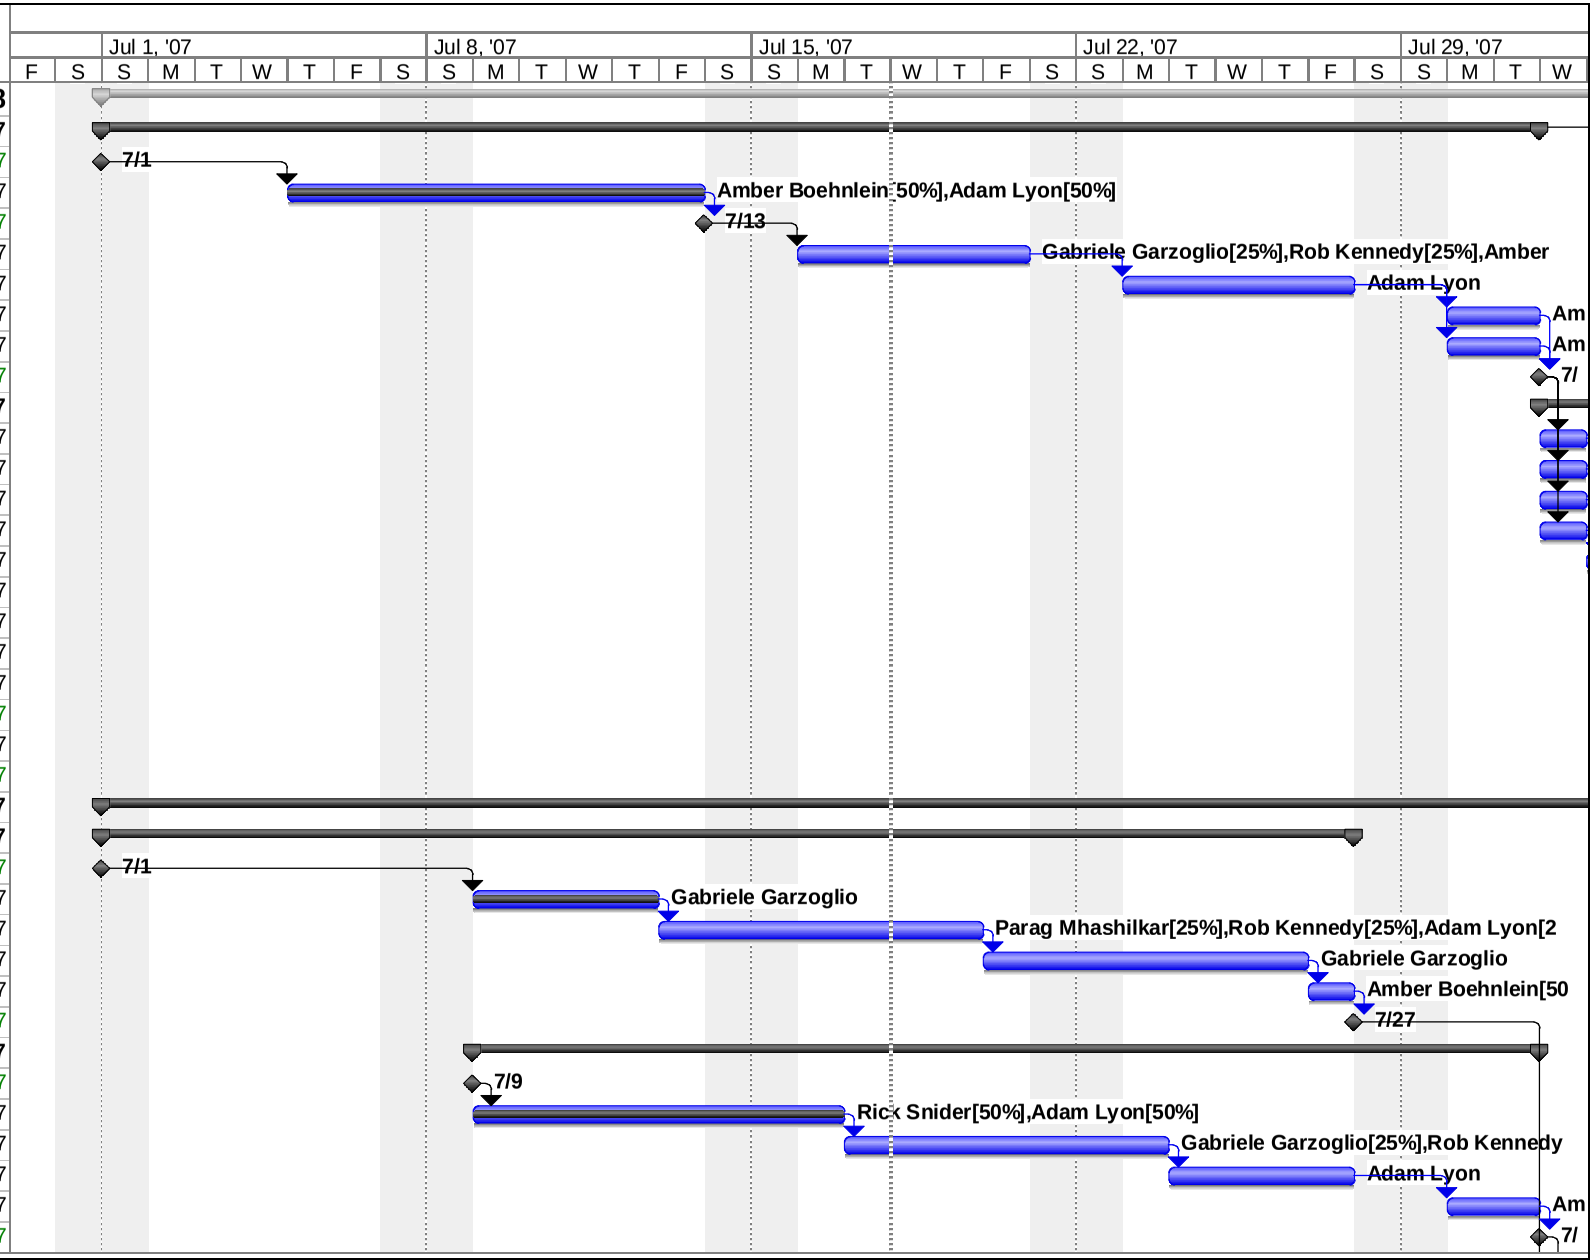

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Wed 8/1/07	**Fri 8/31/07**
Wed 8/1/07	Tue 8/7/07
Wed 8/8/07	Tue 8/14/07
Wed 8/15/07	Tue 8/21/07
Wed 8/22/07	Wed 8/29/07
Thu 8/30/07	Fri 8/31/07
Fri 8/31/07	Fri 8/31/07
Tue 9/4/07	Fri 9/28/07
Mon 10/1/07	Fri 10/5/07
Fri 10/5/07	Fri 10/5/07
Mon 7/2/07	**Fri 8/31/07**
Mon 7/2/07	**Tue 7/31/07**
Mon 7/2/07	**Mon 7/23/07**
Mon 7/2/07	Mon 7/2/07
Mon 7/2/07	Mon 7/9/07
Tue 7/10/07	Thu 7/19/07
Fri 7/20/07	Mon 7/23/07
Mon 7/23/07	Mon 7/23/07
Mon 7/2/07	**Tue 7/31/07**
Mon 7/2/07	Mon 7/2/07
Mon 7/16/07	Tue 7/24/07
Wed 7/25/07	Fri 7/27/07
Mon 7/30/07	Tue 7/31/07
Tue 7/31/07	Tue 7/31/07
Thu 7/12/07	**Fri 7/20/07**
Thu 7/12/07	Fri 7/20/07
Fri 7/20/07	Fri 7/20/07
Tue 7/31/07	Tue 7/31/07
Mon 8/6/07	**Mon 8/6/07**
Mon 8/6/07	Mon 8/6/07
Mon 8/6/07	Mon 8/6/07
Mon 8/6/07	Mon 8/6/07
Mon 8/6/07	Mon 8/6/07
Mon 8/13/07	**Mon 8/13/07**
Mon 8/13/07	Mon 8/13/07
Mon 8/13/07	Mon 8/13/07
Mon 8/13/07	Mon 8/13/07
Mon 8/13/07	Mon 8/13/07

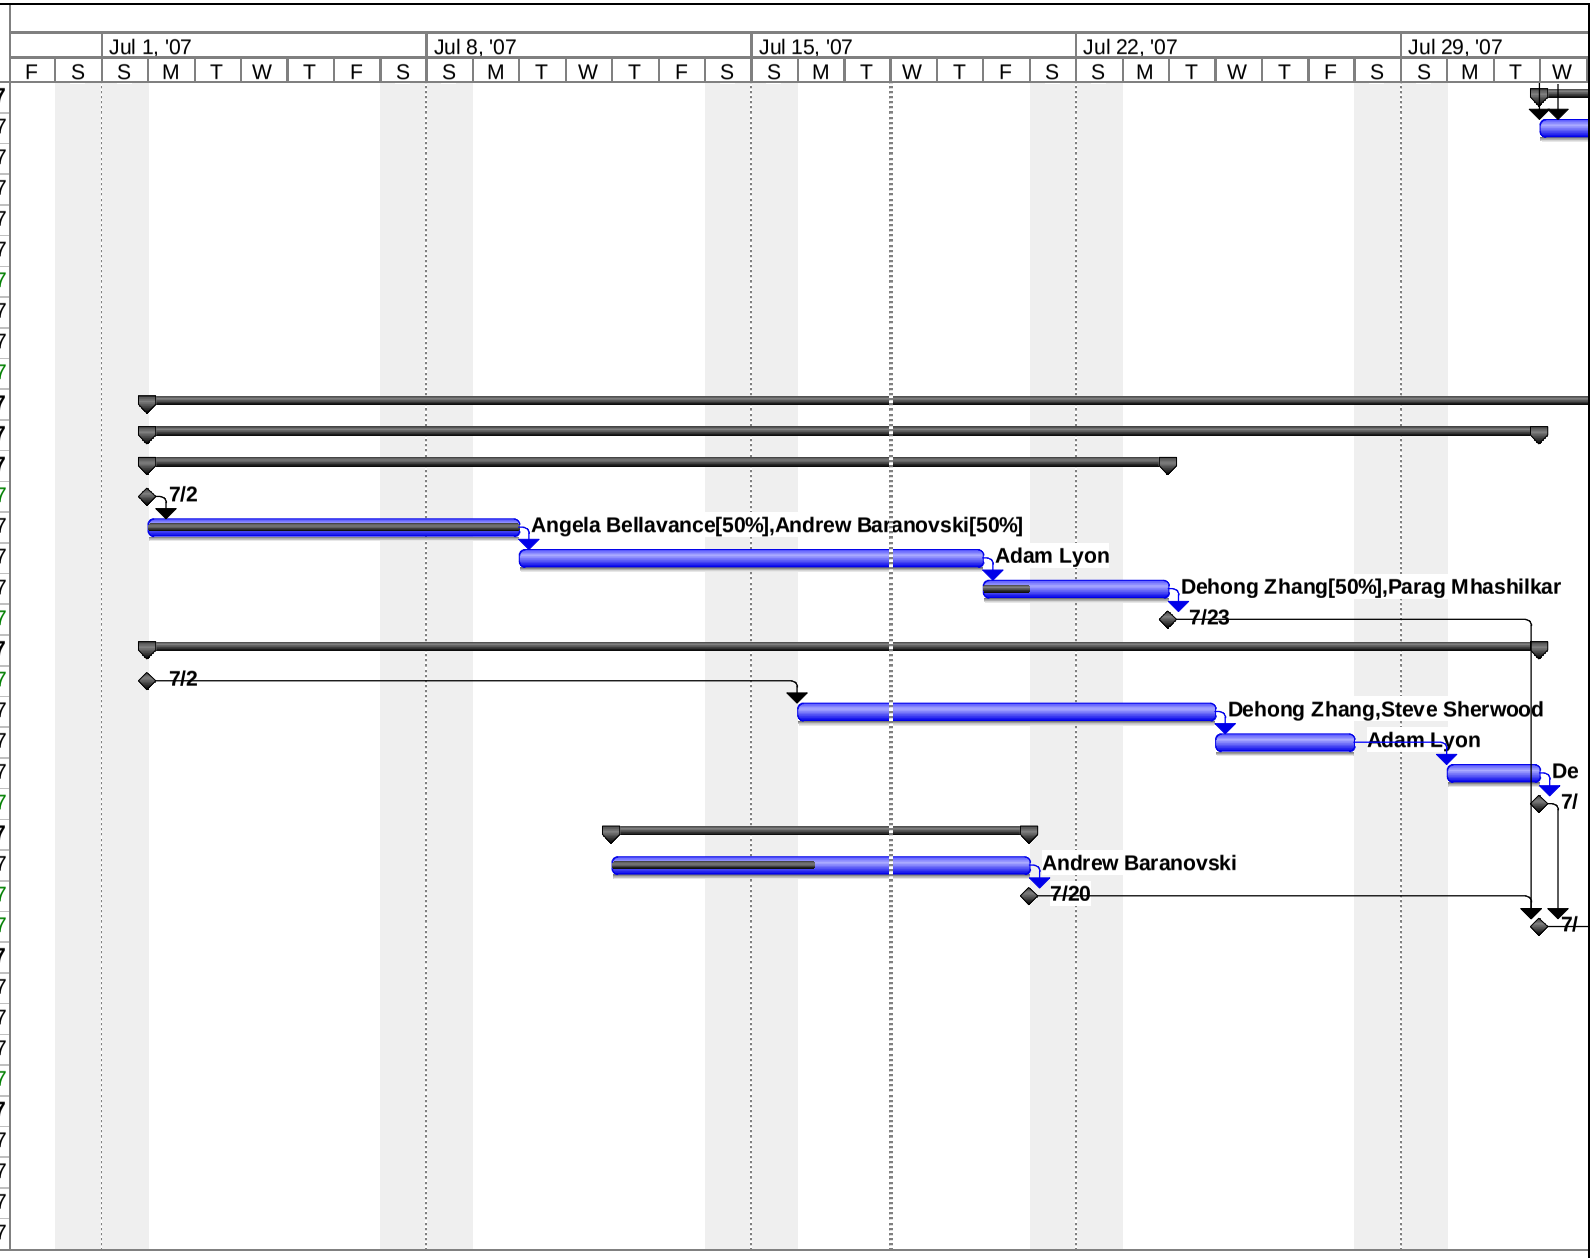

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Mon 8/13/07	Mon 8/13/07
Thu 8/16/07	Thu 8/16/07
Thu 8/16/07	Thu 8/16/07
Thu 8/16/07	Thu 8/16/07
Thu 8/30/07	Fri 8/31/07
Fri 8/31/07	Fri 8/31/07
Mon 7/2/07	**Wed 9/19/07**
Mon 7/2/07	**Fri 7/6/07**
Mon 7/2/07	Mon 7/2/07
Mon 7/2/07	Mon 7/2/07
Tue 7/3/07	Fri 7/6/07
Mon 7/2/07	**Fri 7/27/07**
Mon 7/2/07	Mon 7/2/07
Mon 7/16/07	Mon 7/16/07
Tue 7/17/07	Fri 7/20/07
Tue 7/10/07	Fri 7/20/07
Mon 7/23/07	Mon 7/23/07
Tue 7/24/07	Fri 7/27/07
Fri 7/27/07	Fri 7/27/07
Mon 7/2/07	**Tue 7/31/07**
Mon 7/2/07	Mon 7/2/07
Wed 7/18/07	Tue 7/24/07
Wed 7/25/07	Tue 7/31/07
Tue 7/31/07	Tue 7/31/07
Wed 7/18/07	**Fri 8/3/07**
Wed 7/18/07	Fri 7/27/07
Mon 7/30/07	Fri 8/3/07
Fri 8/3/07	Fri 8/3/07
Mon 8/6/07	**Tue 8/14/07**
Mon 8/6/07	Fri 8/10/07
Mon 8/13/07	Tue 8/14/07
Tue 8/14/07	Tue 8/14/07
Tue 9/4/07	**Wed 9/19/07**
Tue 9/4/07	Wed 9/5/07
Thu 9/6/07	Wed 9/12/07
Thu 9/13/07	Wed 9/19/07
Wed 9/19/07	Wed 9/19/07
Wed 9/5/07	**Wed 9/5/07**

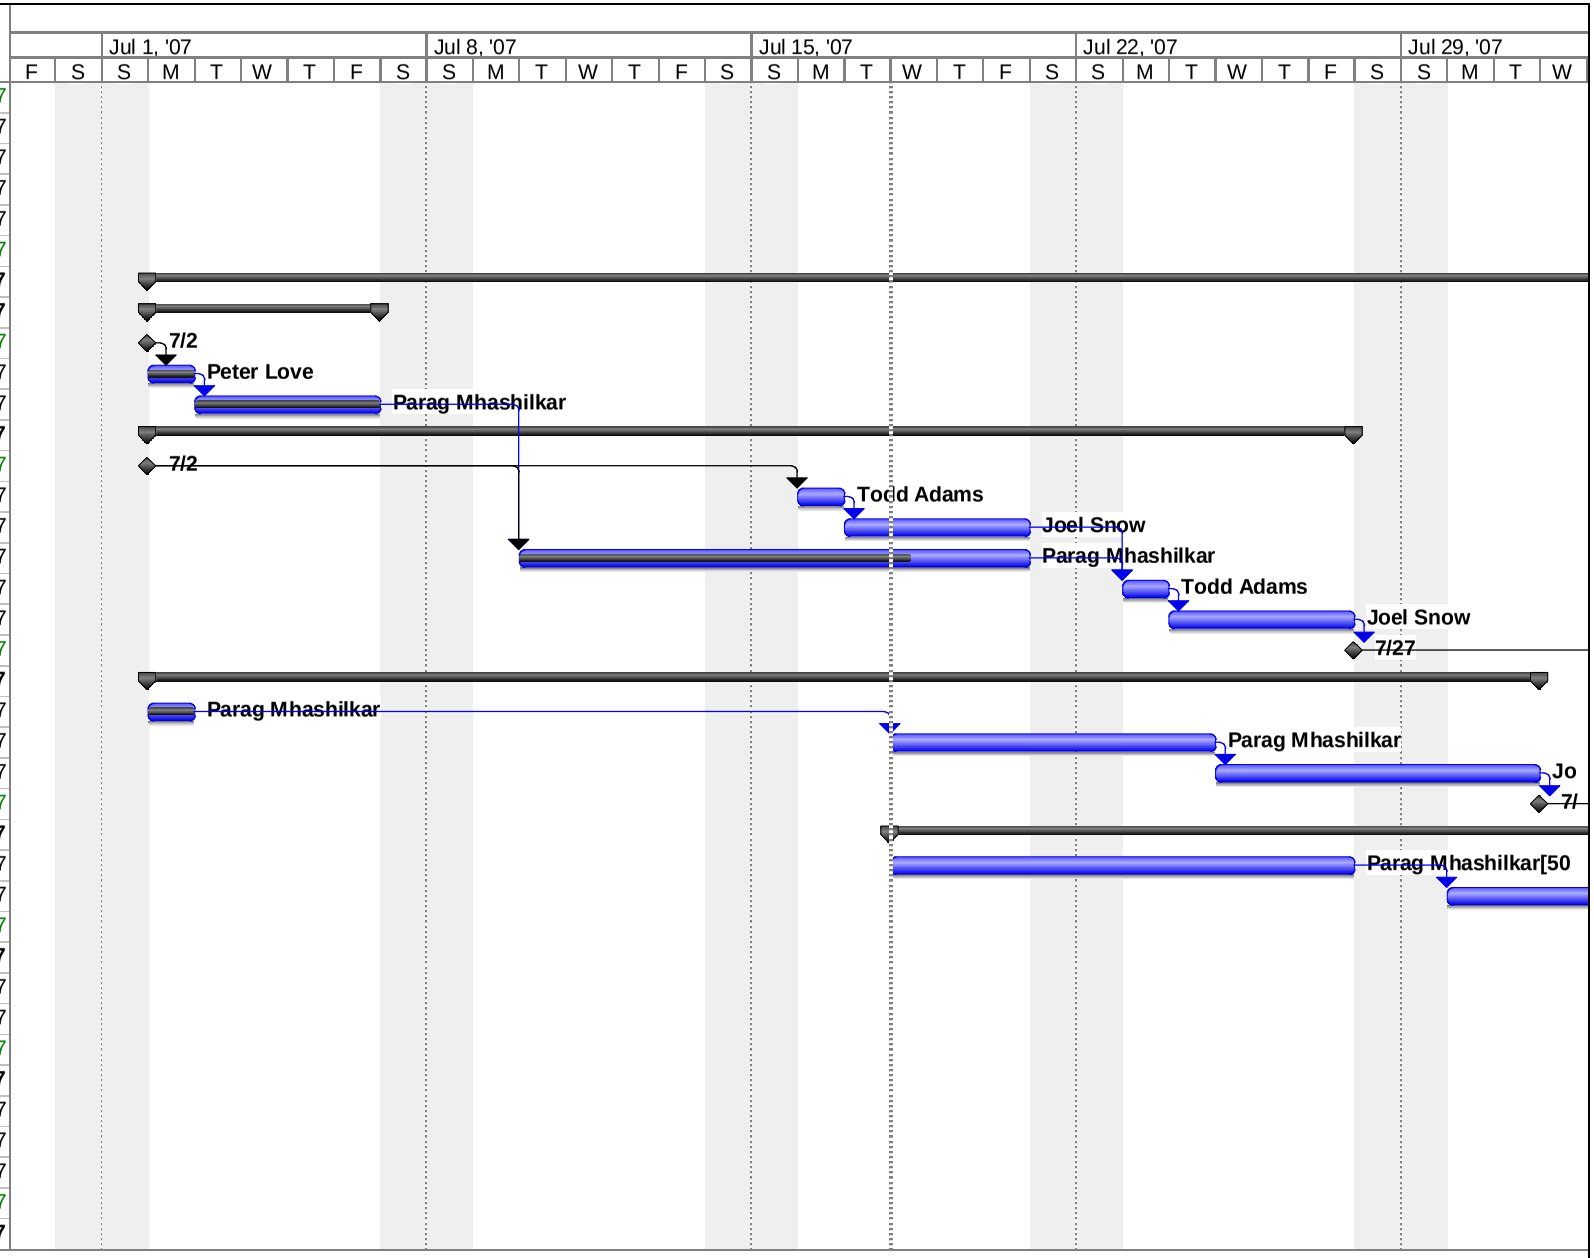

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/19/07	Wed 9/19/07
Sun 7/1/07	**Wed 9/5/07**
Sun 7/1/07	**Tue 7/24/07**
Sun 7/1/07	**Tue 7/24/07**
Sun 7/1/07	Sun 7/1/07
Tue 7/3/07	Tue 7/3/07
Thu 7/5/07	Thu 7/12/07
Fri 7/13/07	Fri 7/13/07
Mon 7/16/07	Mon 7/16/07
Tue 7/17/07	Wed 7/18/07
Fri 7/13/07	Fri 7/20/07
Mon 7/23/07	Tue 7/24/07
Tue 7/24/07	Tue 7/24/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**

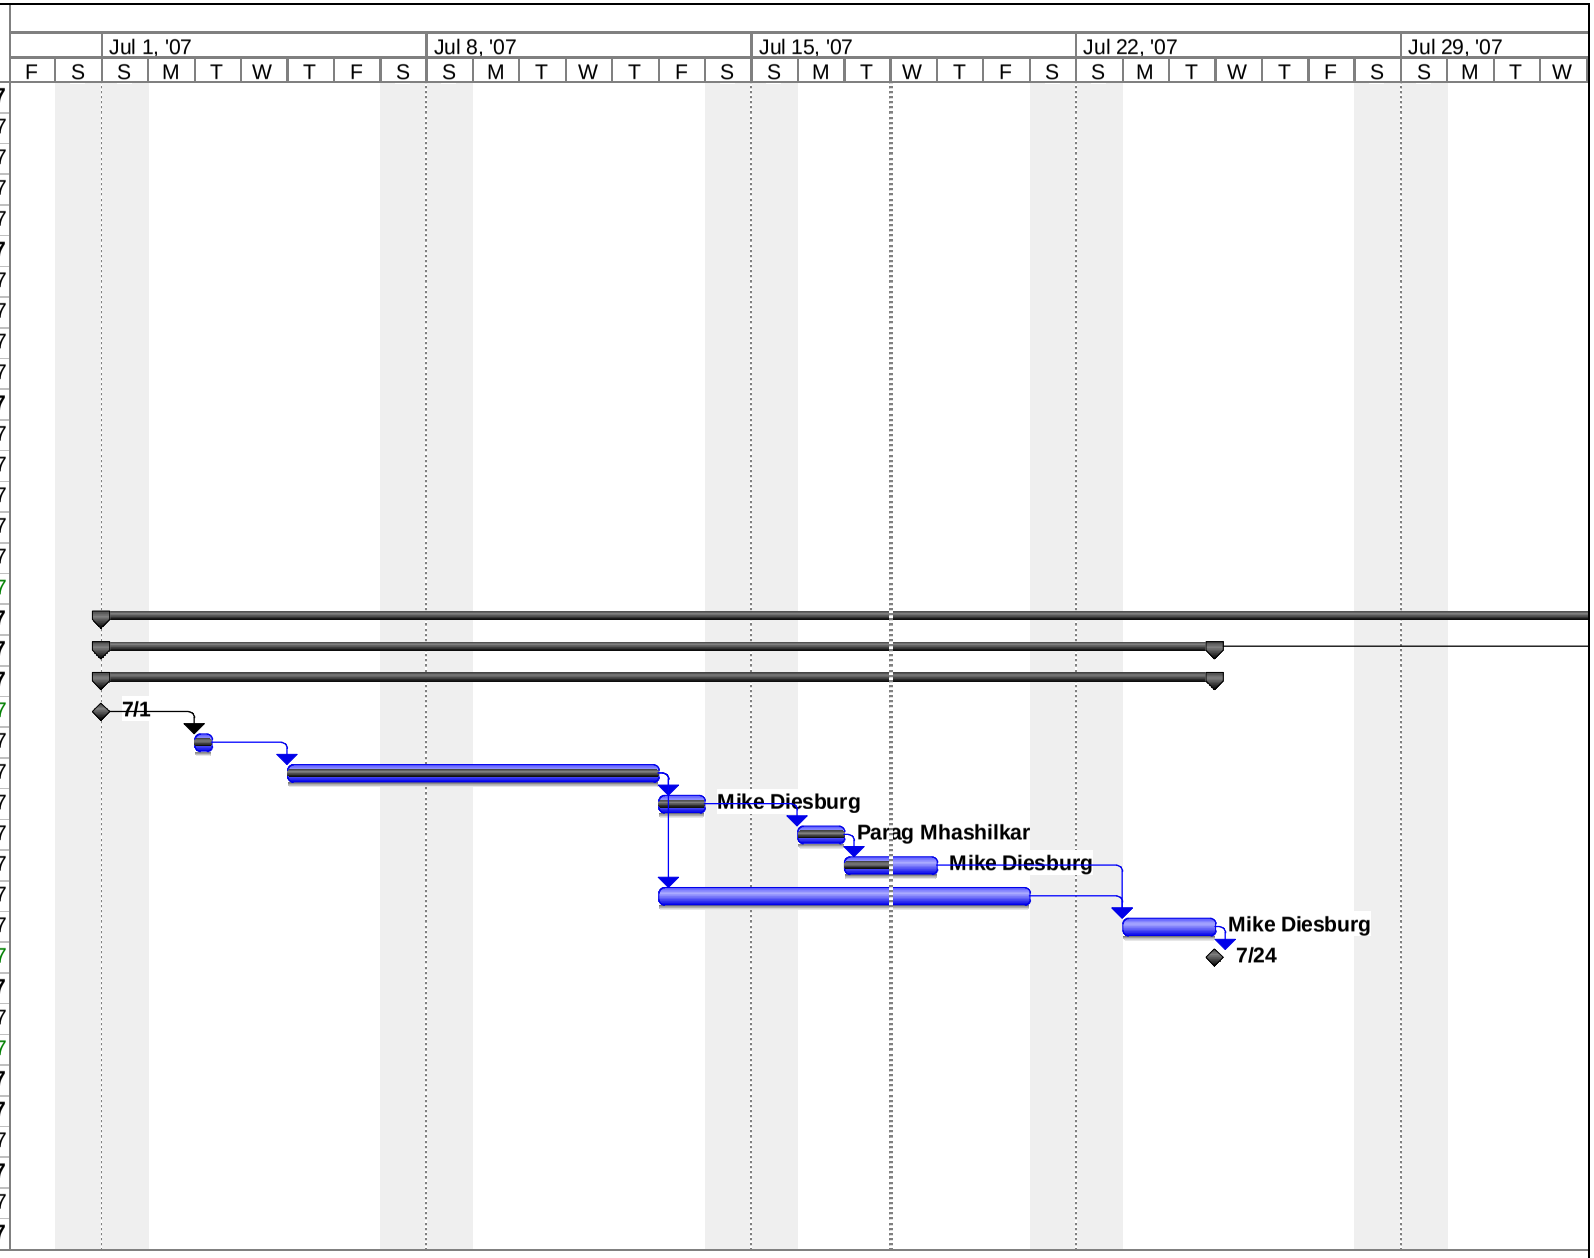

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	**Wed 9/5/07**
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Wed 9/5/07	Wed 9/5/07
Sun 7/1/07	**Mon 1/7/08**
Sun 7/1/07	Sun 7/1/07
Tue 7/3/07	**Wed 1/2/08**
Tue 7/3/07	Tue 7/3/07
Tue 7/17/07	Tue 7/17/07
Tue 7/31/07	Tue 7/31/07
Tue 8/14/07	Tue 8/14/07
Tue 8/28/07	Tue 8/28/07
Tue 9/11/07	Tue 9/11/07
Tue 9/25/07	Tue 9/25/07
Tue 10/9/07	Tue 10/9/07
Tue 10/23/07	Tue 10/23/07
Tue 11/6/07	Tue 11/6/07
Tue 11/20/07	Tue 11/20/07
Tue 12/4/07	Tue 12/4/07
Tue 12/18/07	Tue 12/18/07
Wed 1/2/08	Wed 1/2/08
Tue 7/3/07	**Fri 8/31/07**
Tue 7/3/07	Wed 7/18/07
Wed 7/18/07	Wed 7/18/07
Wed 7/18/07	Fri 7/27/07
Wed 7/18/07	Fri 7/27/07
Fri 7/27/07	Mon 7/30/07
Mon 7/30/07	Tue 7/31/07
Tue 7/31/07	Tue 7/31/07

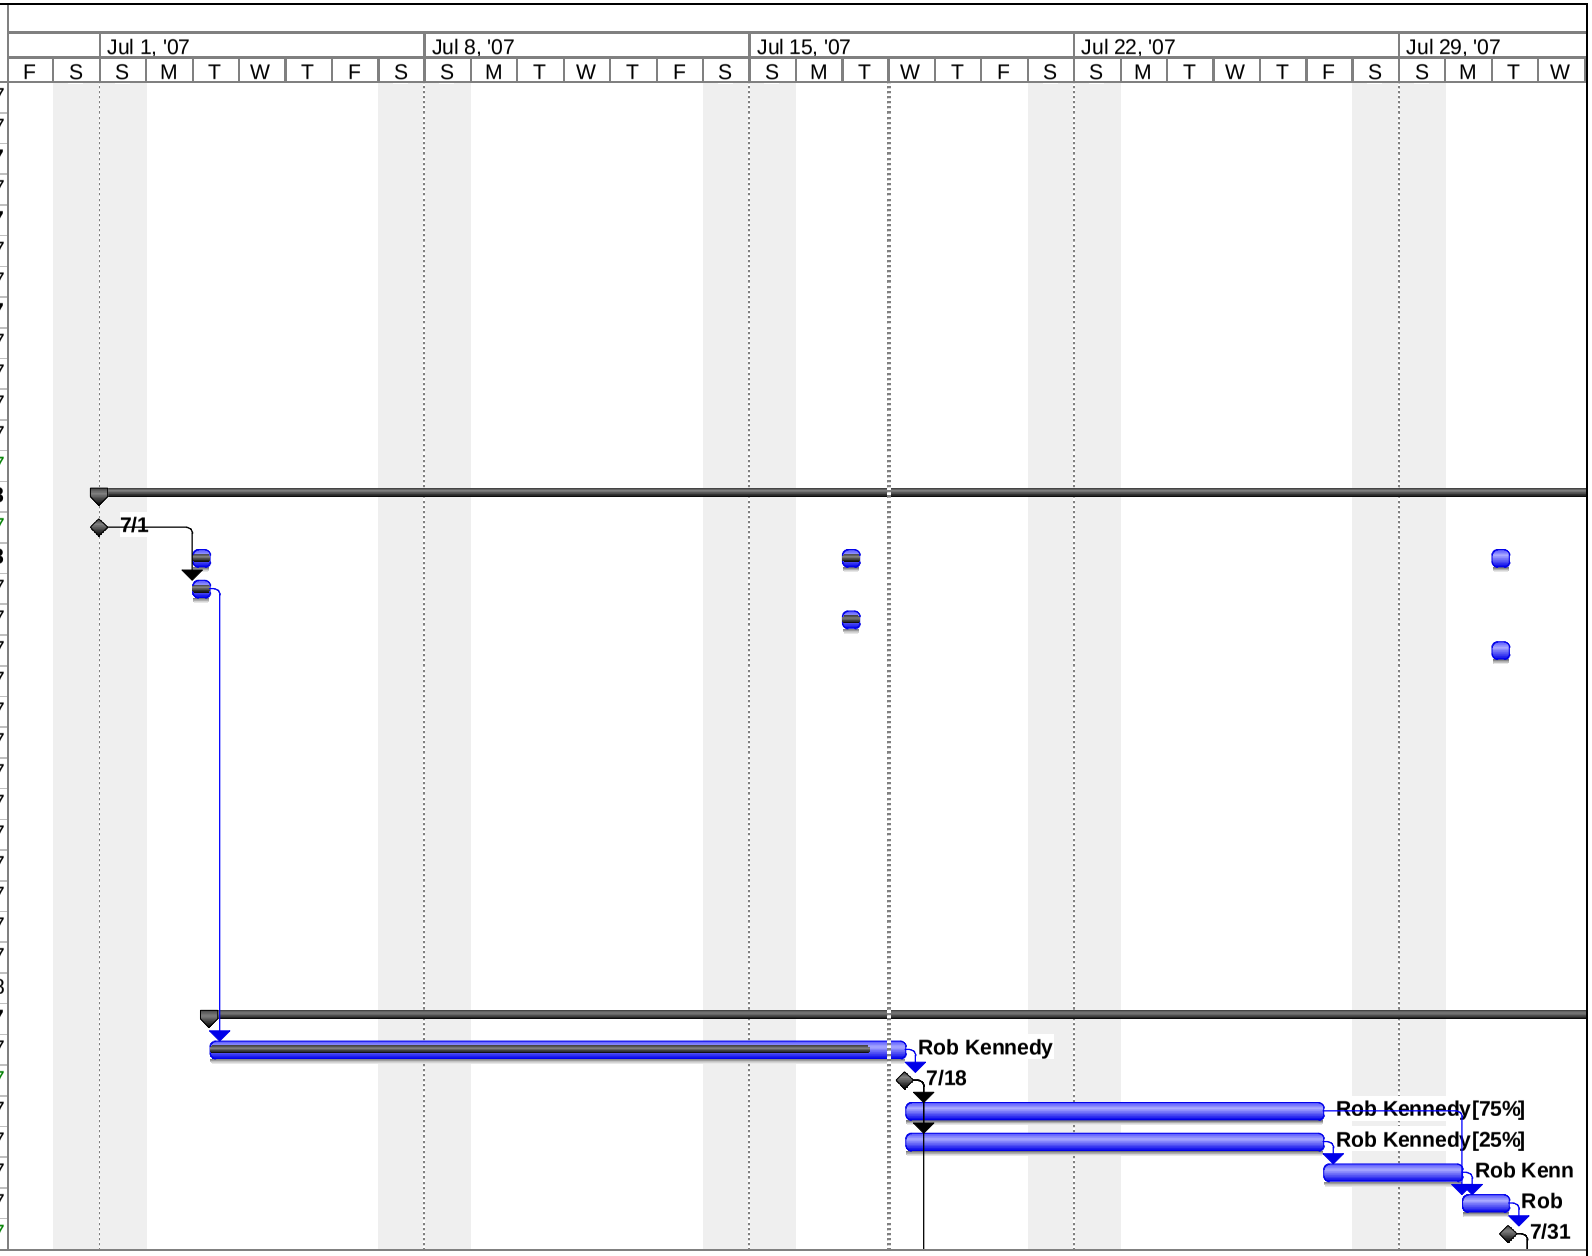

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

Start	Finish
Tue 7/31/07	Wed 8/29/07
Tue 7/31/07	Wed 8/29/07
Wed 8/29/07	Thu 8/30/07
Thu 8/30/07	Fri 8/31/07
Fri 8/31/07	Fri 8/31/07
Wed 7/18/07	**Mon 1/7/08**
Wed 7/18/07	Fri 8/31/07
Tue 9/4/07	Fri 12/28/07
Wed 1/2/08	**Mon 1/7/08**
Wed 1/2/08	Wed 1/2/08
Wed 1/2/08	Thu 1/3/08
Fri 1/4/08	Fri 1/4/08
Mon 1/7/08	Mon 1/7/08
Mon 1/7/08	Mon 1/7/08
Mon 7/2/07	**Fri 12/28/07**
Mon 7/2/07	Fri 12/28/07
Mon 1/7/08	Mon 1/7/08

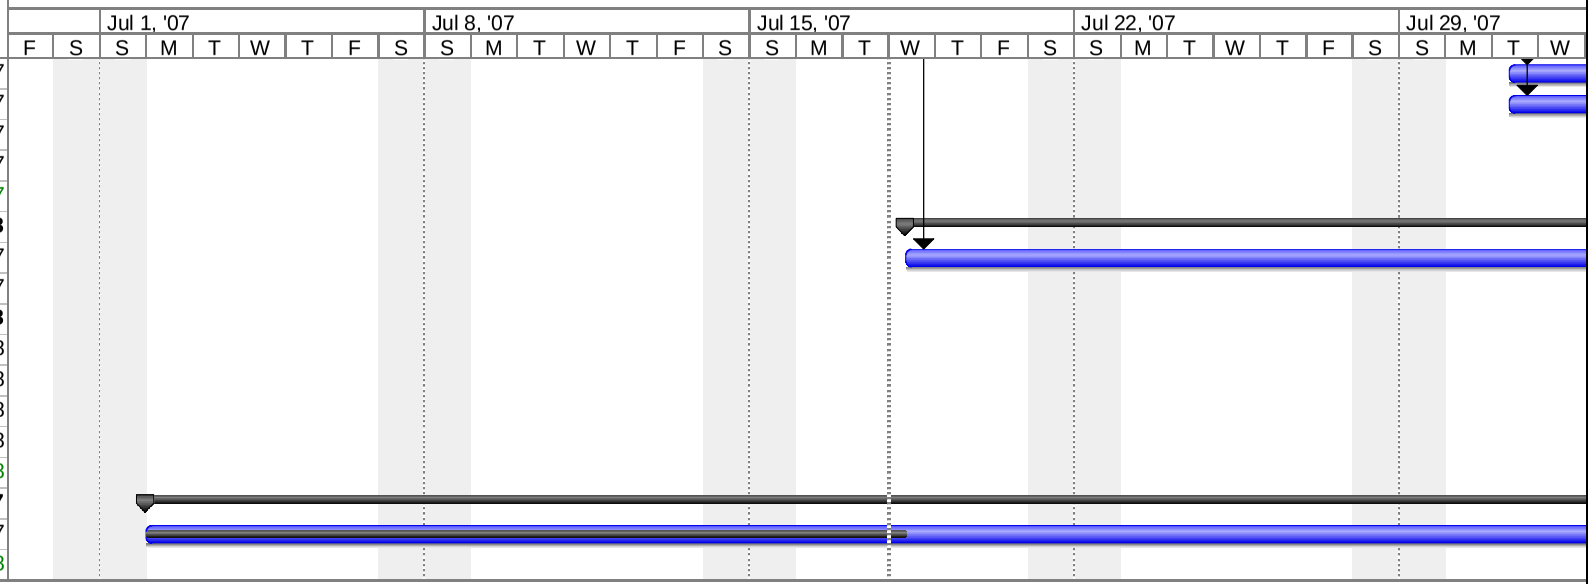

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

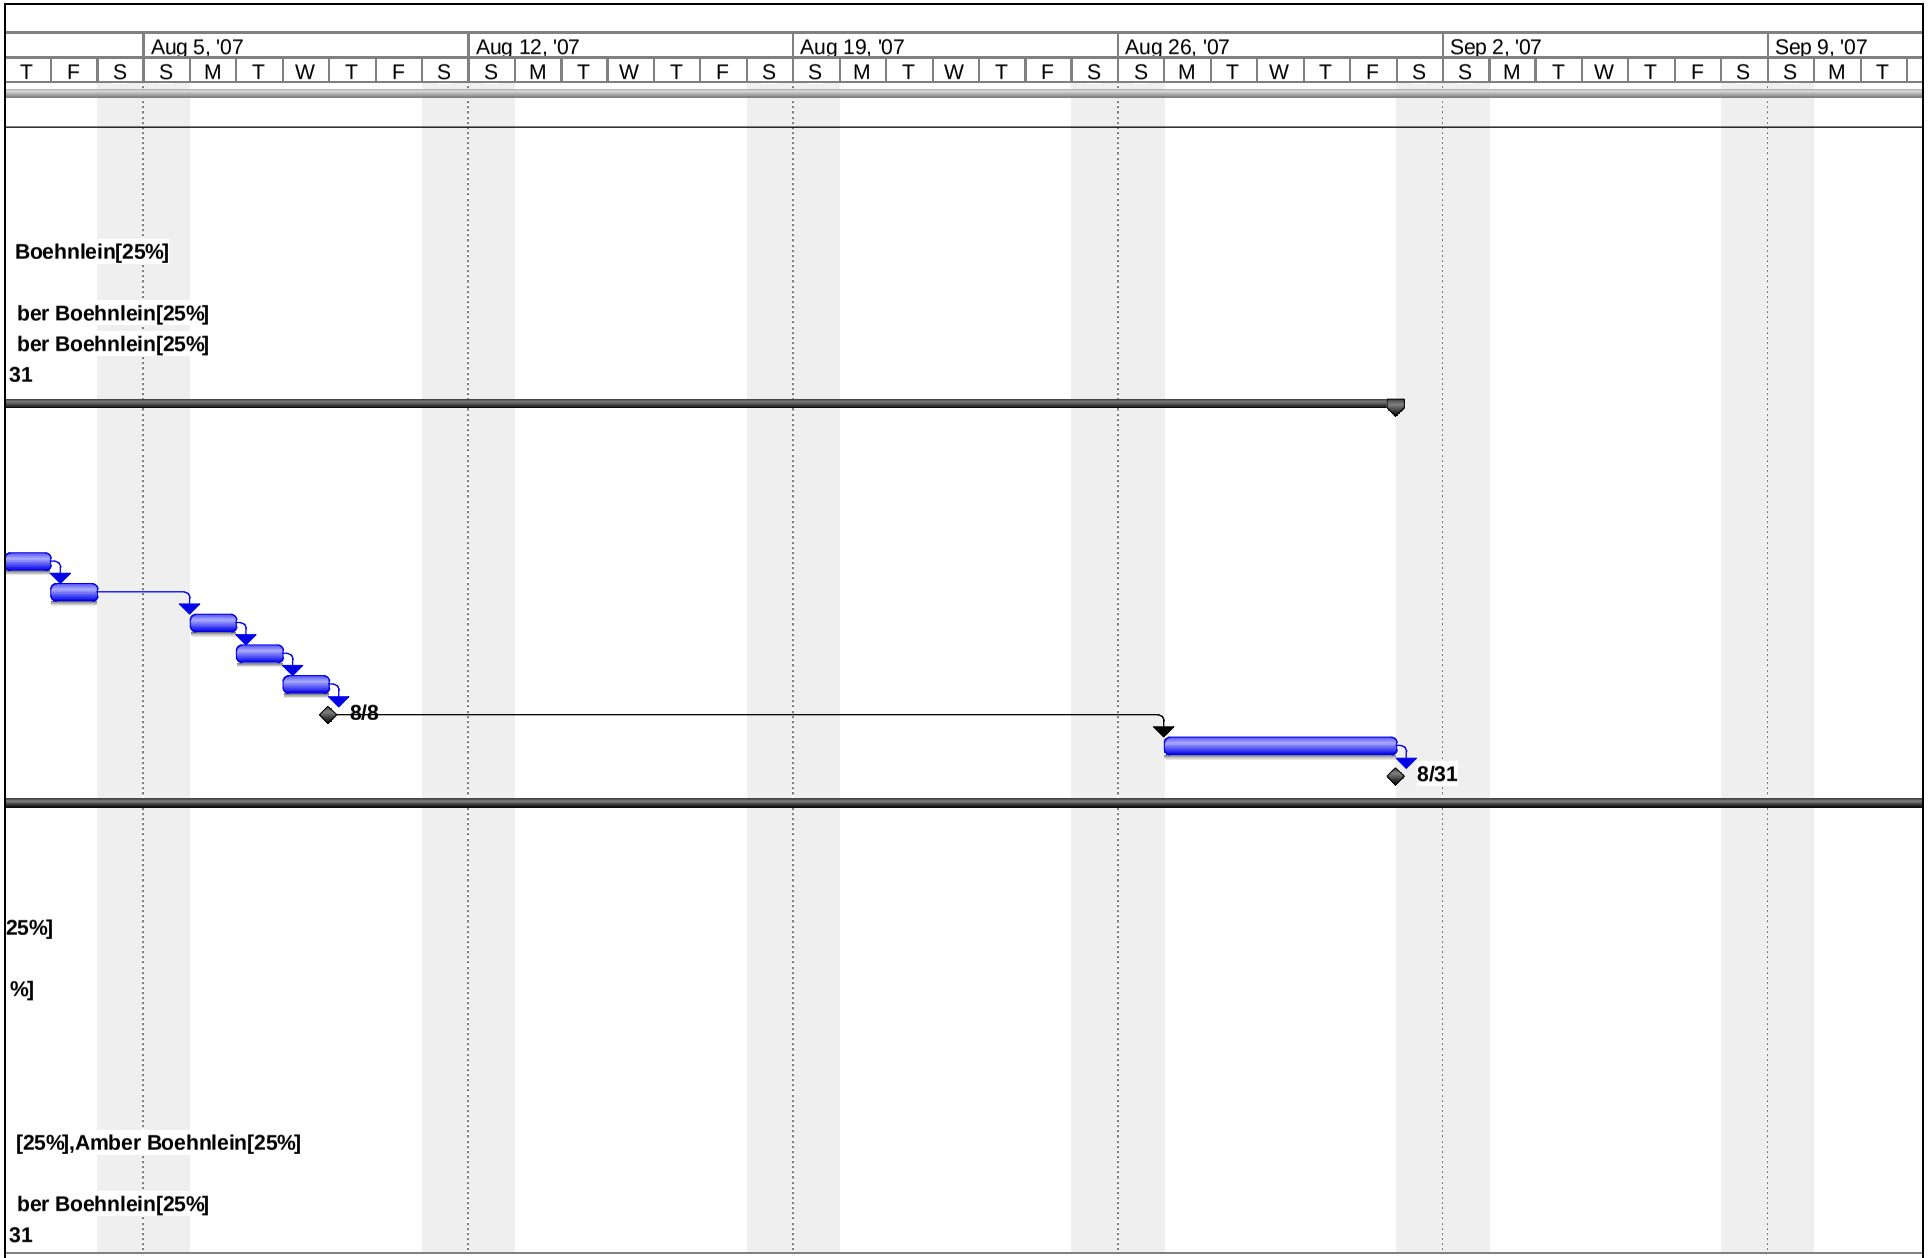

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

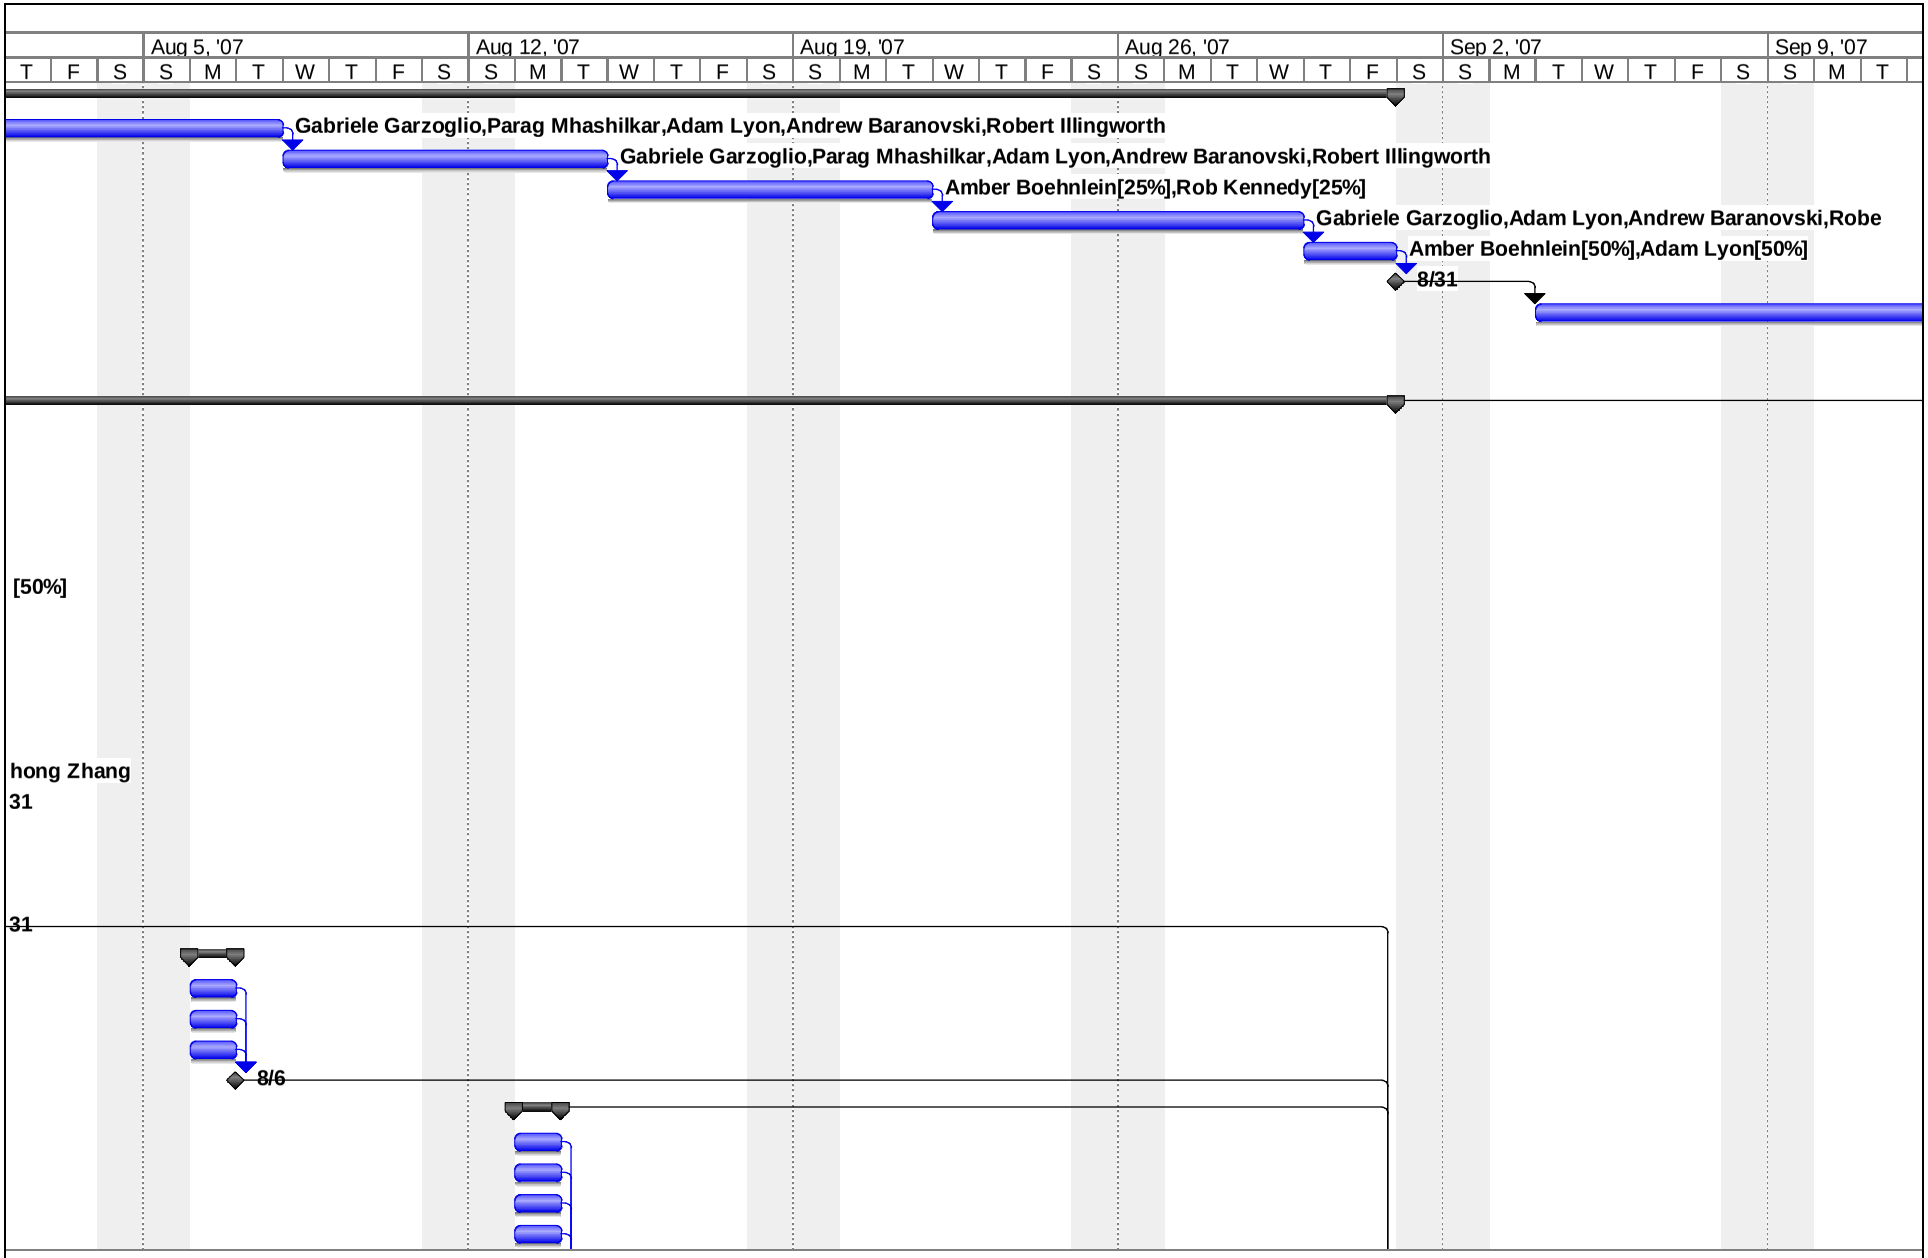

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

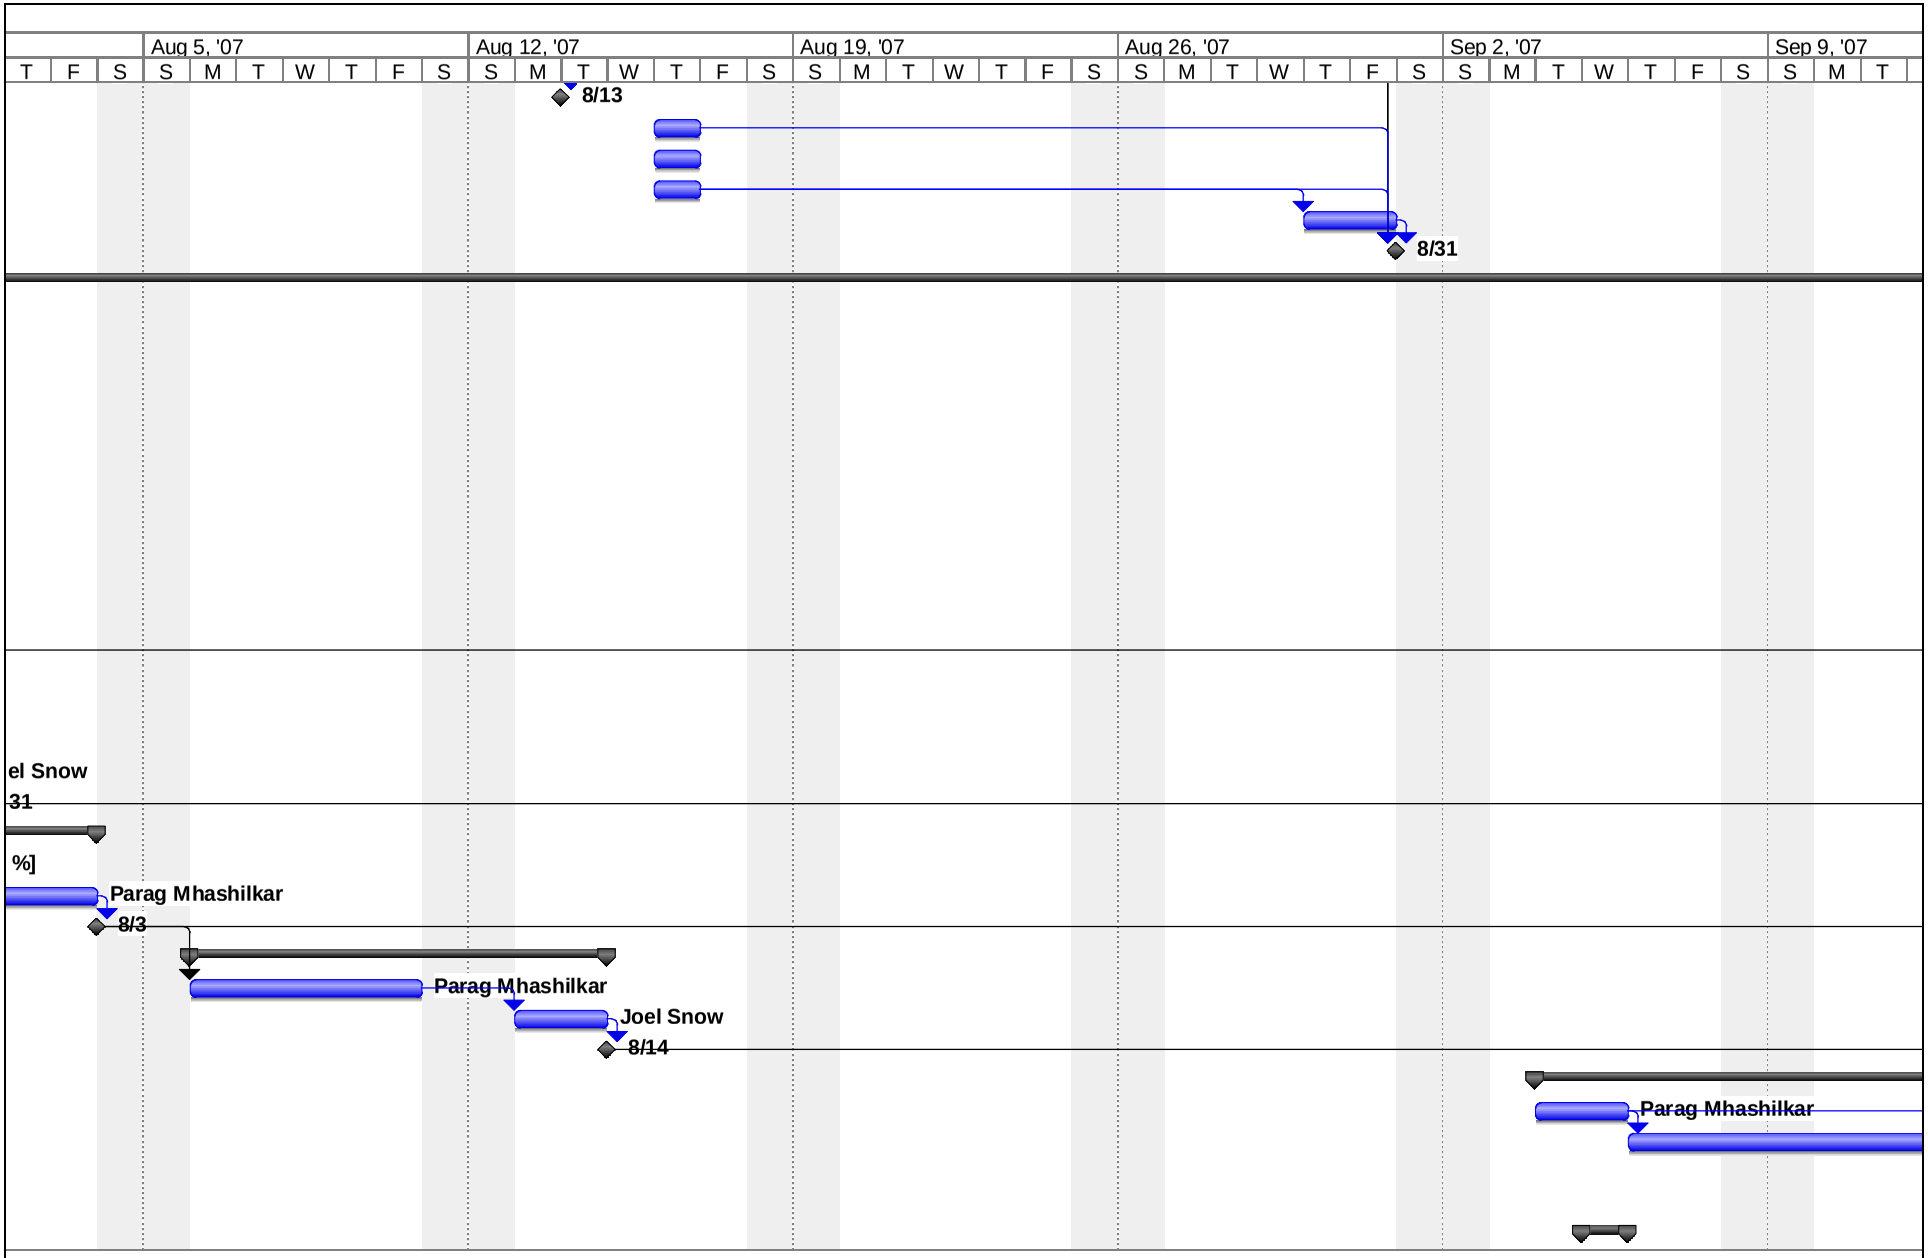

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

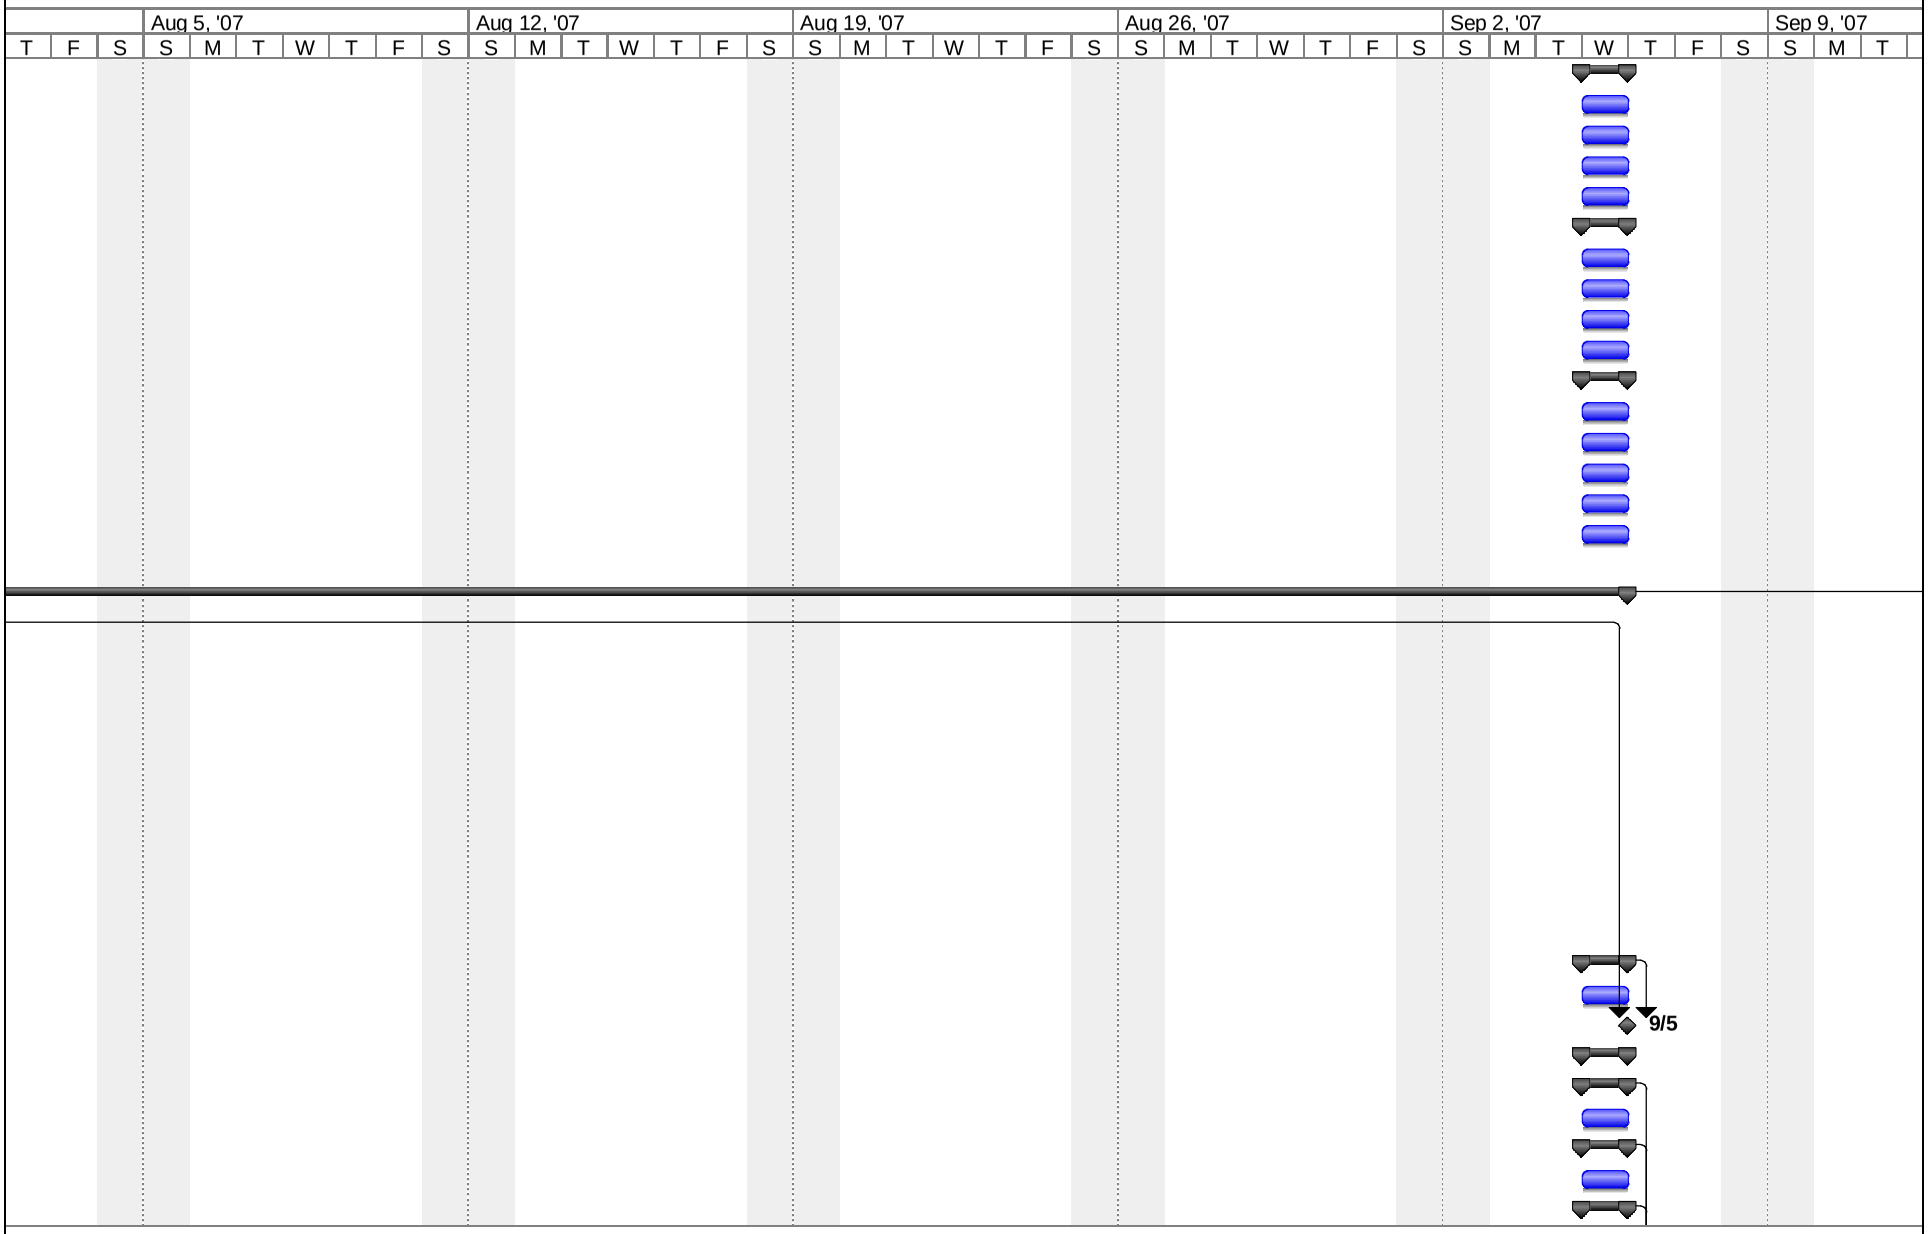

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

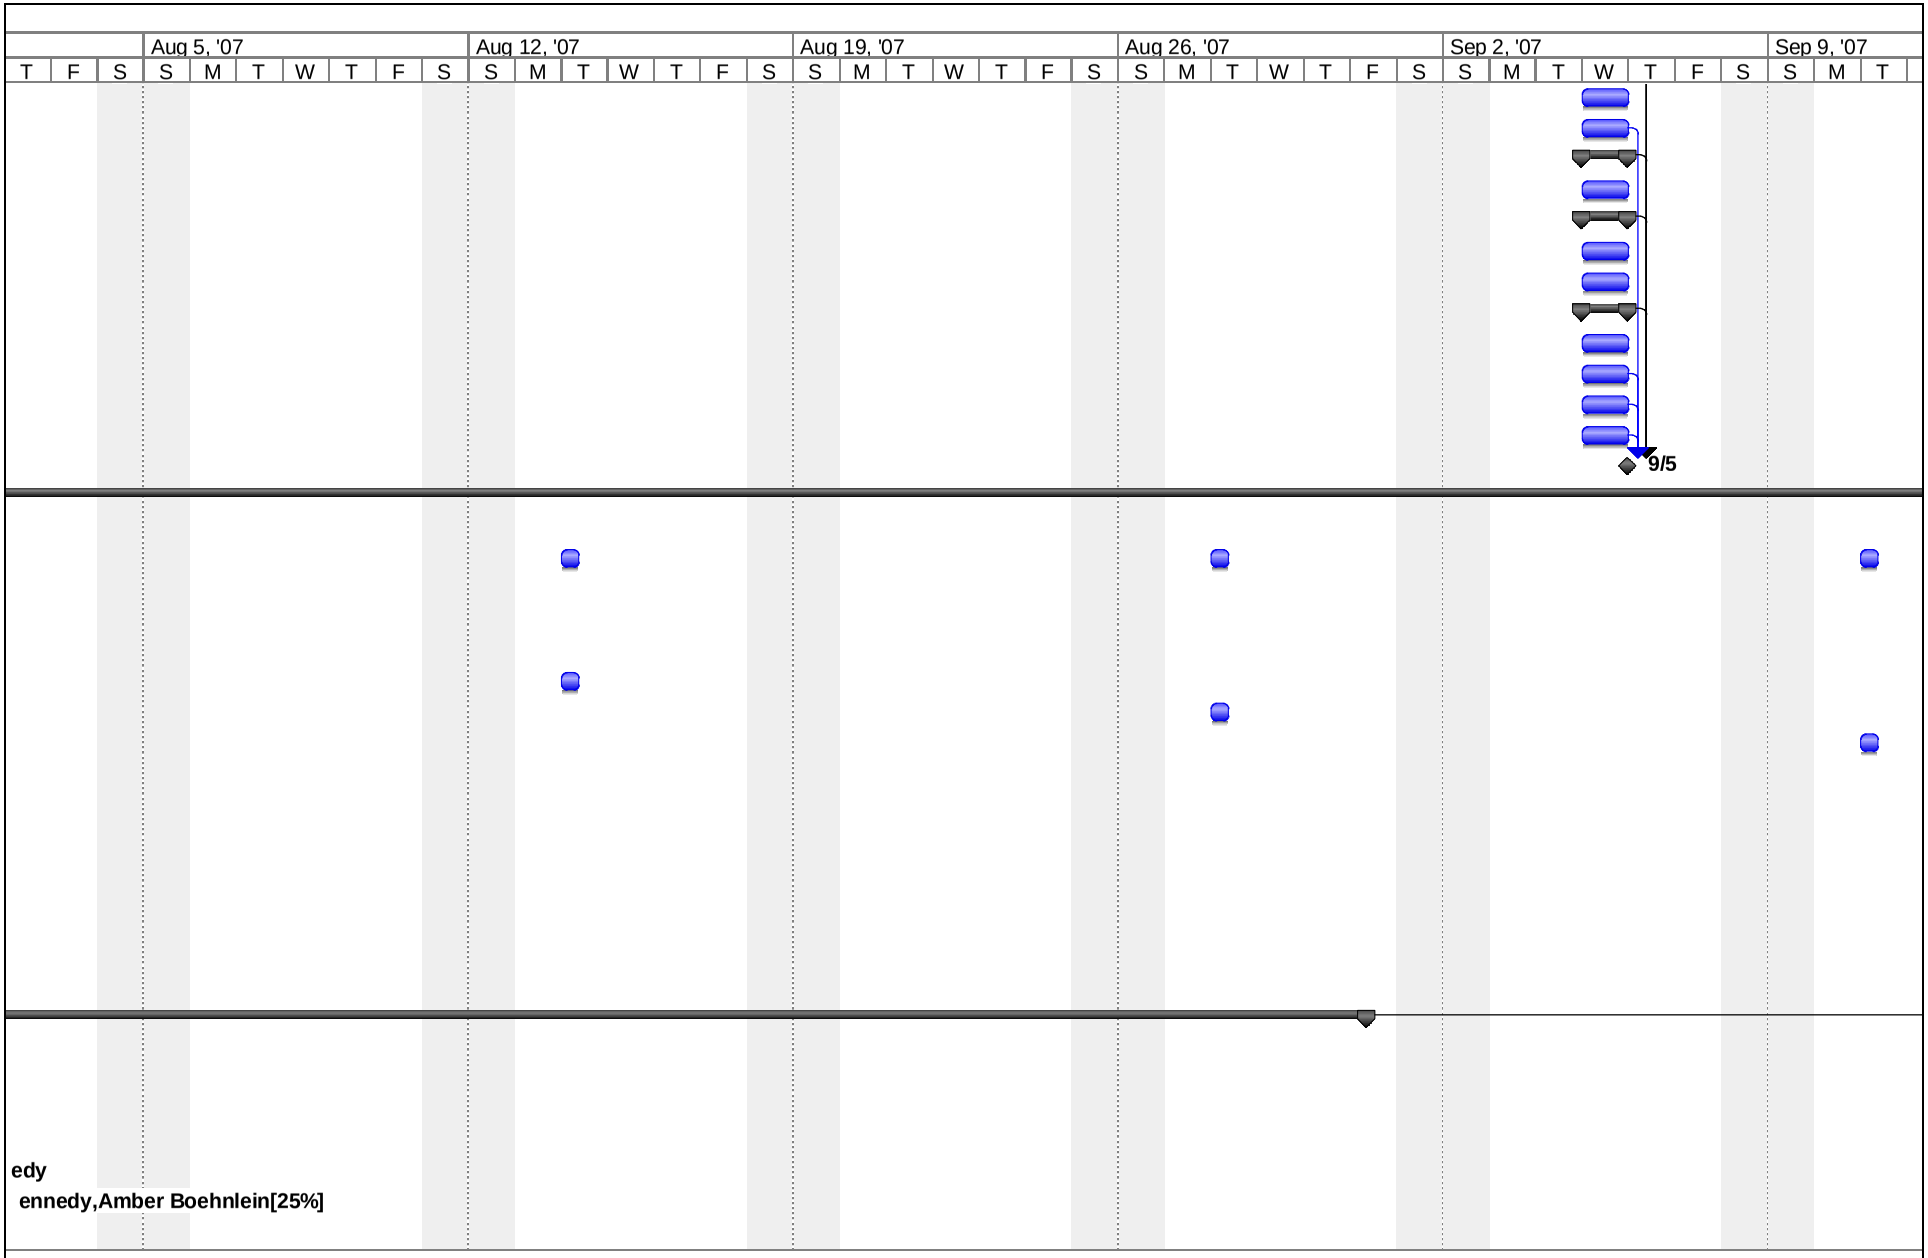

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

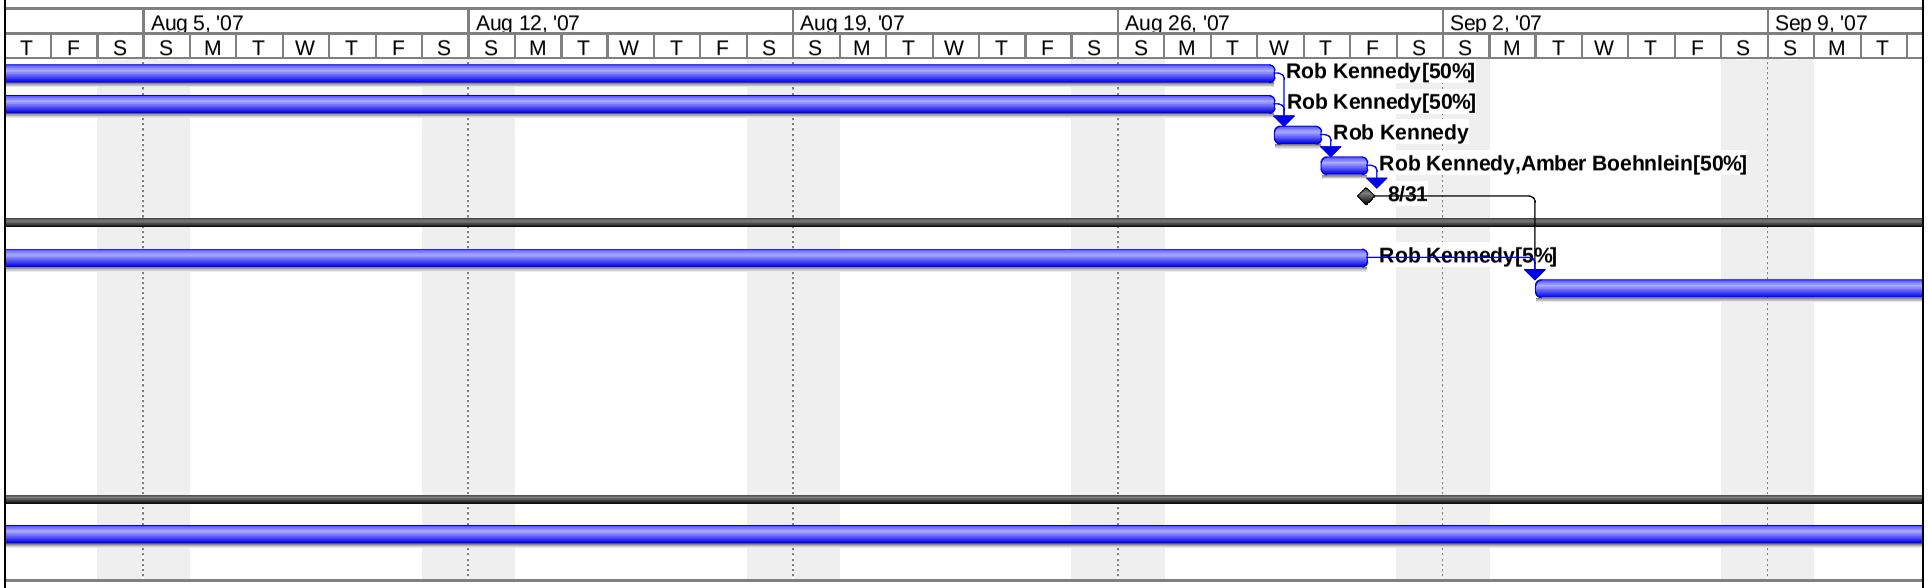

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

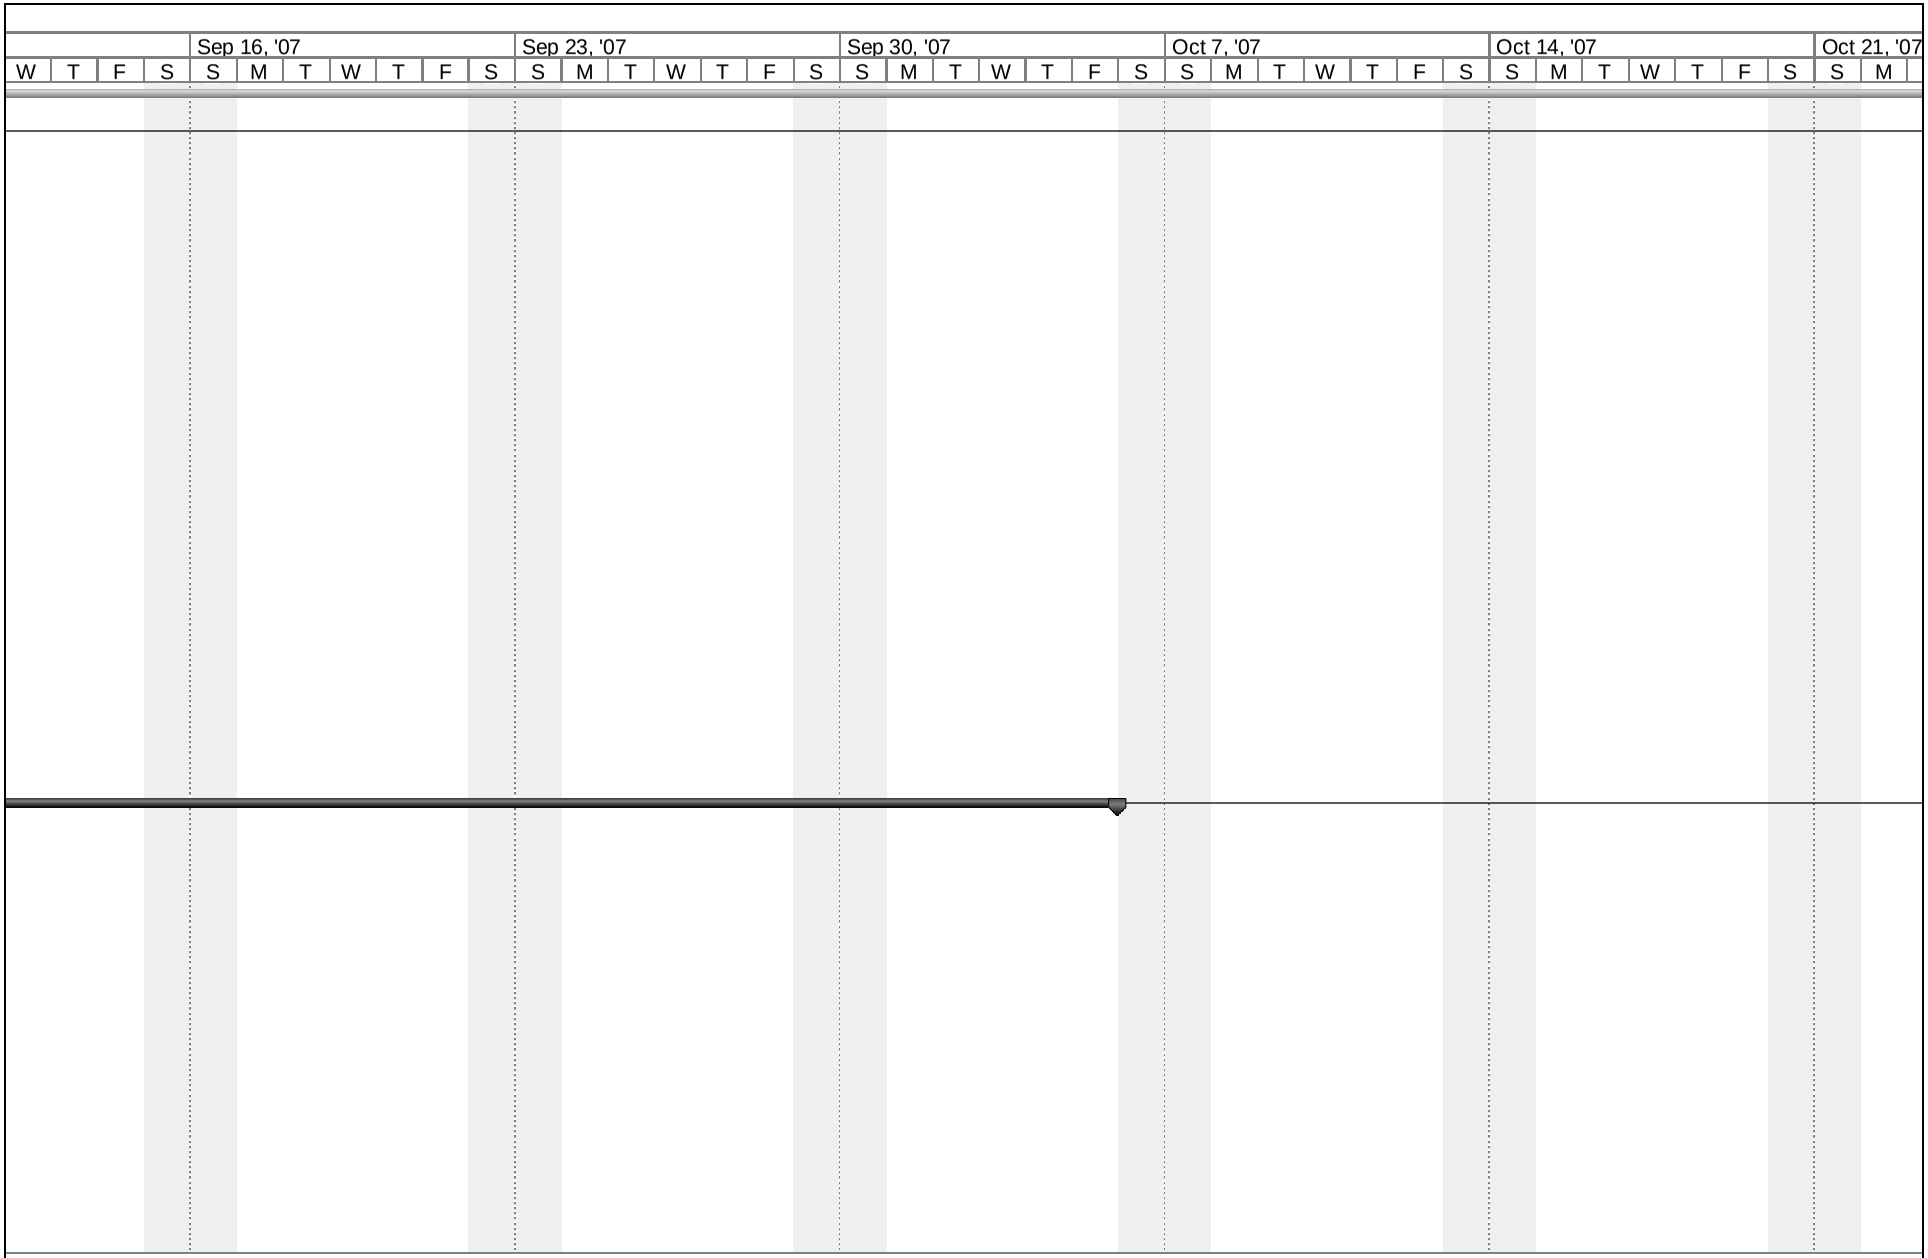

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

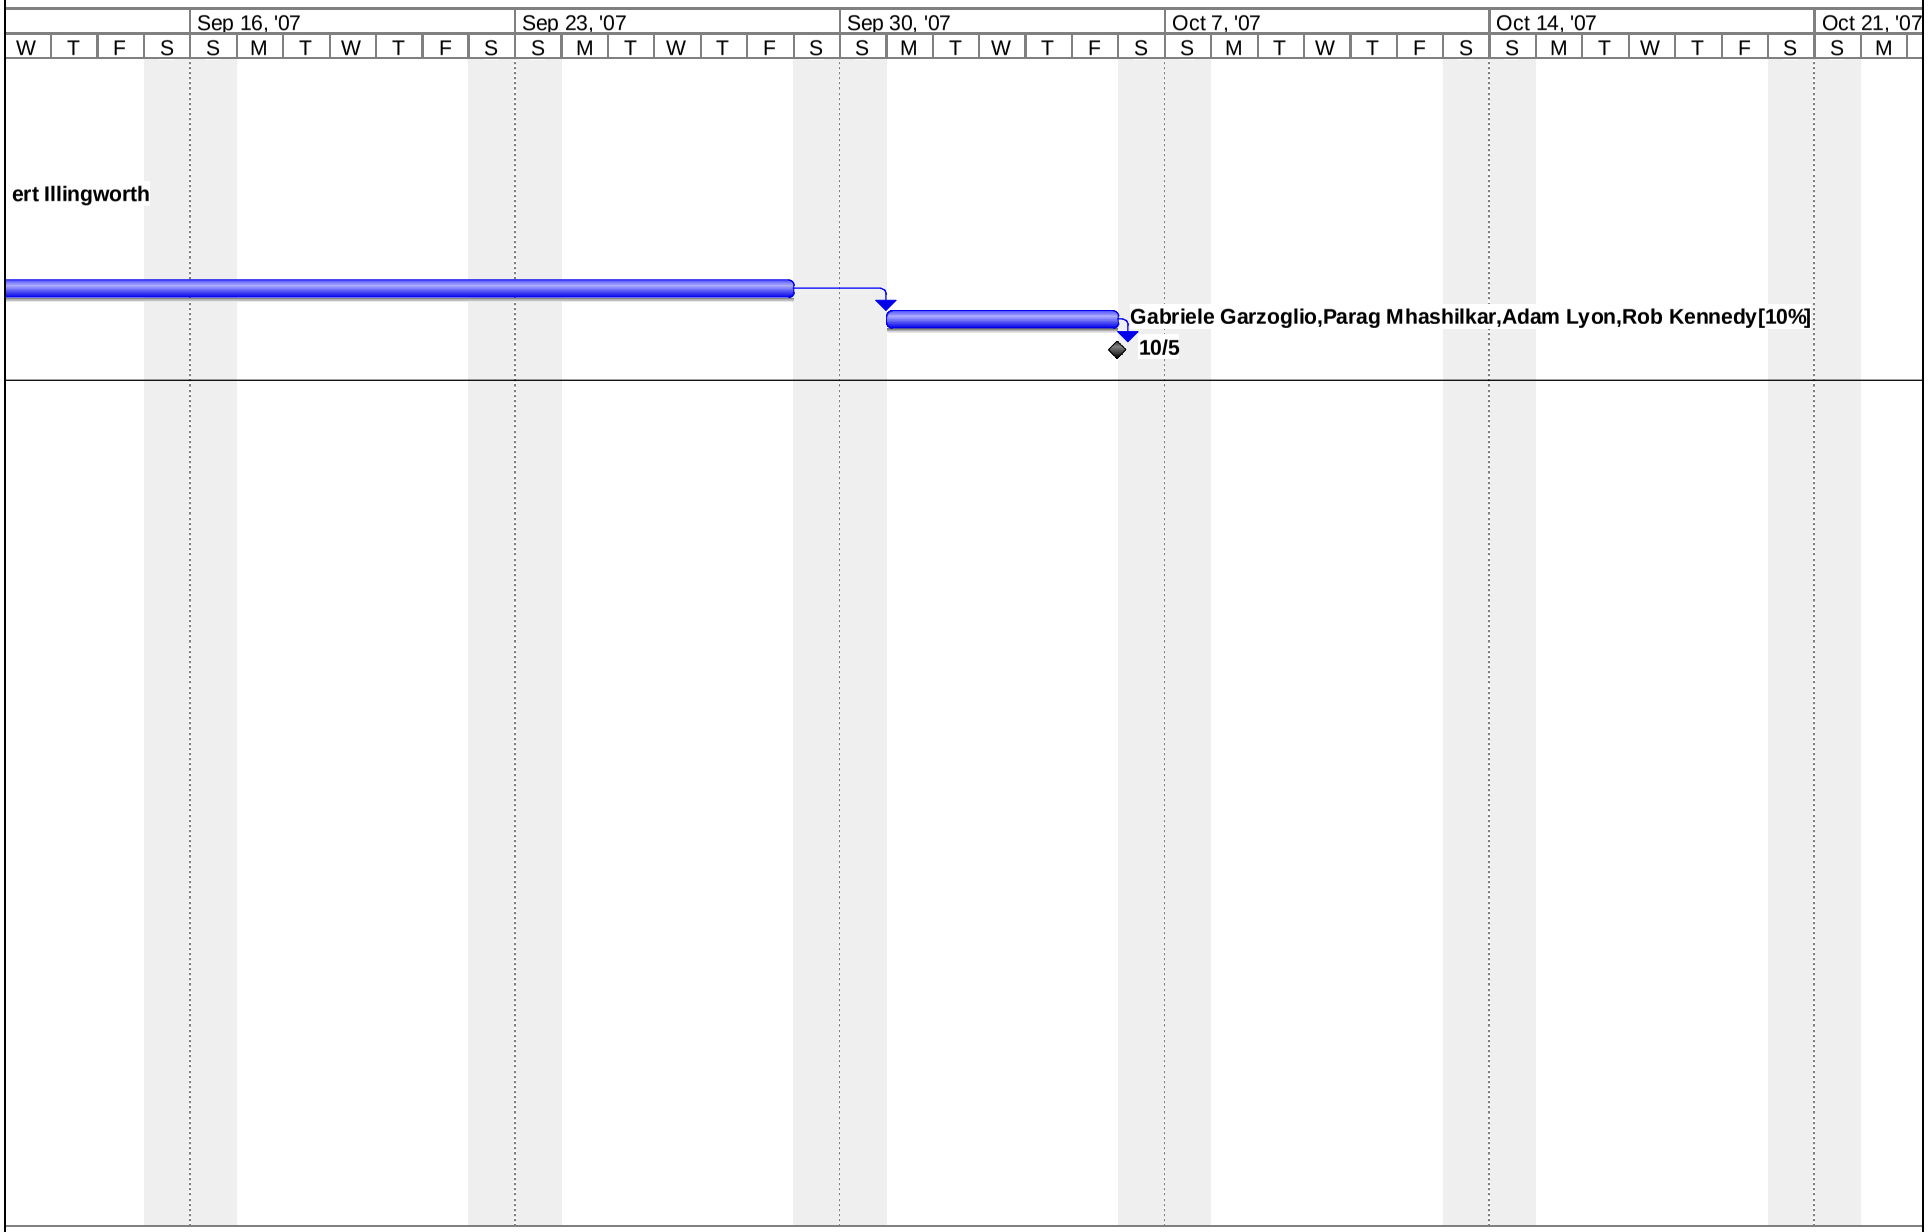

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

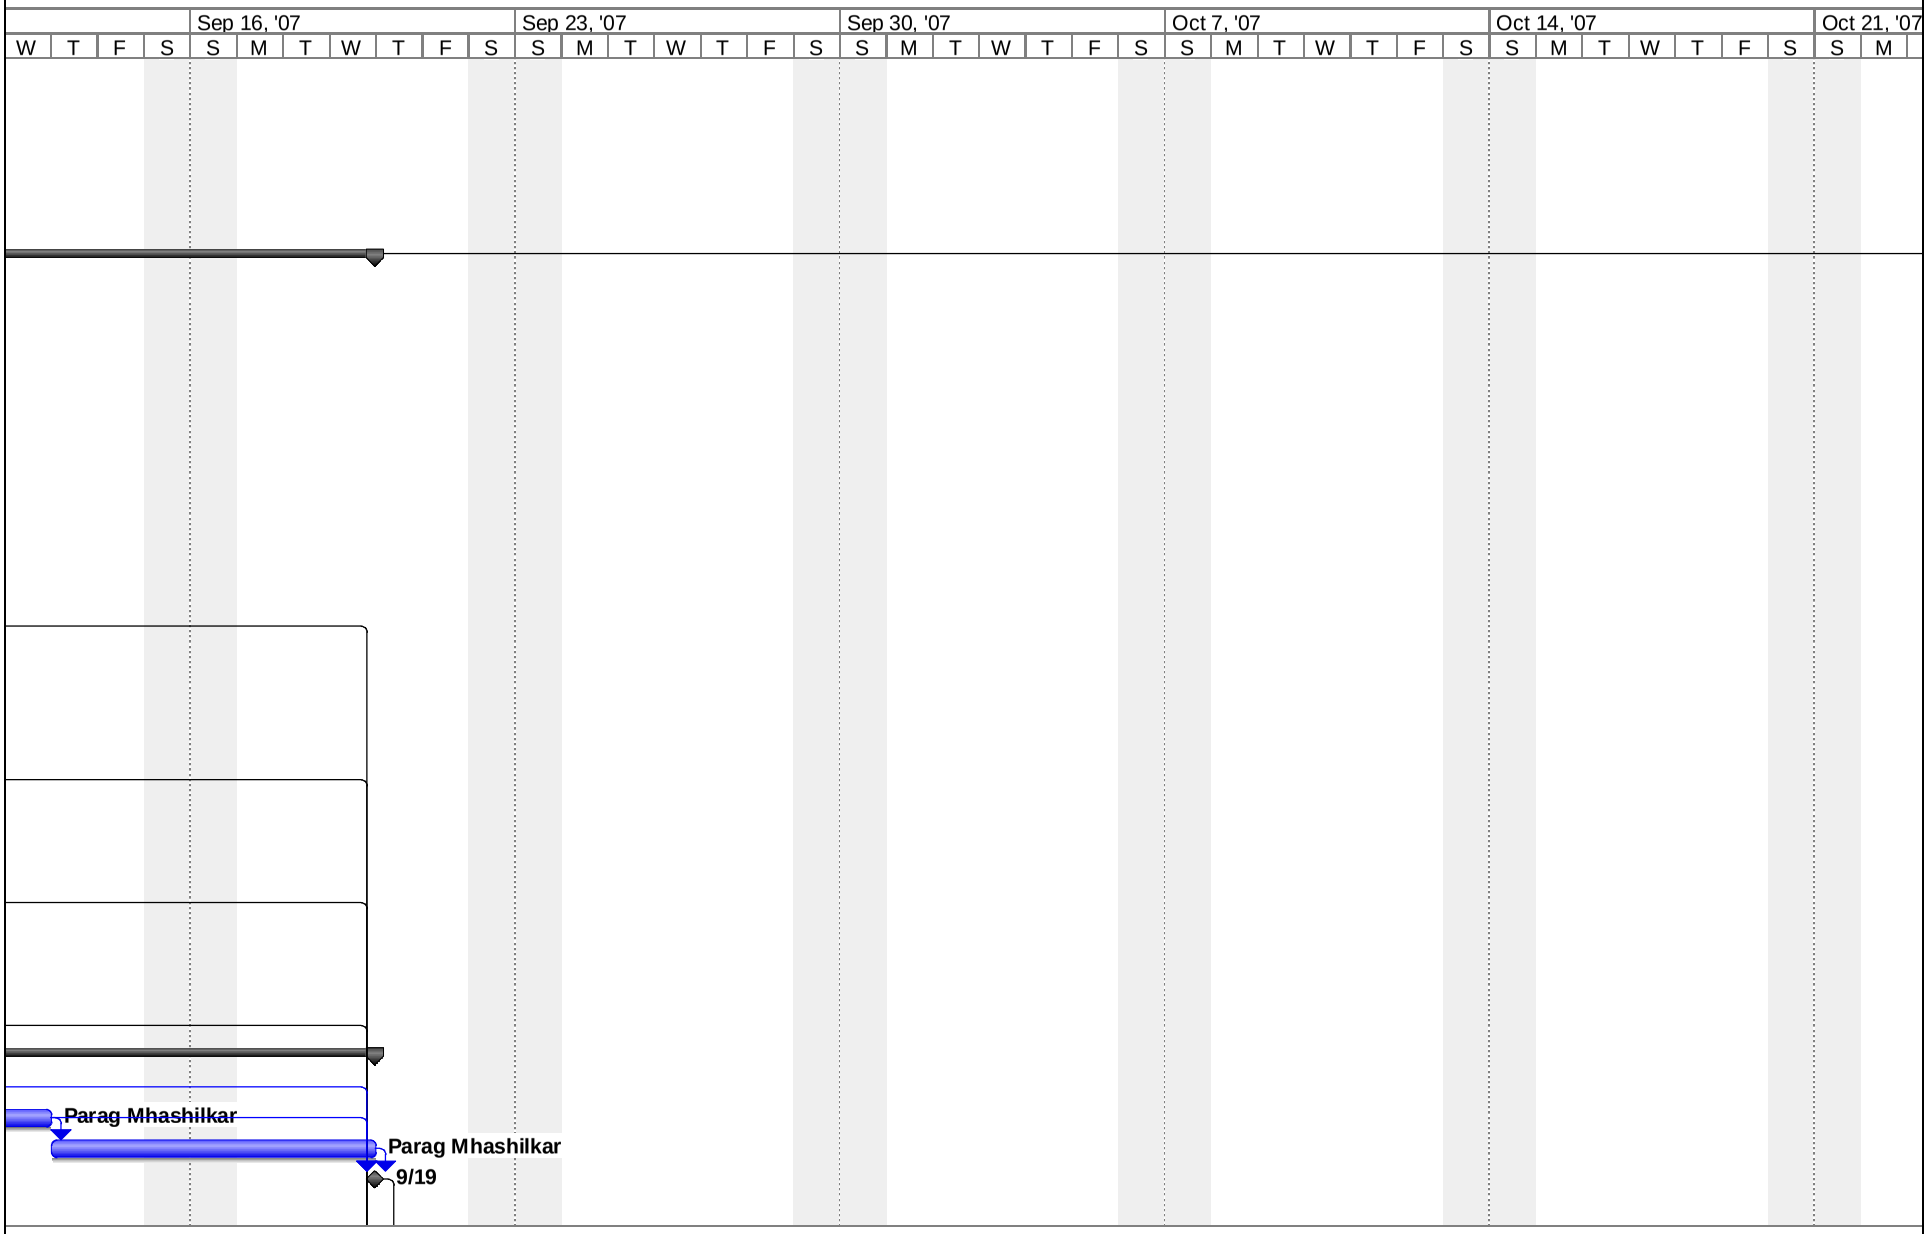

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

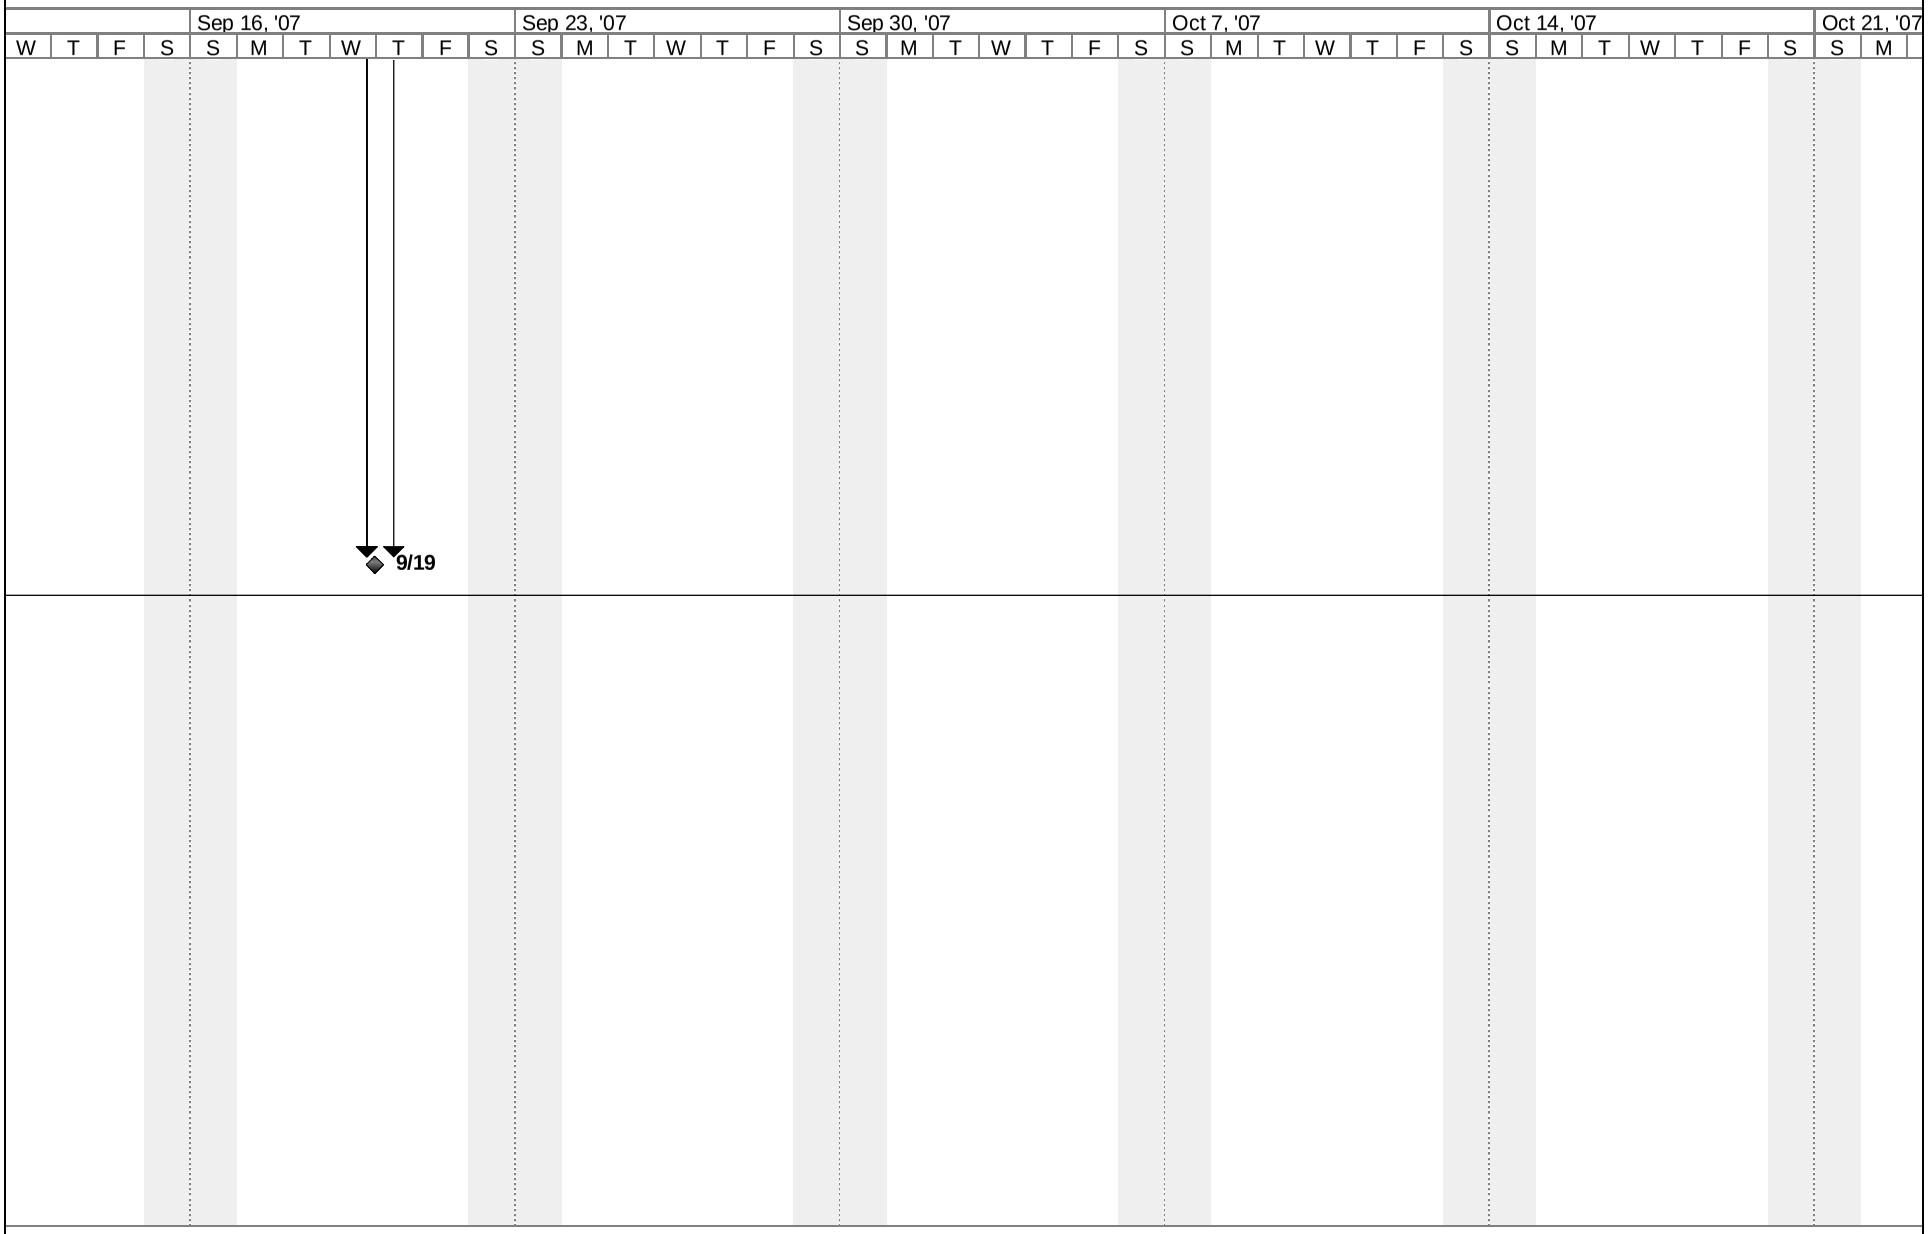

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

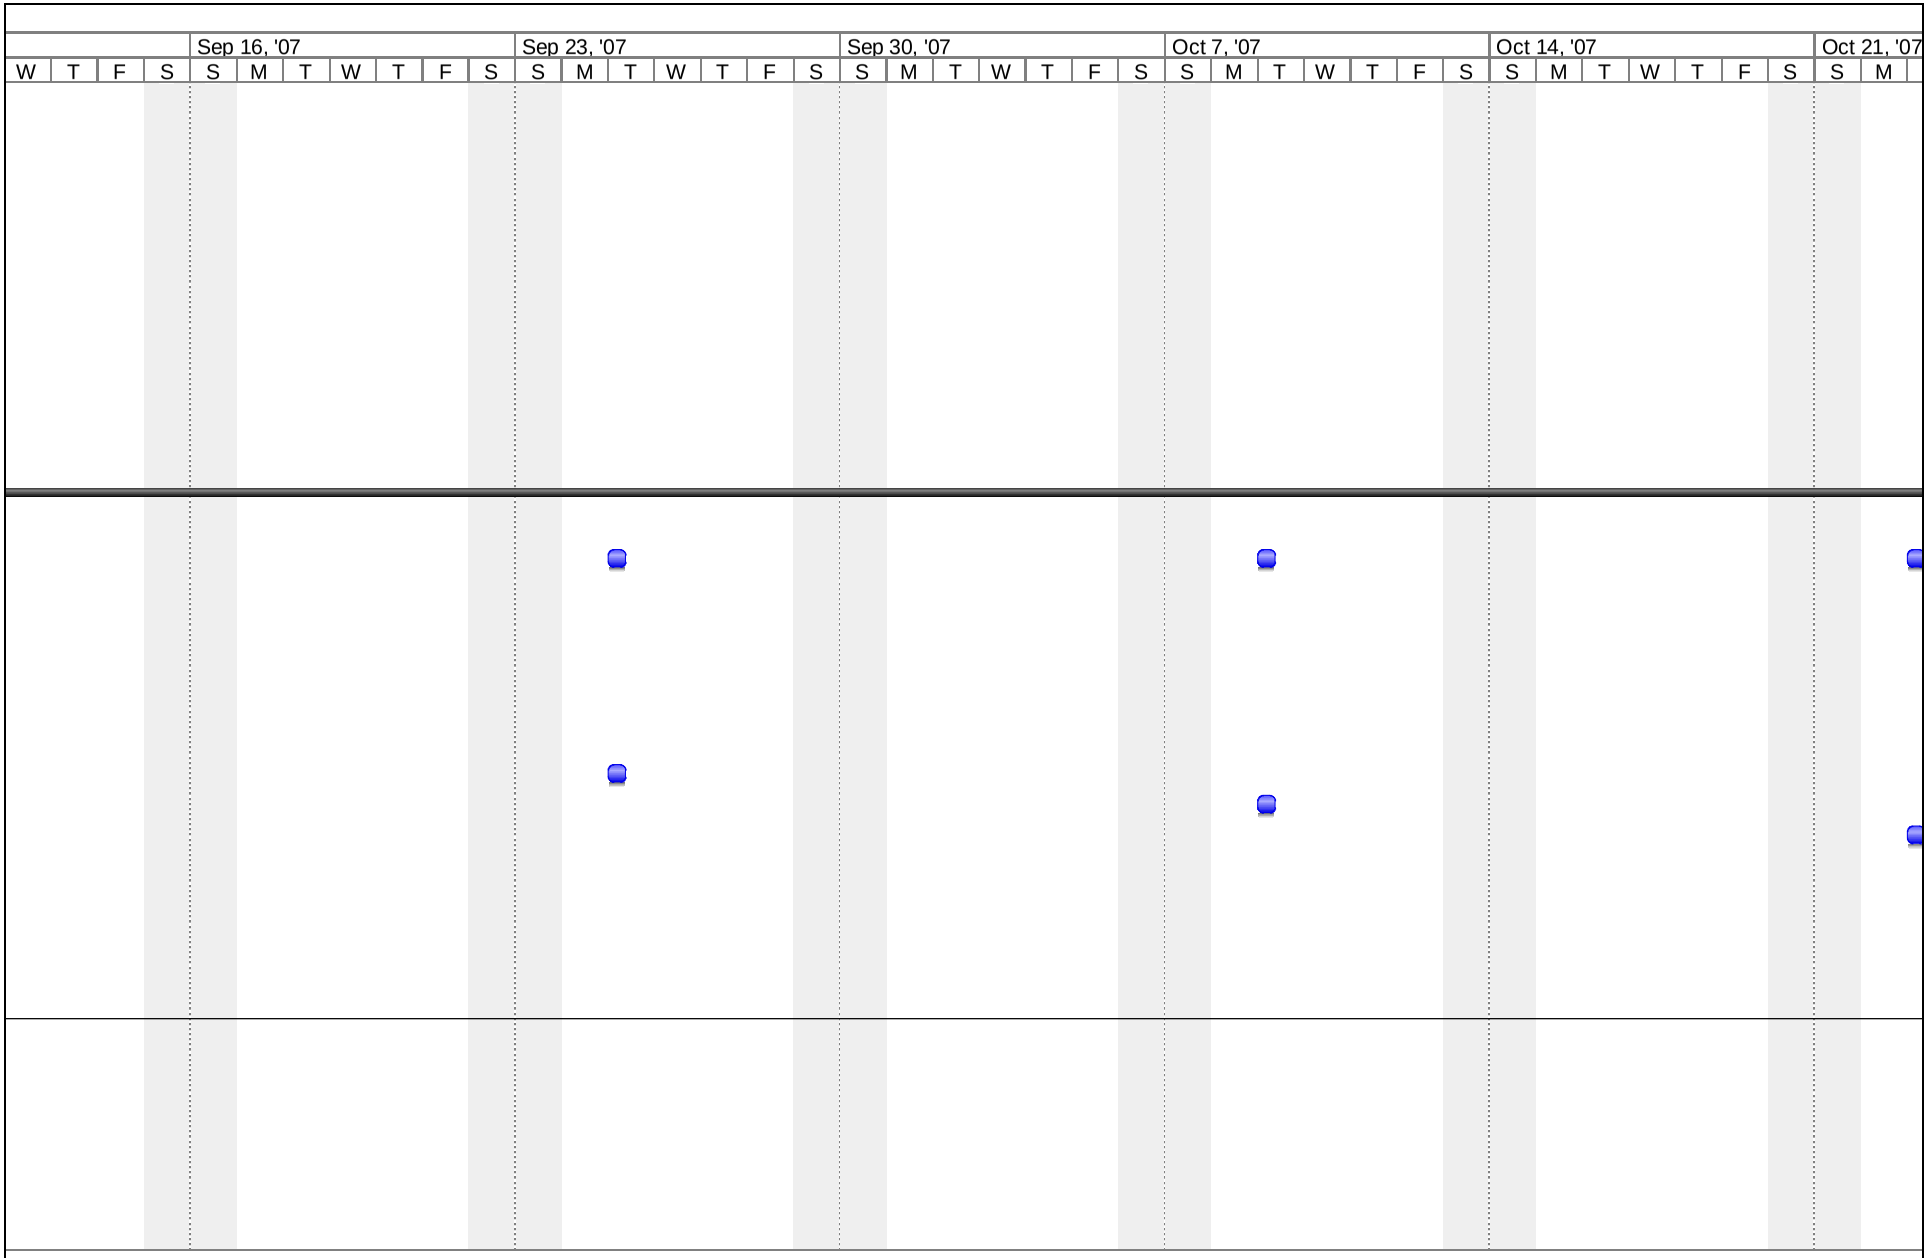

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

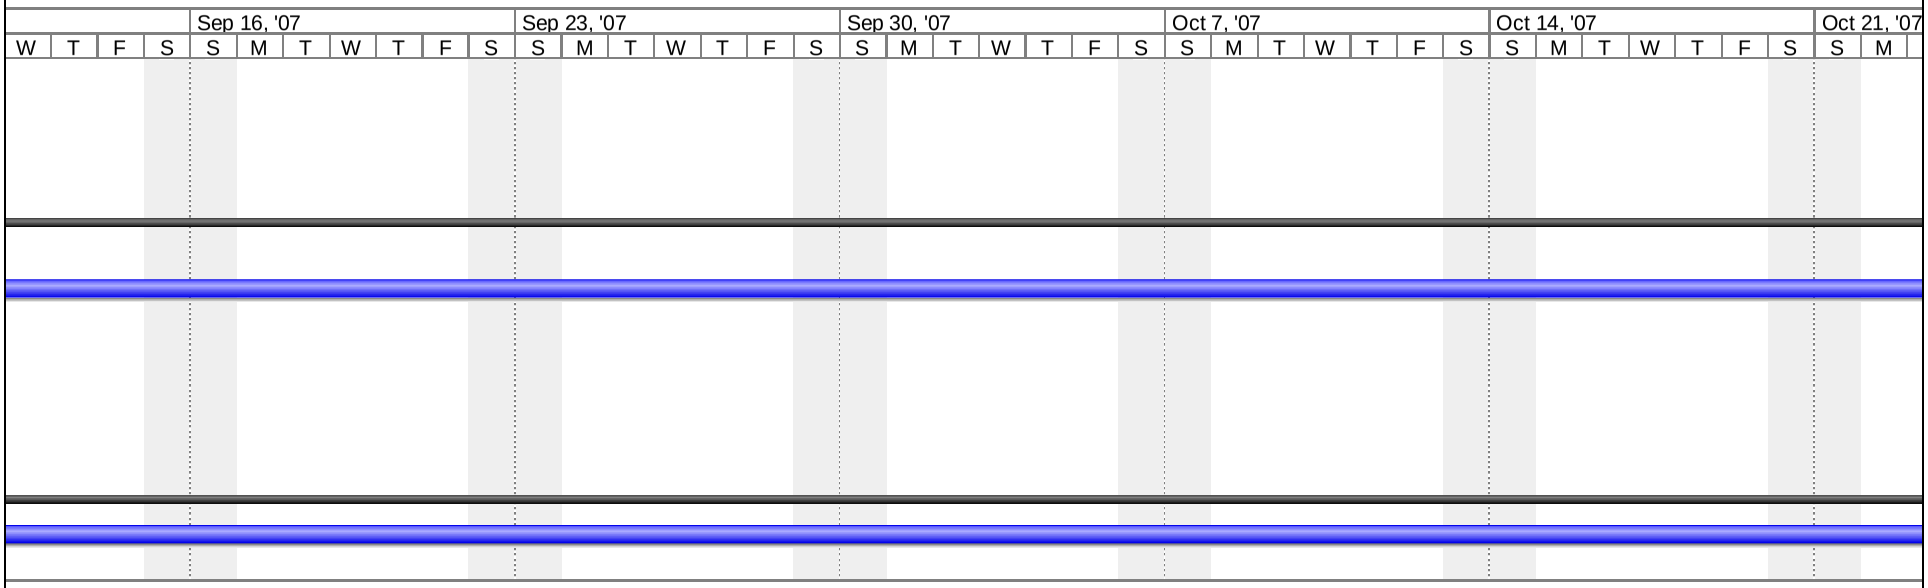

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

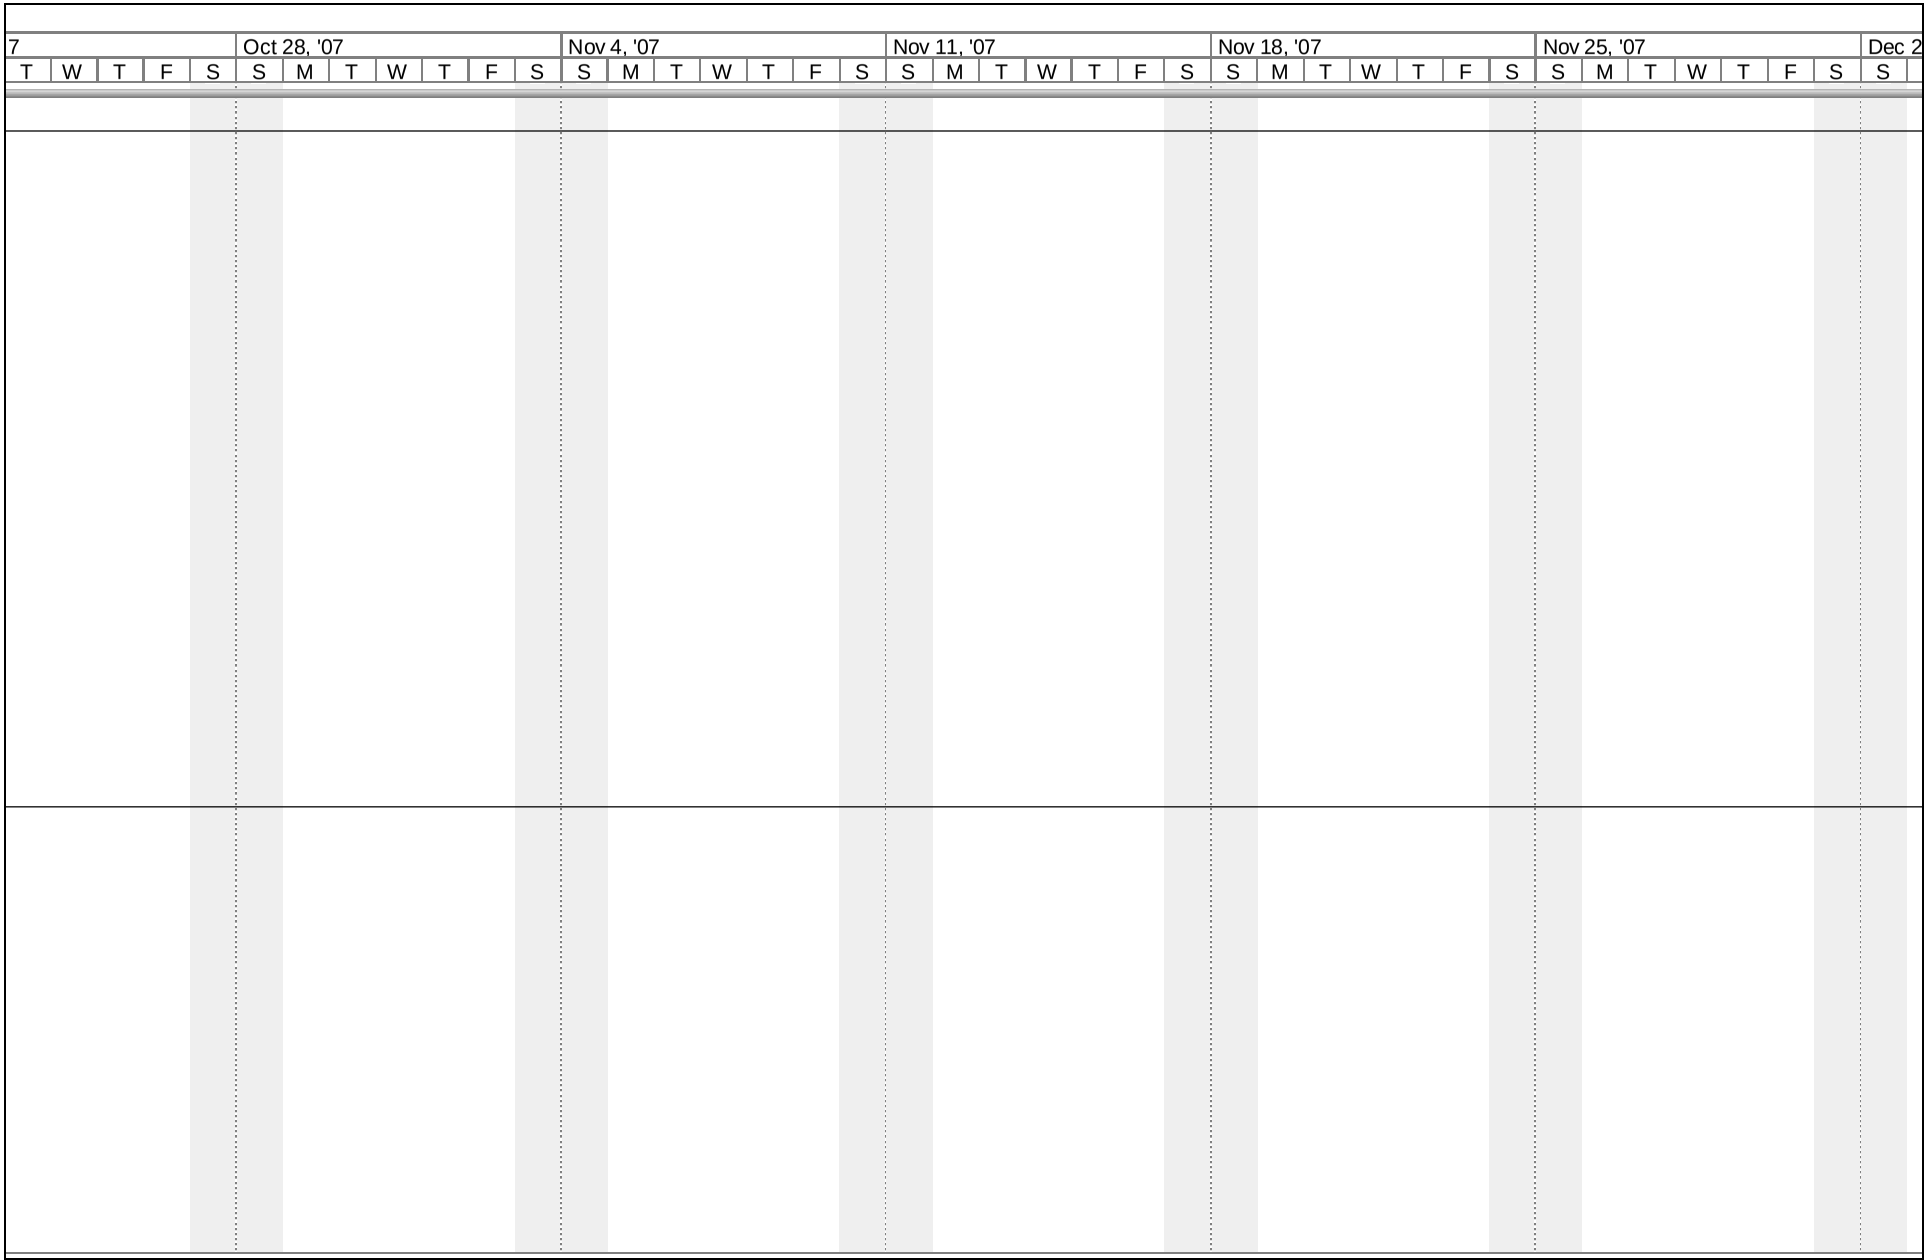

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

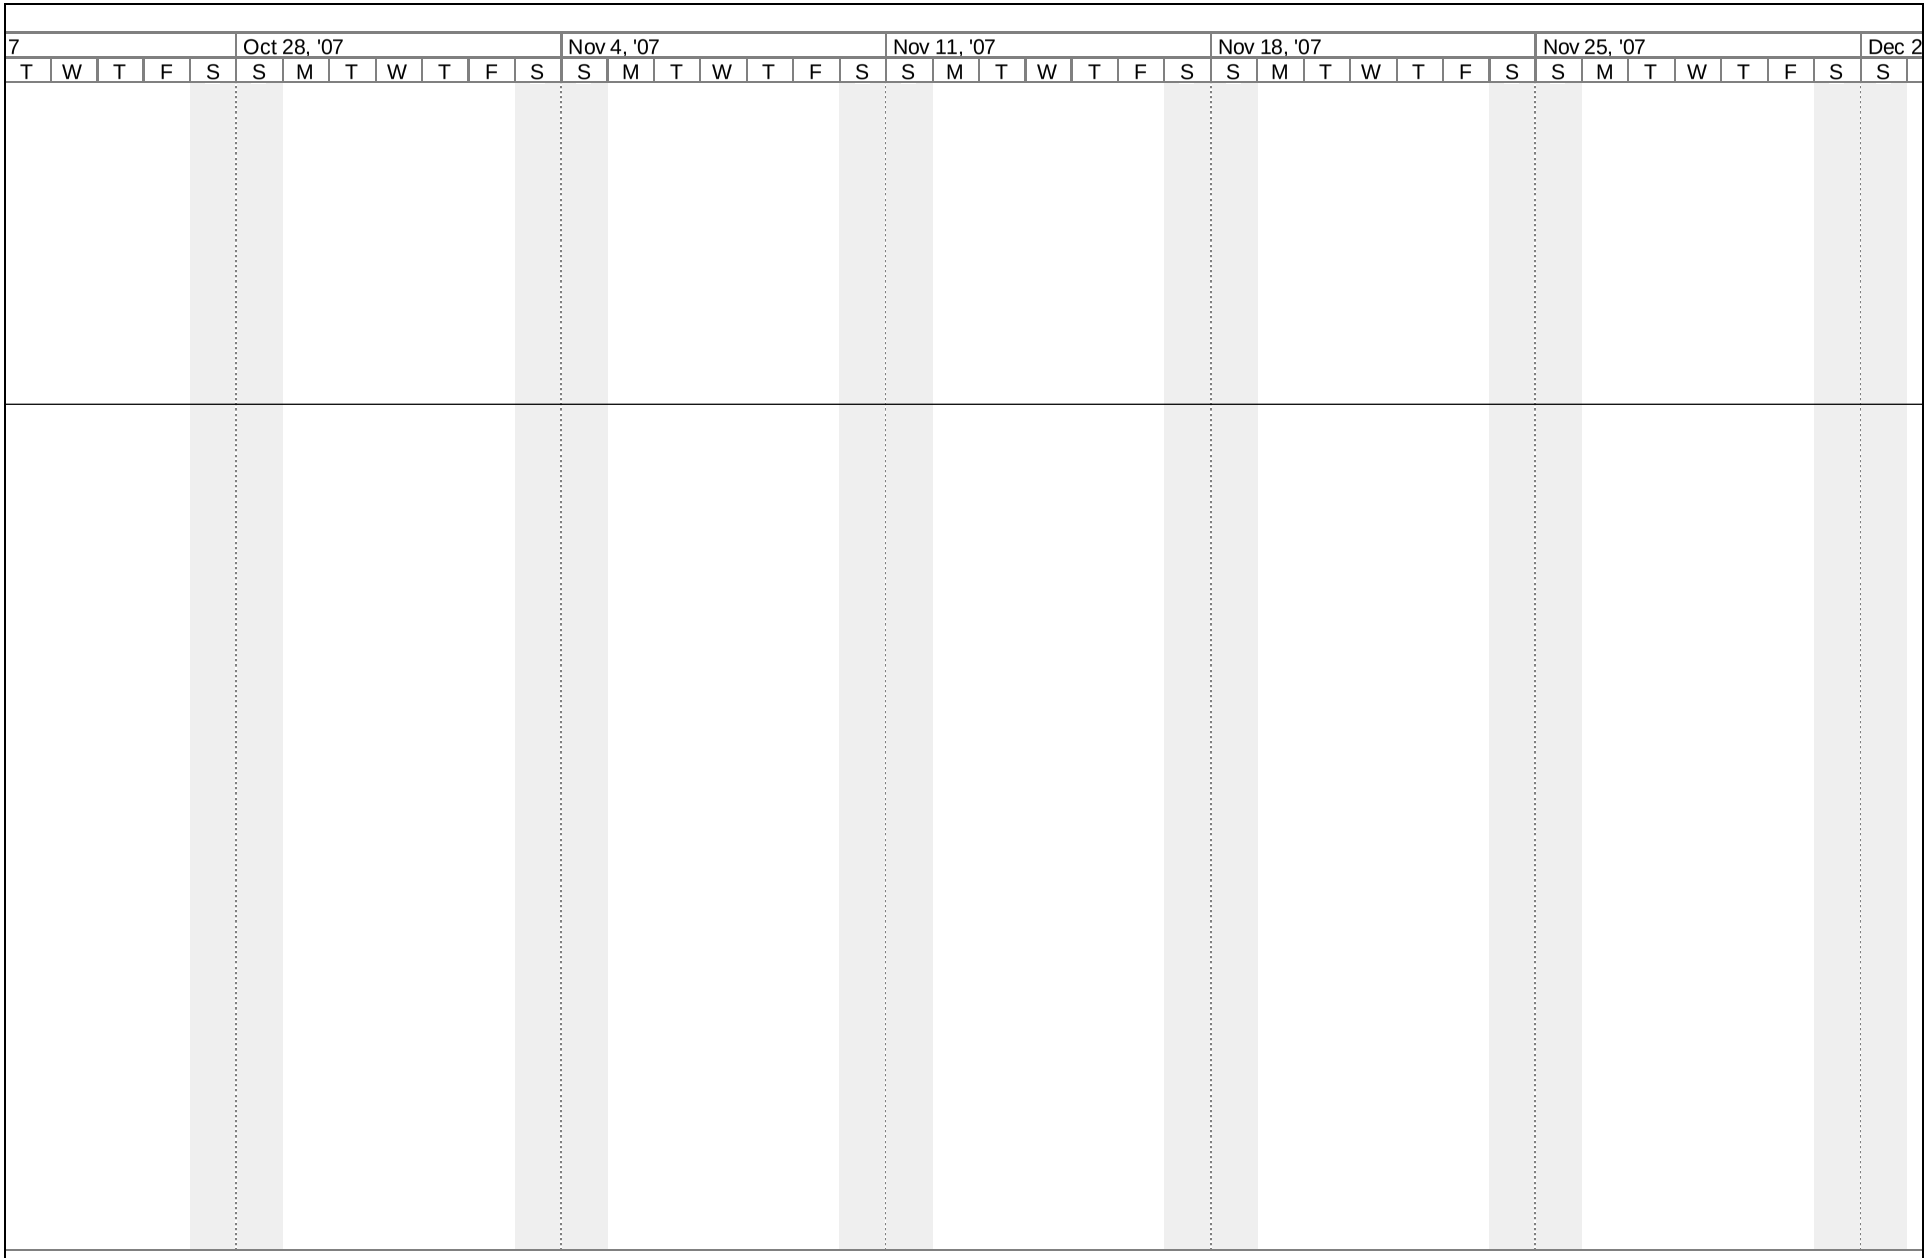

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

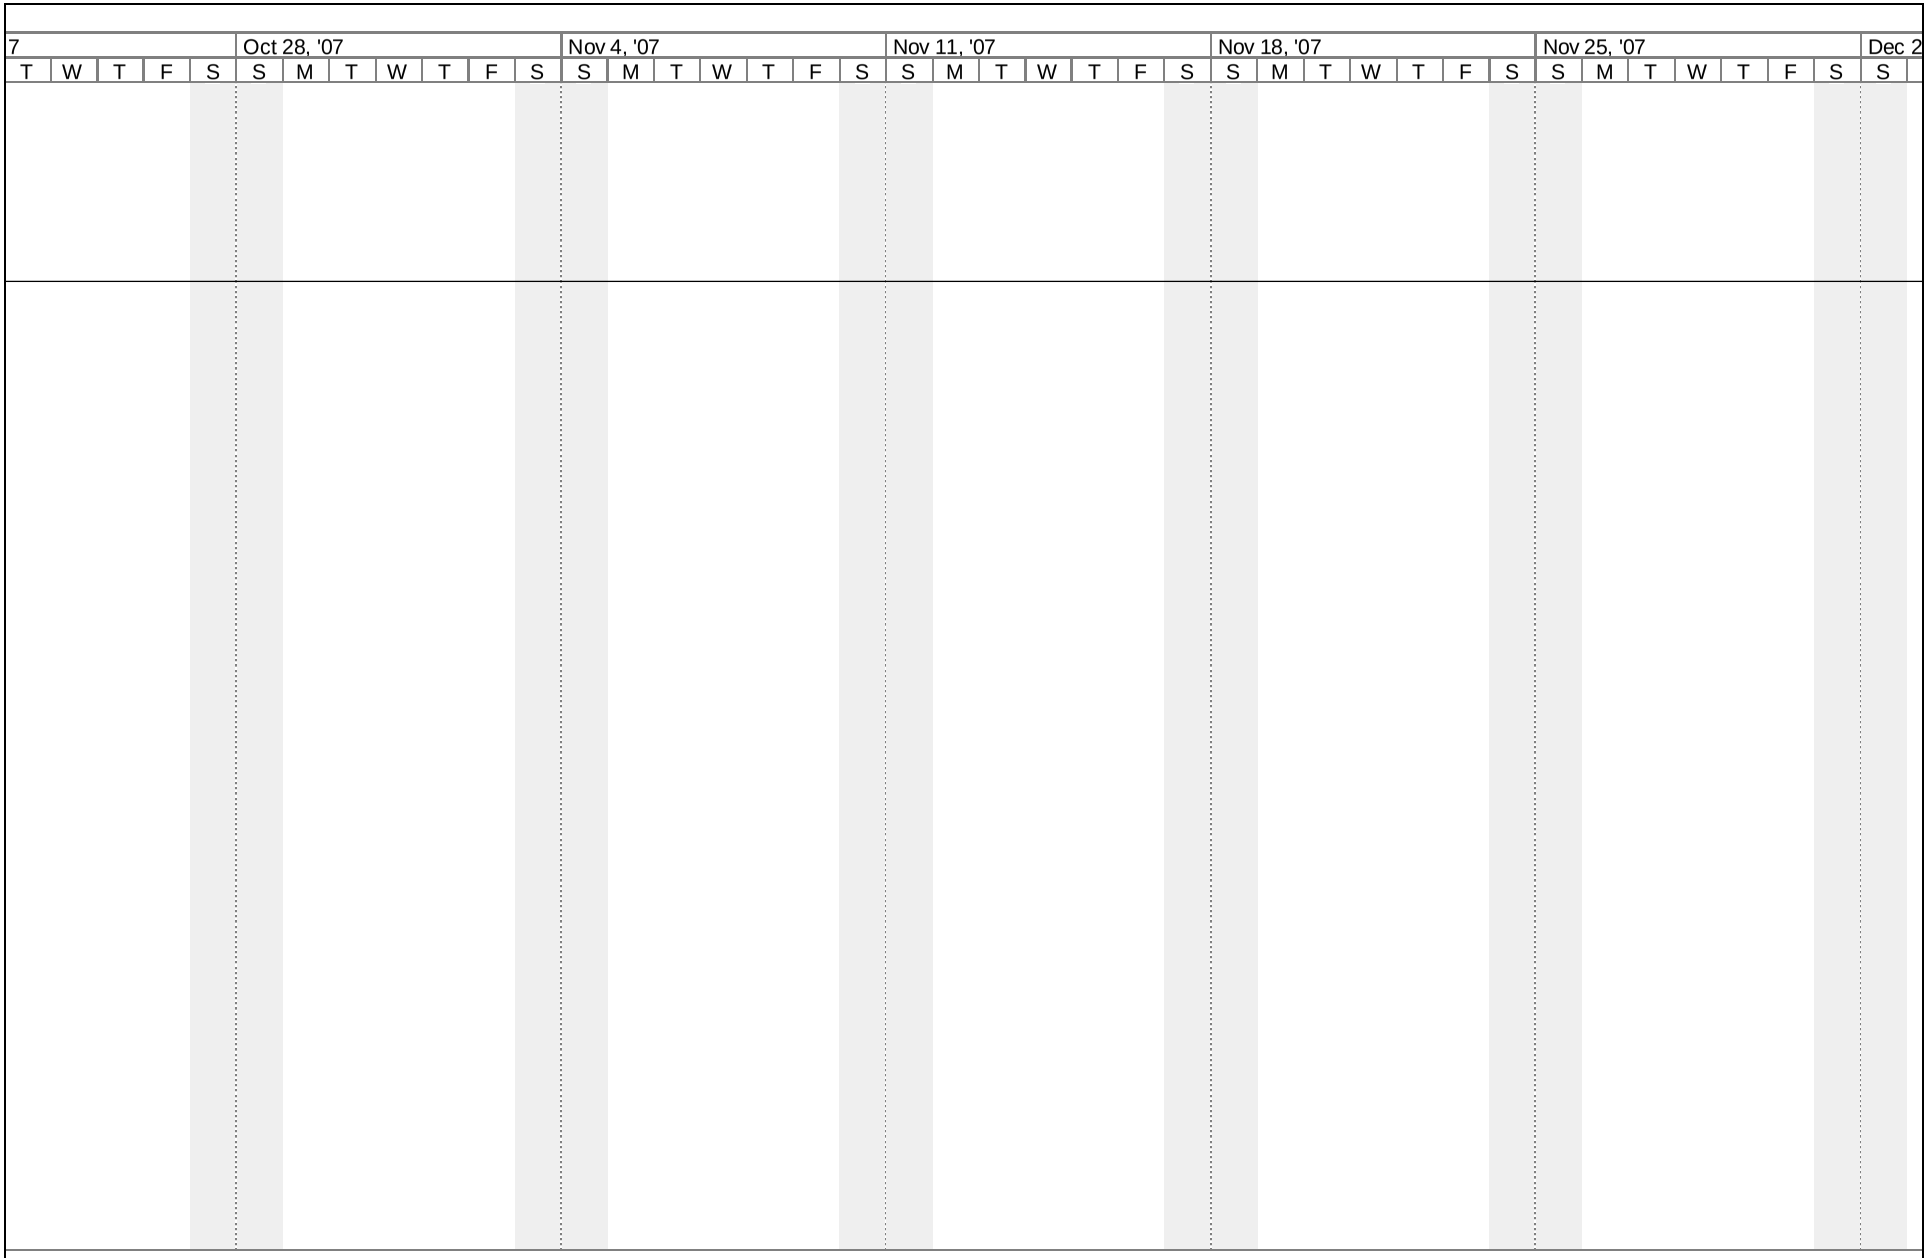

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

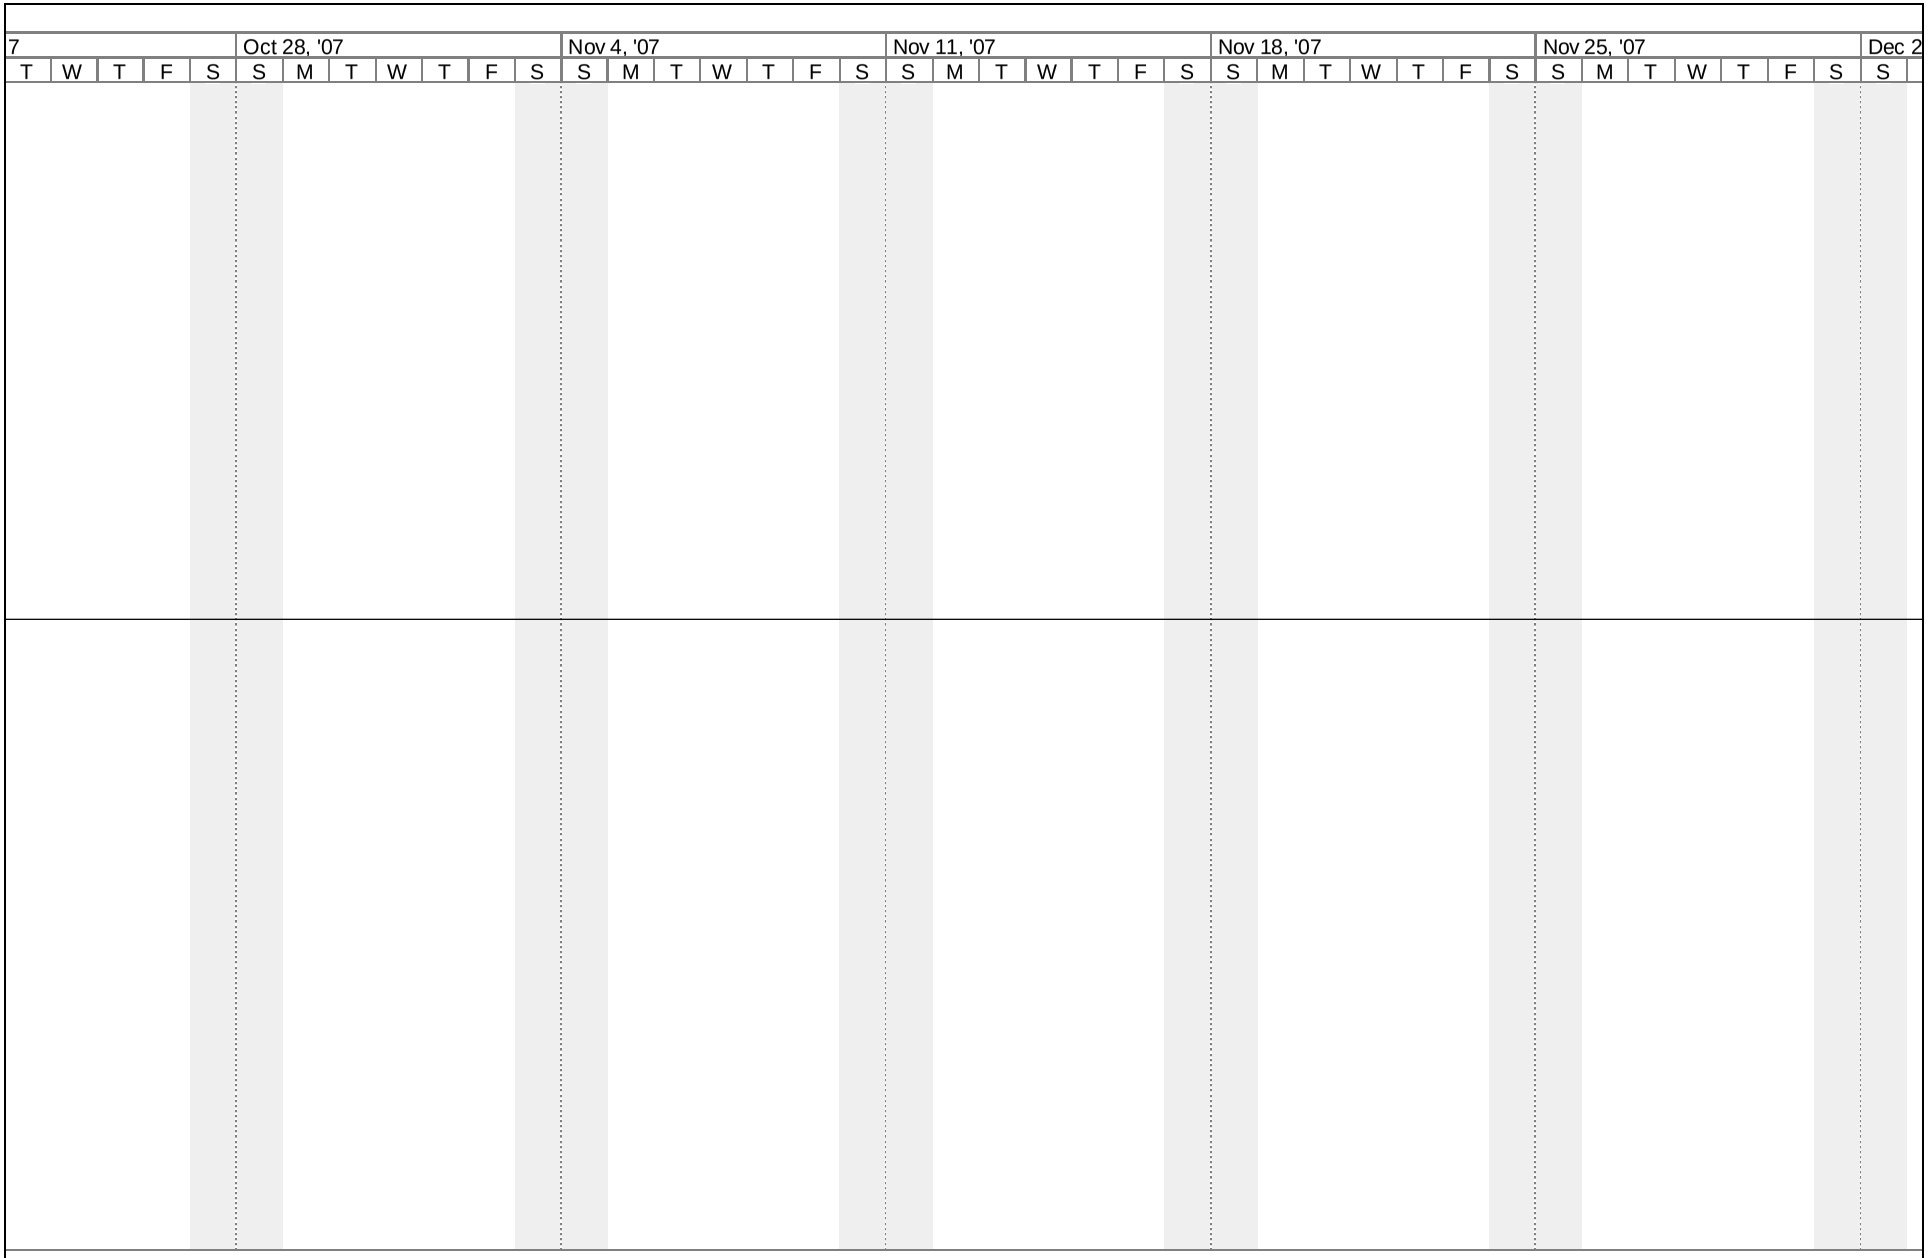

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

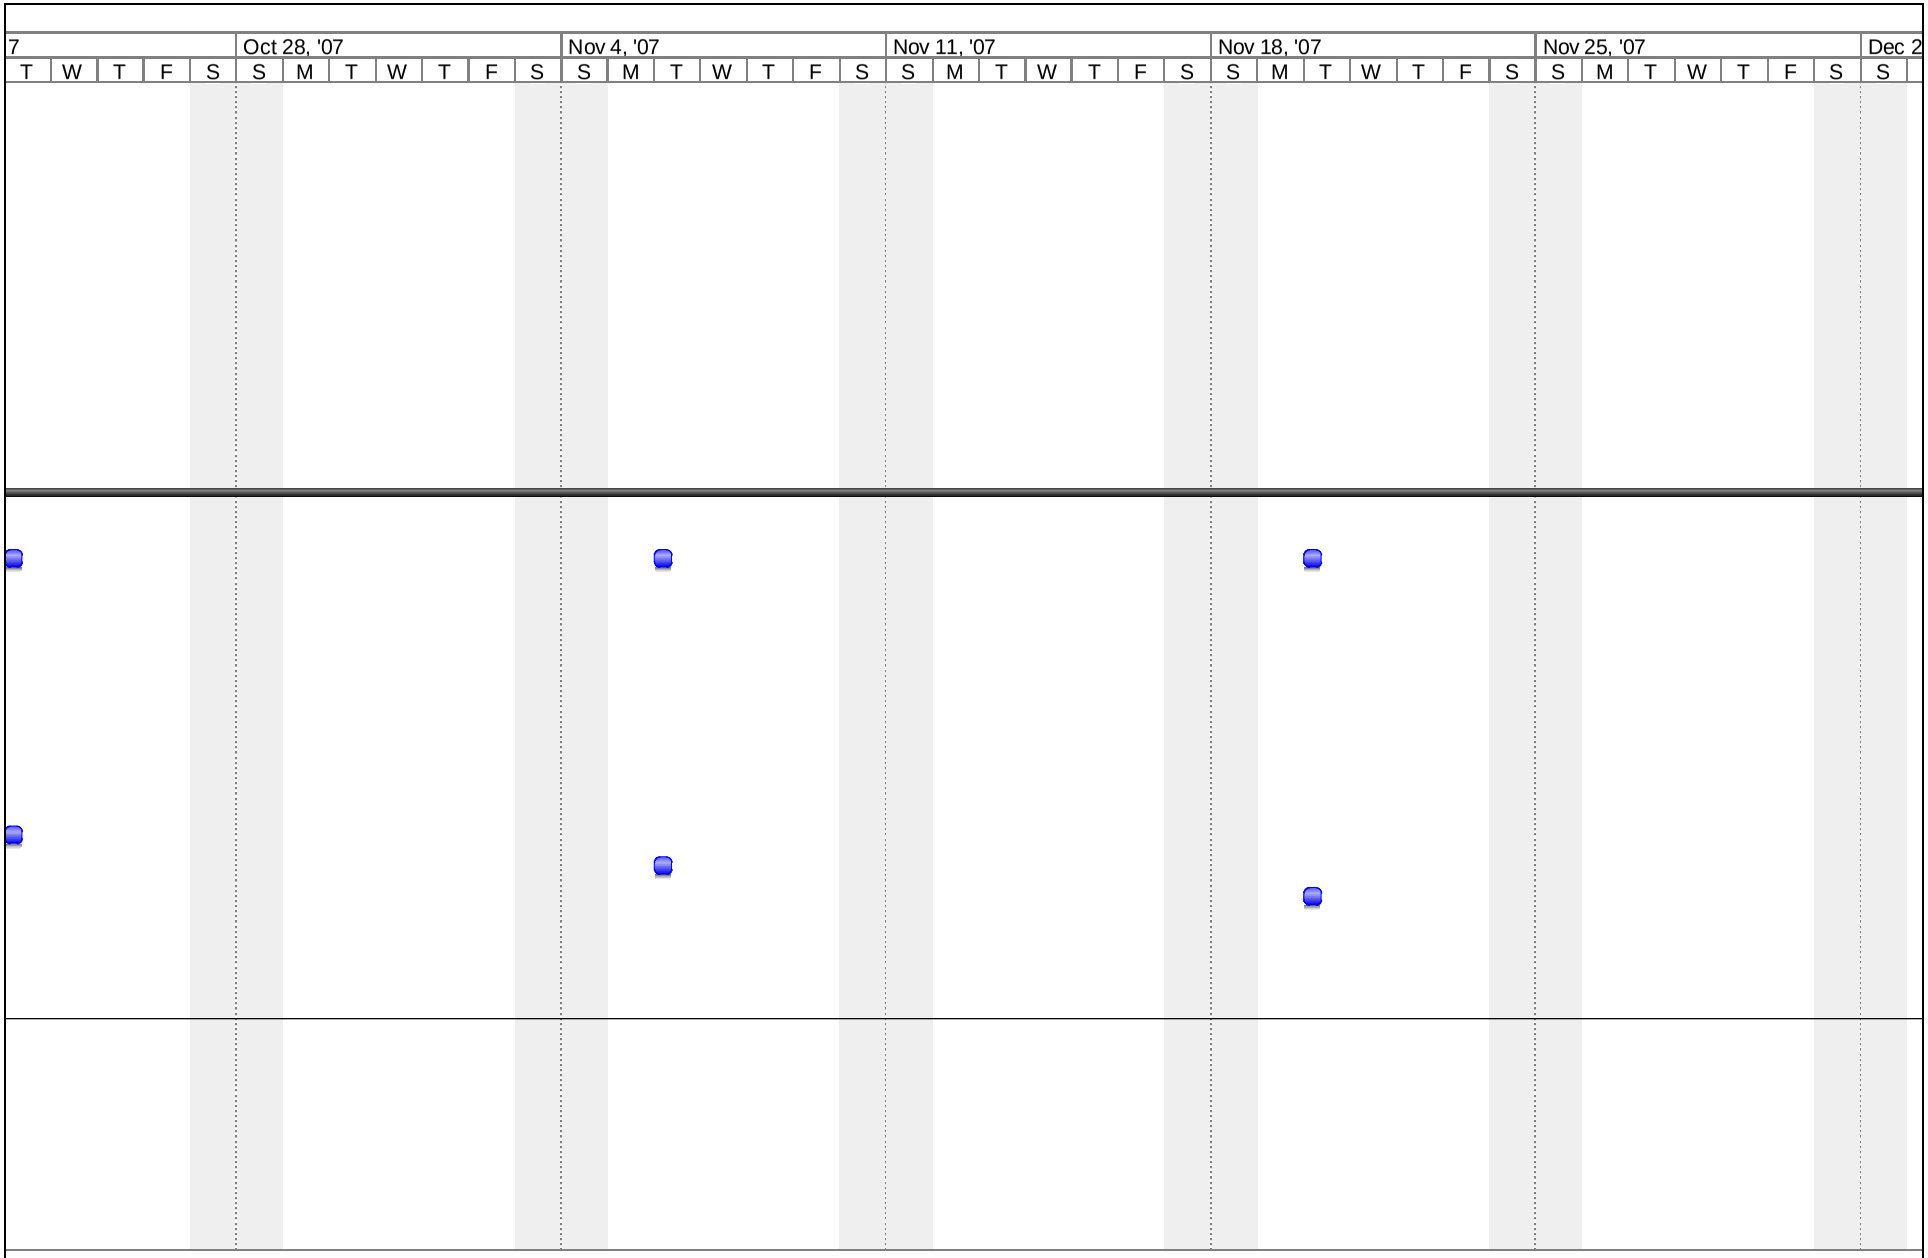

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

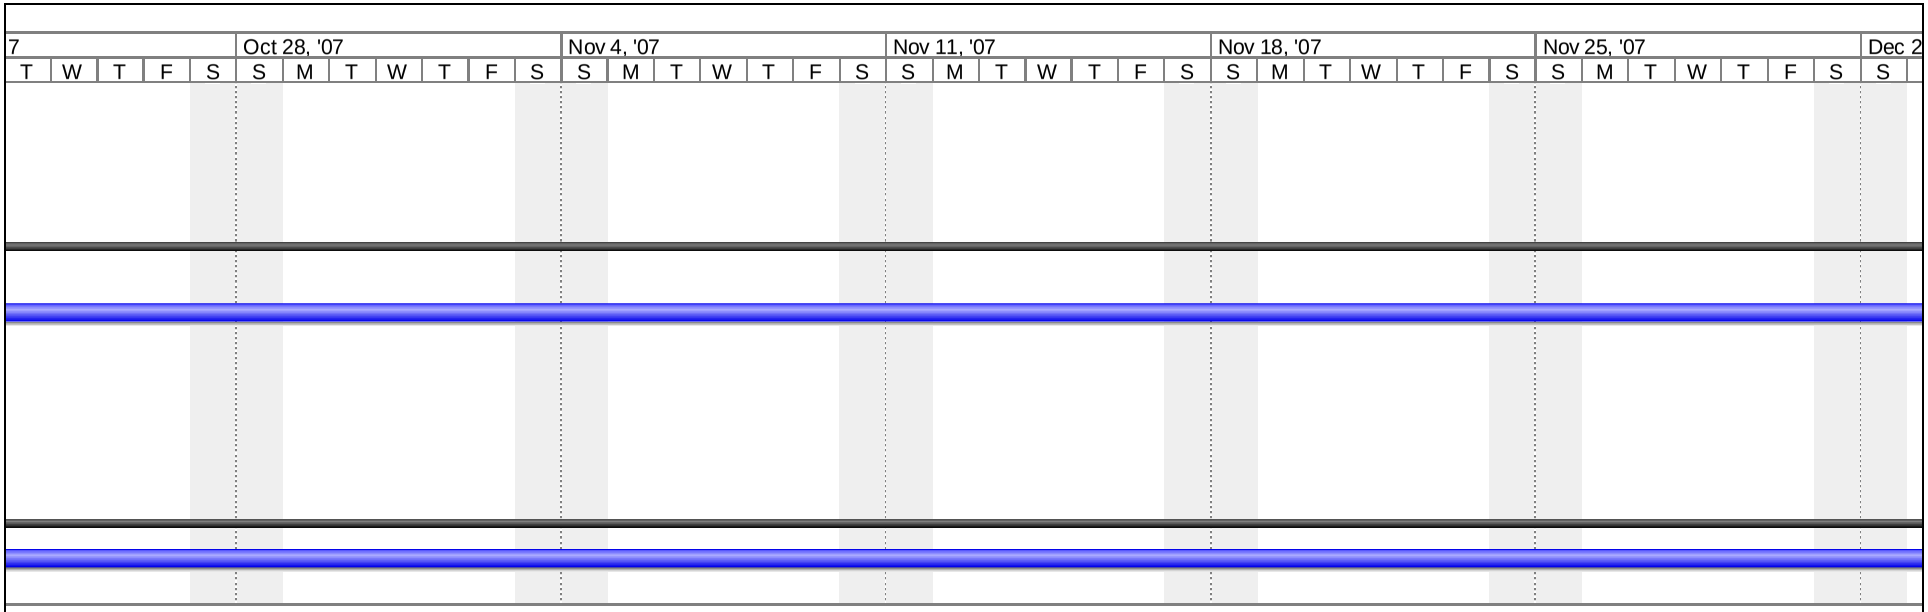

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

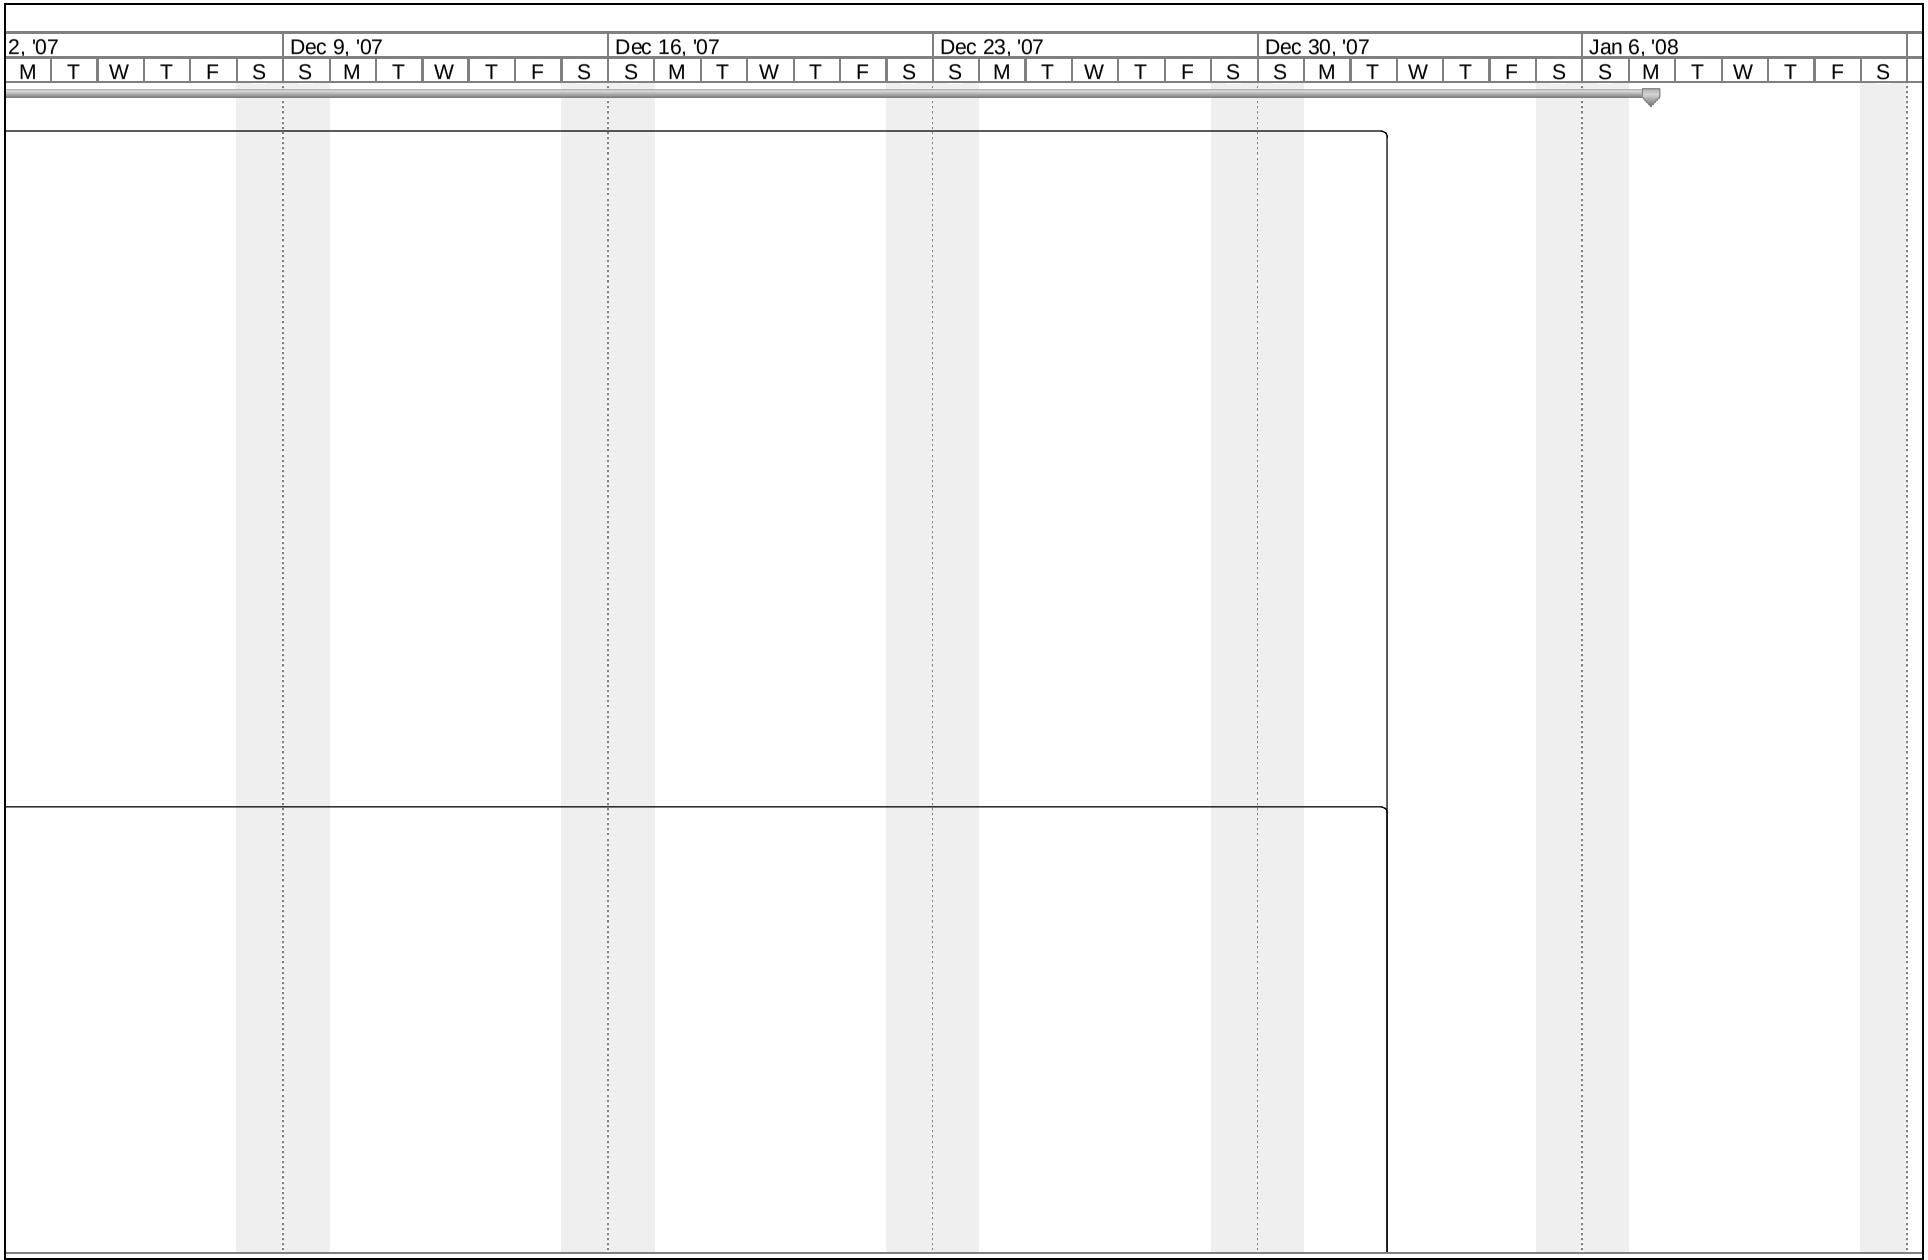

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

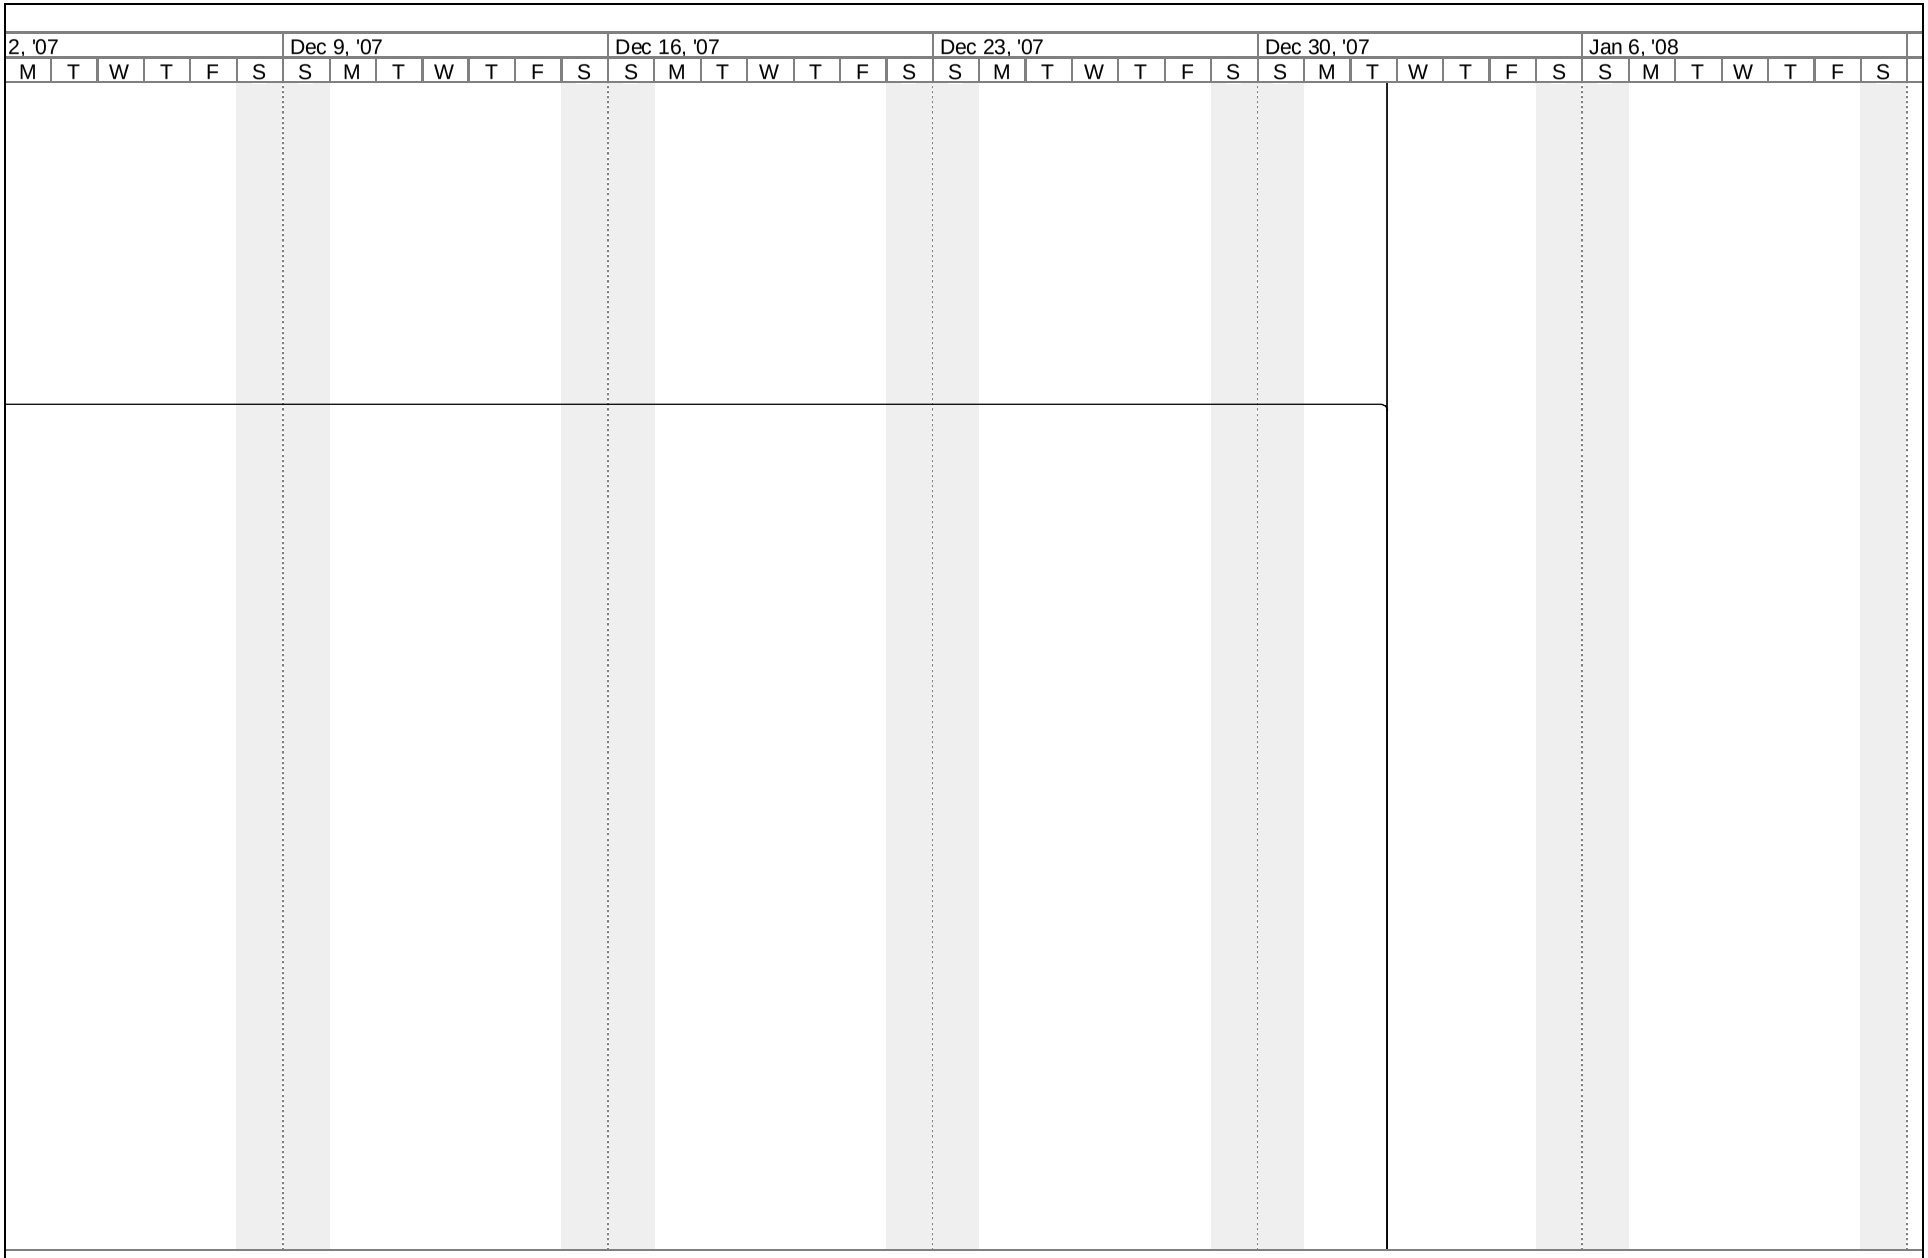

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

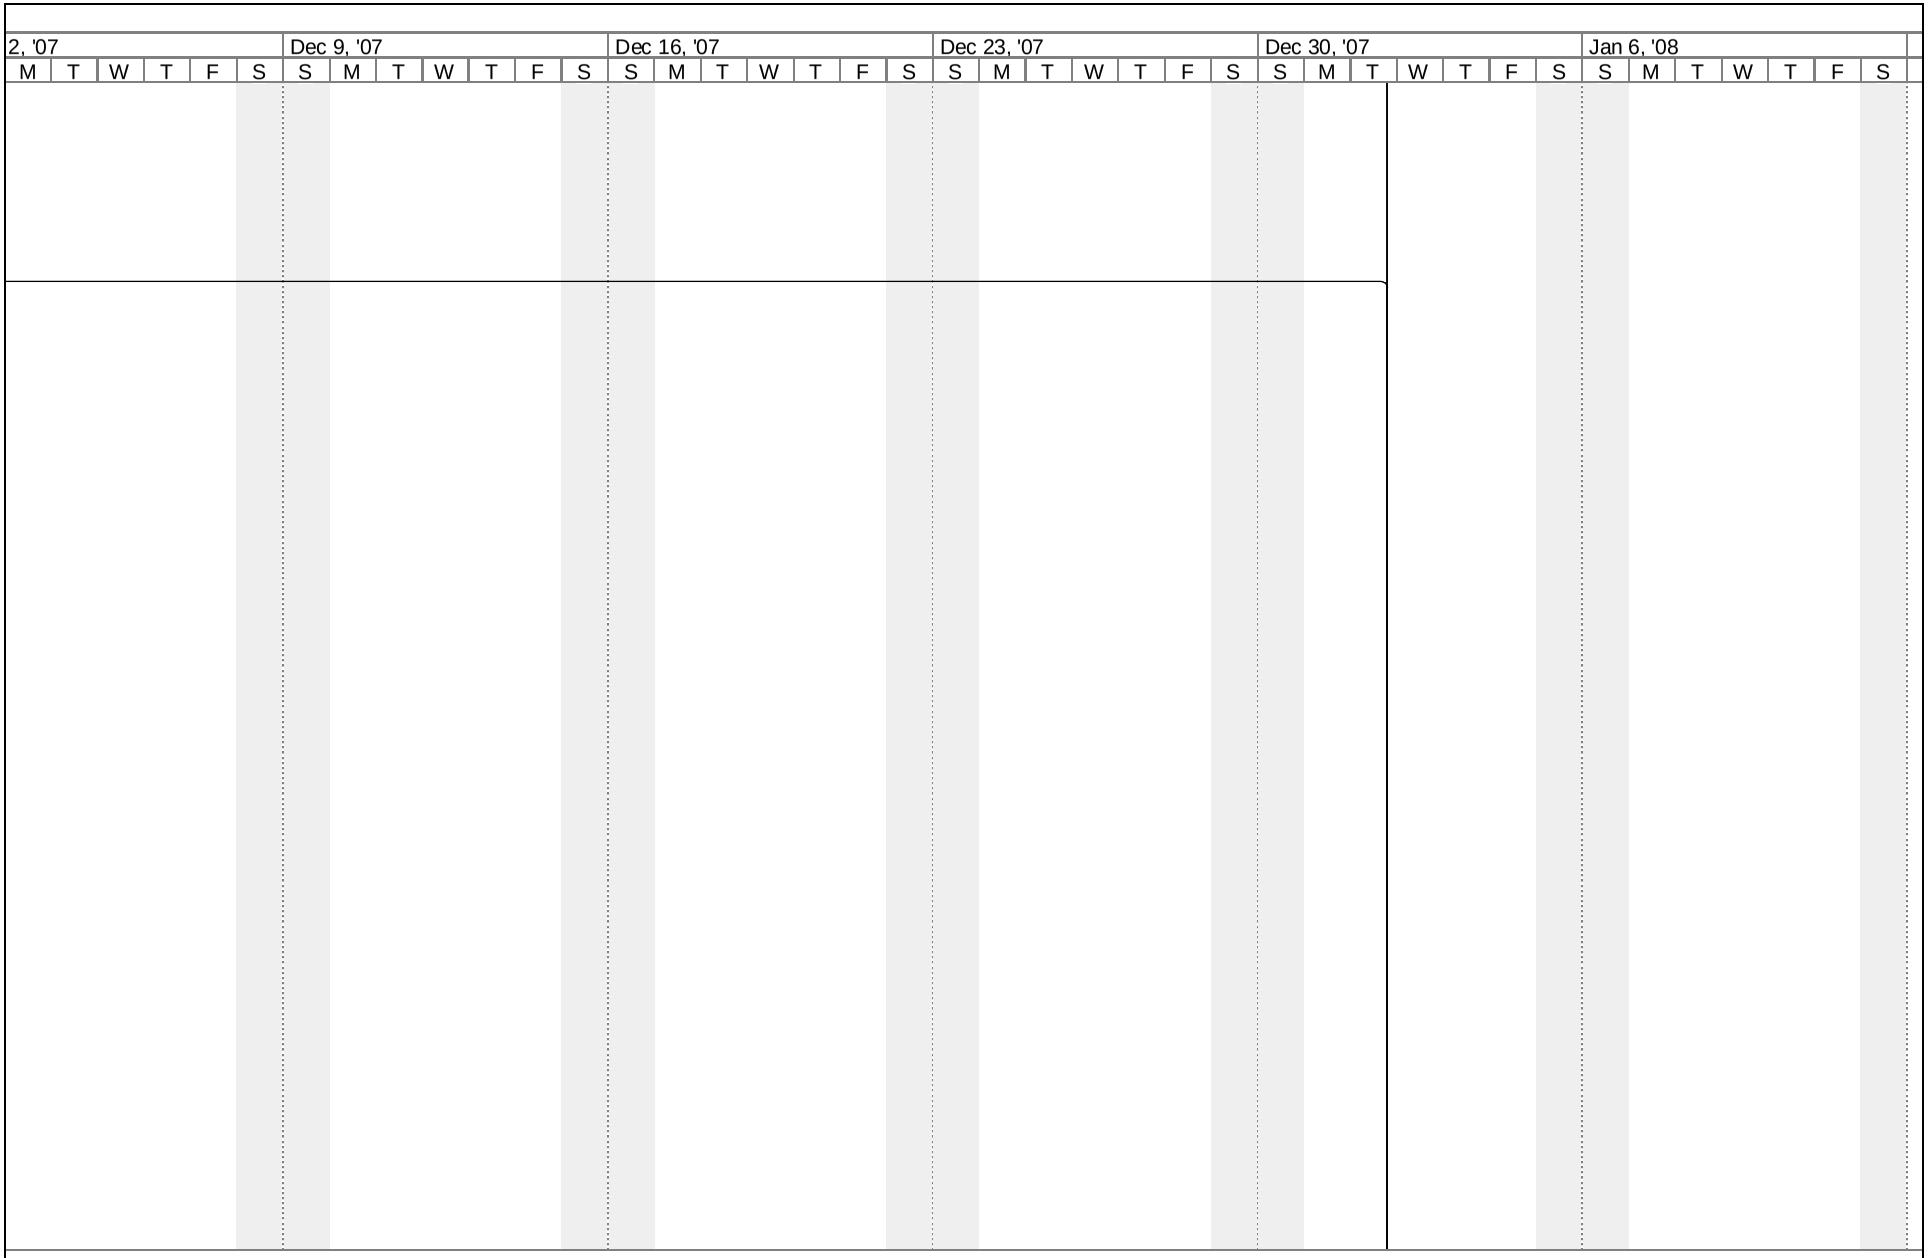

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

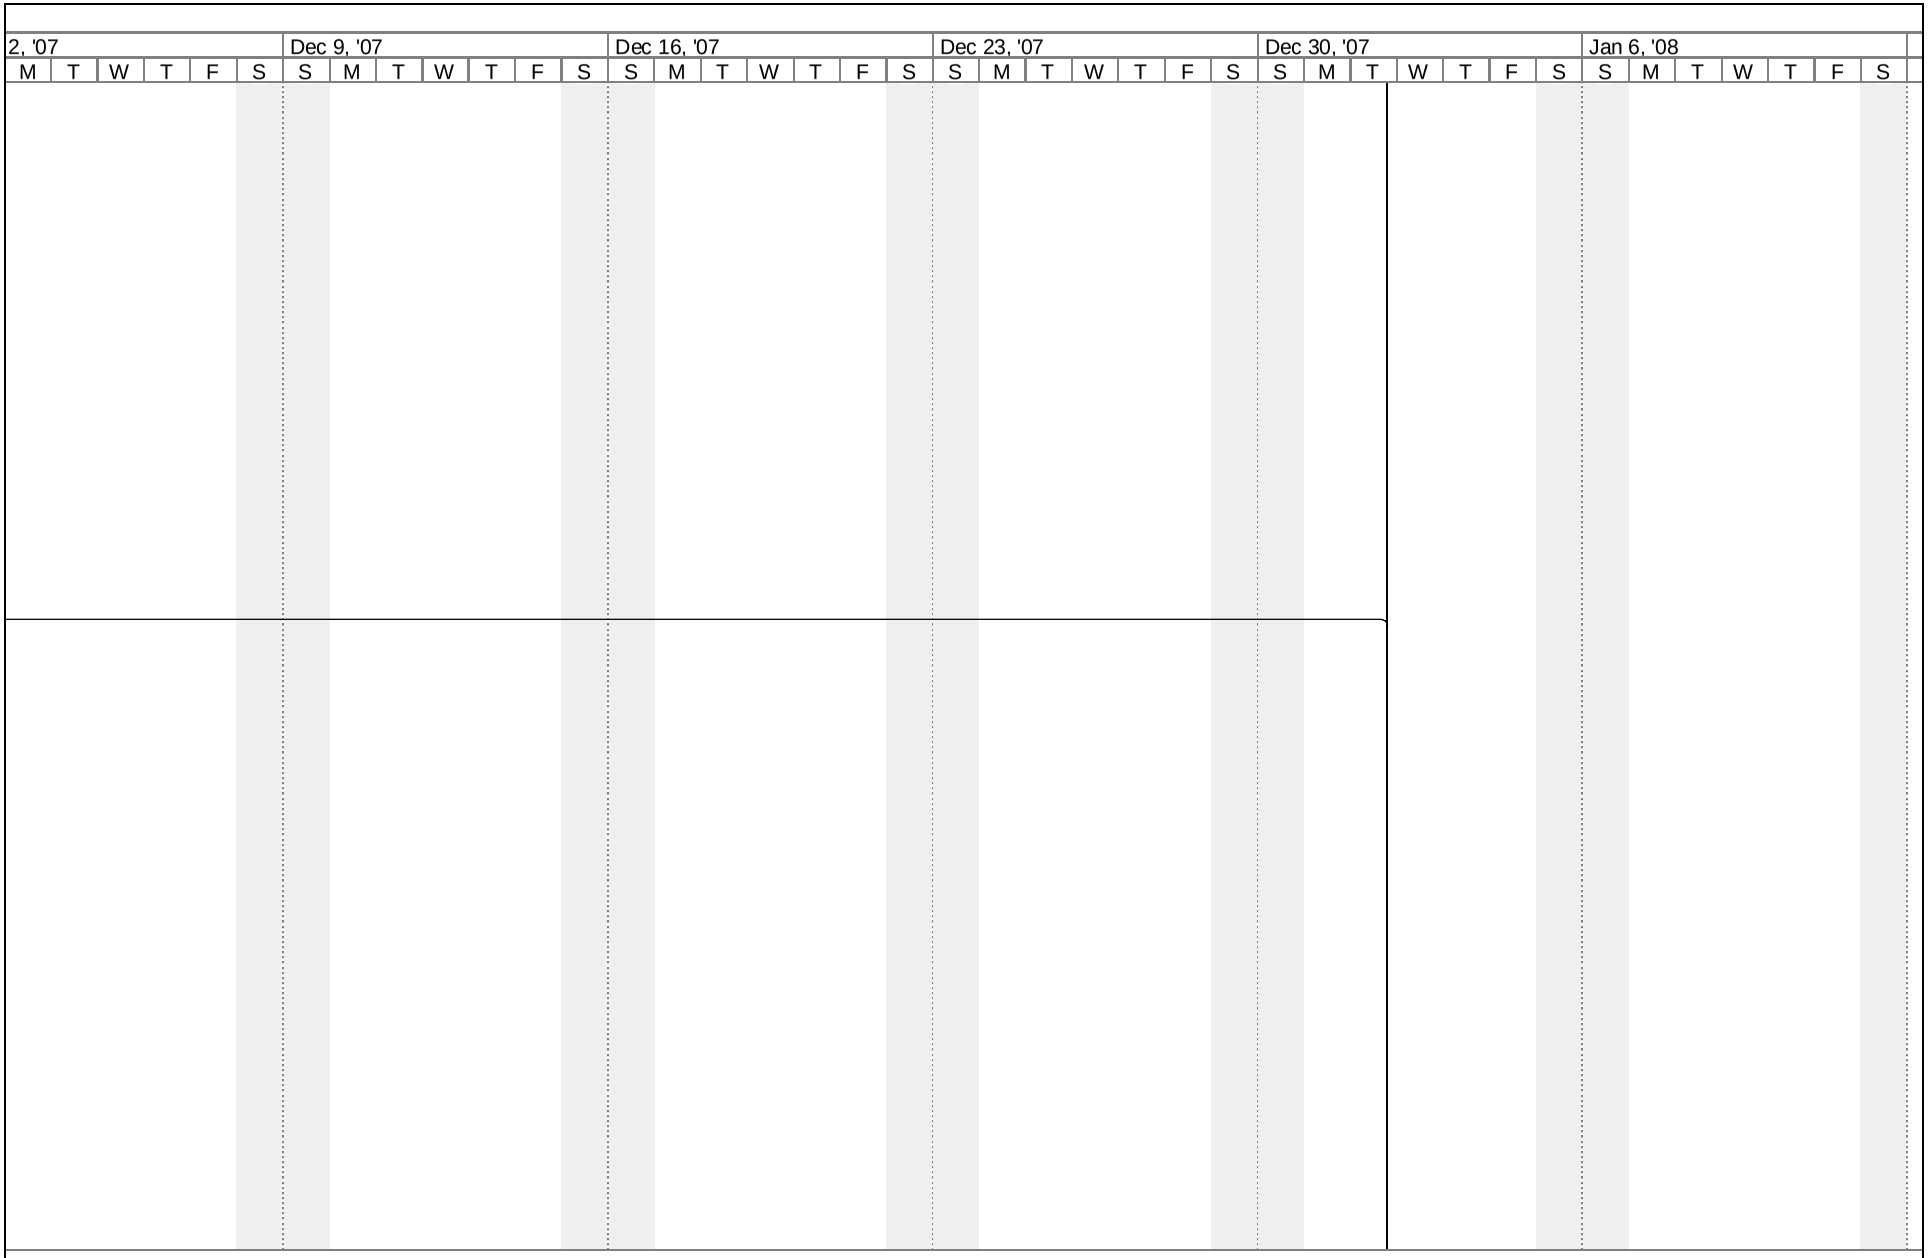

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

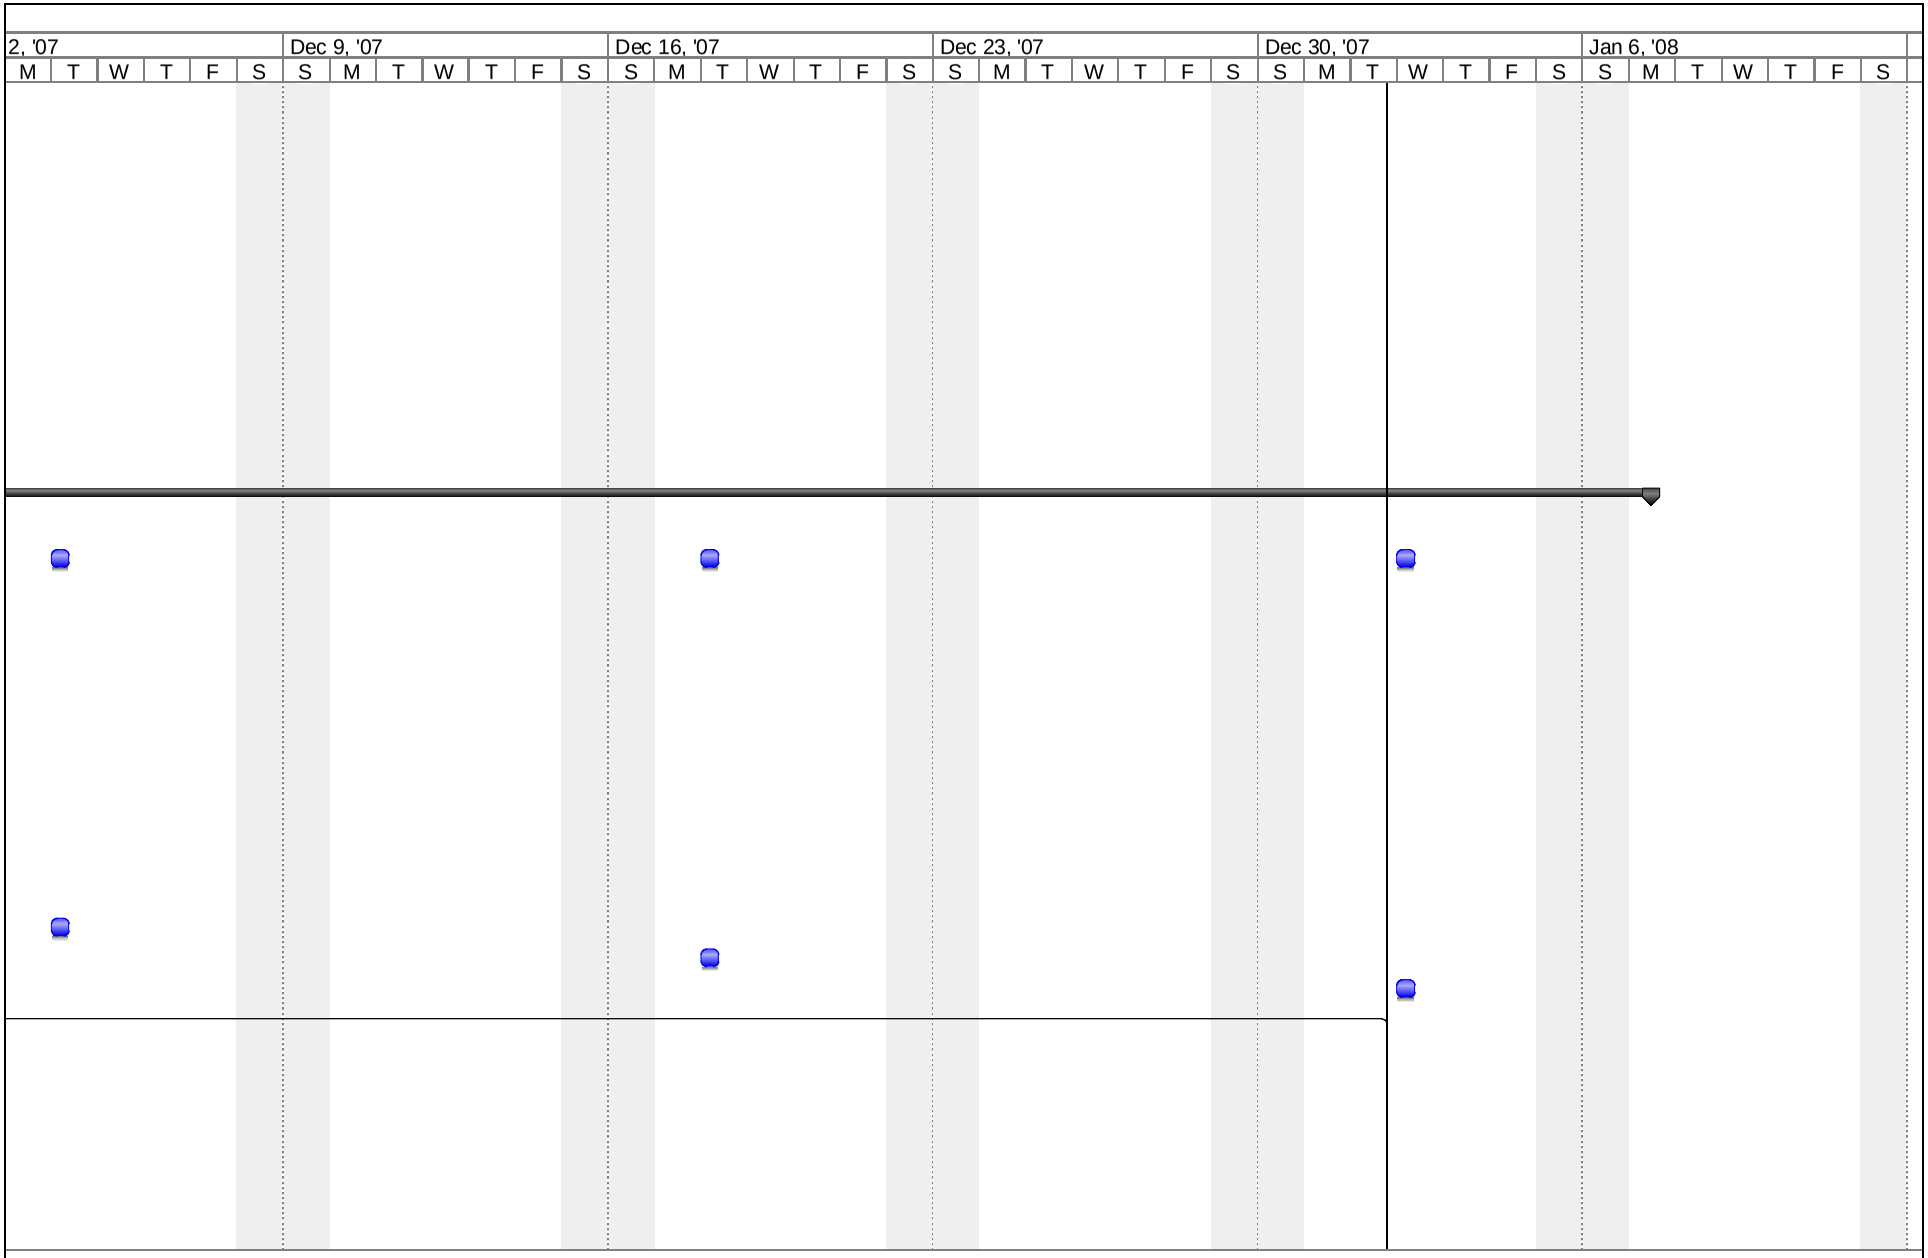

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

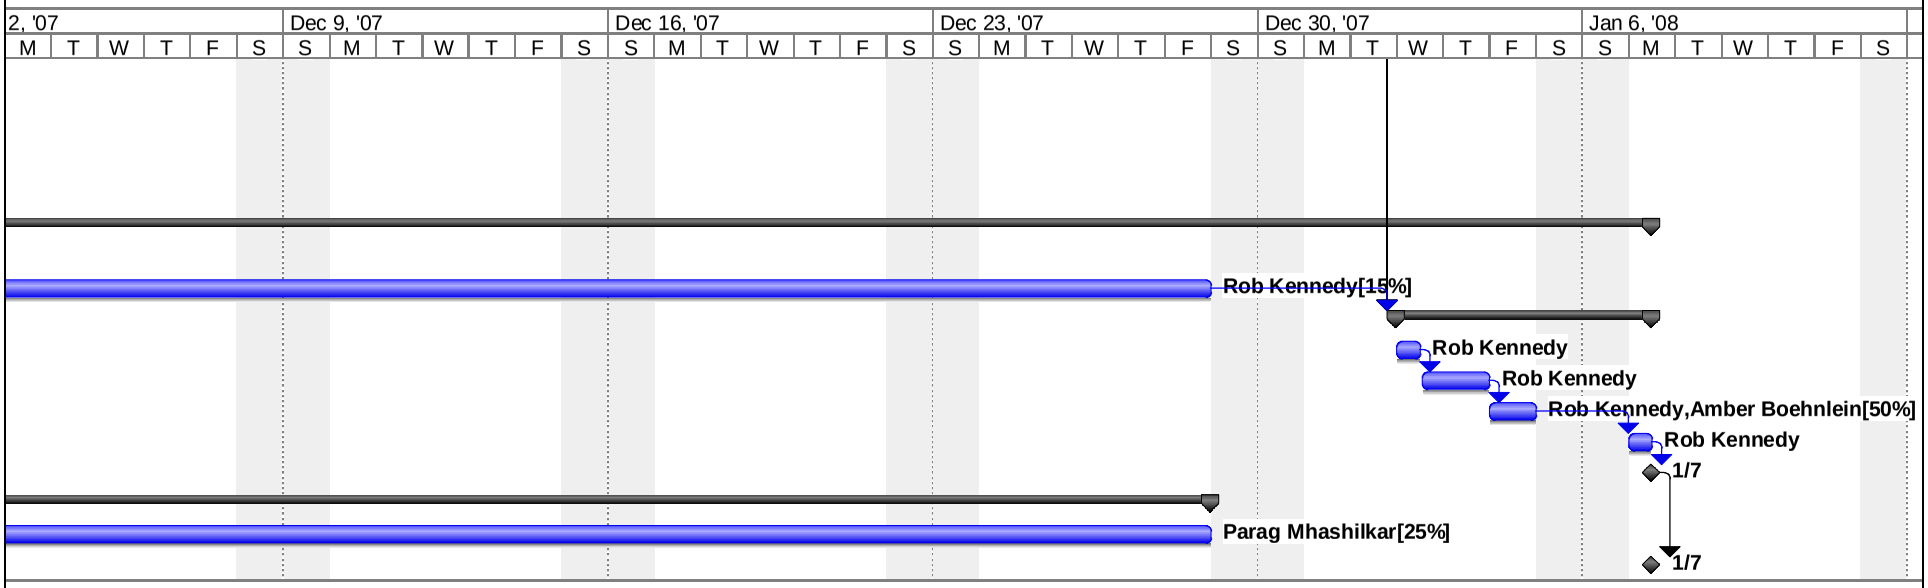

Project: D0 Grid Production Computing
Date: Wed 7/18/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
